PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
143875 PF-225			713.0d	411.0d		06-Mar-07	06-Mar-07 A		18-Aug-09
143875.01000 Program Management & Oversight (CBP 1745-7000-1)			510.0d	252.0d		02-Apr-07	02-Apr-07 A		31-Dec-08
143875.01000.075 Program Management & Oversight			510.0d	252.0d		02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1030	Program Management & Oversight-SWL		100.0d	365.0d	15%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1045	Program Management & Oversight-SWG		620.0d	365.0d	12%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1000	Program Management & Oversight-SWF		650.0d	365.0d	38%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1010	Program Management & Oversight-SPK		620.0d	365.0d	0%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1020	Program Management & Oversight-SWD		620.0d	365.0d	49%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1001	PM/EVMS/GIS Support - SWF		650.0d	365.0d	11%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1040	Program Management & Oversight-SPL		620.0d	365.0d	21%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1048	Program Management & Oversight-SPA		620.0d	365.0d	27%	02-Apr-07	02-Apr-07 A		31-Dec-08
PMO1050	TI MATOC SSEB - SPL		45.0d	100.0d	44%	01-Jun-07	01-Jun-07 A		10-Apr-08
PMO1060	TI MATOC SSEB - DCAA		74.0d	0.0d	100%	11-Jun-07	11-Jun-07 A	30-Nov-07	30-Nov-07 A
PMO1002	GIS Support - GIS		519.0d	365.0d	31%	29-Jun-07	29-Jun-07		31-Dec-08
PMO1041	Program Management & Oversight-SPL-Con Ops		562.0d	365.0d	12%	01-Jul-07	01-Jul-07 A		31-Dec-08
PMO1003	Public Affairs Support - SWF		519.0d	365.0d	27%	01-Aug-07	01-Aug-07 A		31-Dec-08
PMO1025	Program Management & Oversight - SPD		488.0d	365.0d	36%	29-Aug-07	29-Aug-07 A		31-Dec-08
PMO1005	Program Management & Oversight-HQ		488.0d	365.0d	13%	01-Sep-07	01-Sep-07 A		31-Dec-08
PMO1049	Program Management & Oversight-PFI Support		426.0d	365.0d	7%	01-Nov-07	01-Nov-07 A		31-Dec-08
PMO1004	EKO Support		426.0d	365.0d	7%	01-Nov-07	01-Nov-07 A		31-Dec-08
143875.01000.500 Project Definition			20.0d	14.0d		15-May-07	15-May-07 A		16-Apr-08
DEF0100	Final Phase 2 Laydown Plan	DEF4000	5.0d	5.0d	0%		10-Apr-08		16-Apr-08
143875.01000.500.100 OBP Outreach			22.0d	89.0d		15-May-07	15-May-07 A		09-Apr-08
DEF1000	OBP Outreach		22.0d	0.0d	100%	15-May-07	15-May-07 A	14-Jun-07	14-Jun-07 A
DEF1010	OBP Tactical/Operational Evaluation	DEF1000	10.0d	8.0d	0%	14-Jun-07	14-Jun-07 A		11-Jan-08
DEF1020	Technical Evaluation	DEF1000	10.0d	8.0d	0%	14-Jun-07	14-Jun-07 A		11-Jan-08
DEF3000	Project Formulation	DEF1010, DEF1020, DEF5000, DEF5010, DEF5020, DE...	5.0d	5.0d	0%		31-Jan-08		06-Feb-08
DEF4000	IBWC Coordination	DEF3000	44.0d	44.0d	0%		07-Feb-08		09-Apr-08
143875.01000.500.100.010 Landowner Engagement			20.0d	20.0d			02-Jan-08		30-Jan-08
DEF5000	Discuss Preferred Fence Alignment	DEF1000	10.0d	10.0d	0%		02-Jan-08		15-Jan-08
DEF5010	Discuss Preferred Fence Type	DEF1000	10.0d	10.0d	0%		02-Jan-08		15-Jan-08
DEF5020	Discuss Preferred Estate for Acquisition	DEF1000	10.0d	10.0d	0%		02-Jan-08		15-Jan-08
DEF5030	Request ROE for Survey & Exploration	DEF1000	10.0d	10.0d	0%		02-Jan-08		15-Jan-08
DEF5040	S1 Policy Decision on RE Approach	DEF5000, DEF5010, DEF5020, DEF5030	10.0d	10.0d	0%		16-Jan-08		30-Jan-08
143875.40000 Preliminary Design Phase (CBP 1745-7000-4)			694.0d	174.0d		02-Apr-07	02-Apr-07 A		08-Sep-08
143875.40000.001 Design Phase Project Management			429.0d	174.0d		2-Apr-07	02-Apr-07 A		08-Sep-08
DES5480	Program Management and Oversight SPL		100.0d	251.0d	57%	02-Apr-07	02-Apr-07 A		08-Sep-08
DES5481	TI MATOC Solicitation & SSEBs - SWT		136.0d	251.0d	82%	02-Apr-07	02-Apr-07 A		08-Sep-08
DES5470	Program Management and Oversight-SWF		100.0d	251.0d	7%	02-Apr-07	02-Apr-07 A		08-Sep-08
DES5475	Program Management and Oversight-SWG		100.0d	251.0d	7%	02-Apr-07	02-Apr-07 A		08-Sep-08
DES5478	Program Management and Oversight-SPA		100.0d	251.0d	14%	02-Apr-07	02-Apr-07 A		08-Sep-08
DES5483	TI MATOC's Guaranteed Minimums		30.0d	30.0d	100%	20-Jun-07	20-Jun-07 A		31-Jan-08
DES5482	Site Visits - SPA		120.0d	251.0d	64%	01-Jul-07	01-Jul-07 A		08-Sep-08
DES5484	Std Designs & Levee Fencing - SWL		59.0d	251.0d	67%	01-Oct-07	01-Oct-07 A		08-Sep-08
DES5485	Model RFP Development-ERDC		426.0d	251.0d	10%	01-Oct-07	01-Oct-07 A		08-Sep-08
143875.40000.075 Design Phase 1			194.0d	21.0d		18-May-07	18-May-07 A		22-Feb-08
143875.40000.075.01 Design Phase 1 (30.75 miles)			194.0d	21.0d		18-May-07	18-May-07 A		22-Feb-08
143875.40000.075.01.01 TCA - Design			175.0d	36.0d		12-Jun-07	12-Jun-07 A		22-Feb-08
143875.40000.075.01.01.001 D-2 (2005-1/2008-1) RFP #1 (5.20 Miles) SEA Ajo Station			72.0d	0.0d		12-Jun-07	12-Jun-07 A	21-Sep-07	21-Sep-07 A
DES6535	A-E Services	DES6540	21.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	21-Sep-07	21-Sep-07 A
DES6540	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES6550	Prepare Draft RFP	DES6540	49.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	30-Jul-07	30-Jul-07 A
DES6555	Government Site Visit	DES6540	1.0d	0.0d	100%	11-Jul-07	11-Jul-07 A	11-Jul-07	11-Jul-07 A
DES6560	RFP Review-95%	DES6560	3.0d	0.0d	100%	31-Jul-07	31-Jul-07 A	02-Aug-07	02-Aug-07 A
DES6570	Comment Annotation	DES6570	4.0d	0.0d	100%	03-Aug-07	03-Aug-07 A	06-Aug-07	06-Aug-07 A
DES6575	Government Review Conference-95%	DES6575	1.0d	0.0d	100%	07-Aug-07	07-Aug-07 A	07-Aug-07	07-Aug-07 A
DES6580	Sector Approval -	DES6580	0.0d	0.0d	100%			07-Aug-07	07-Aug-07 A
DES6510	Pre-Bid Conference (Site Visit)	DES6580	1.0d	0.0d	100%	08-Aug-07	08-Aug-07 A	08-Aug-07	08-Aug-07 A
DES6590	RTA RFP	DES6530	5.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	13-Aug-07	13-Aug-07 A
DES6500	100% Submission	DES6590	0.0d	0.0d	100%			13-Aug-07	13-Aug-07 A
DES6600	RFP Evaluation	DES6600	4.0d	0.0d	100%	13-Aug-07	13-Aug-07 A	16-Aug-07	16-Aug-07 A
DES6610	Back Check Review	DES6600	2.0d	0.0d	100%	14-Aug-07	14-Aug-07 A	16-Aug-07	16-Aug-07 A

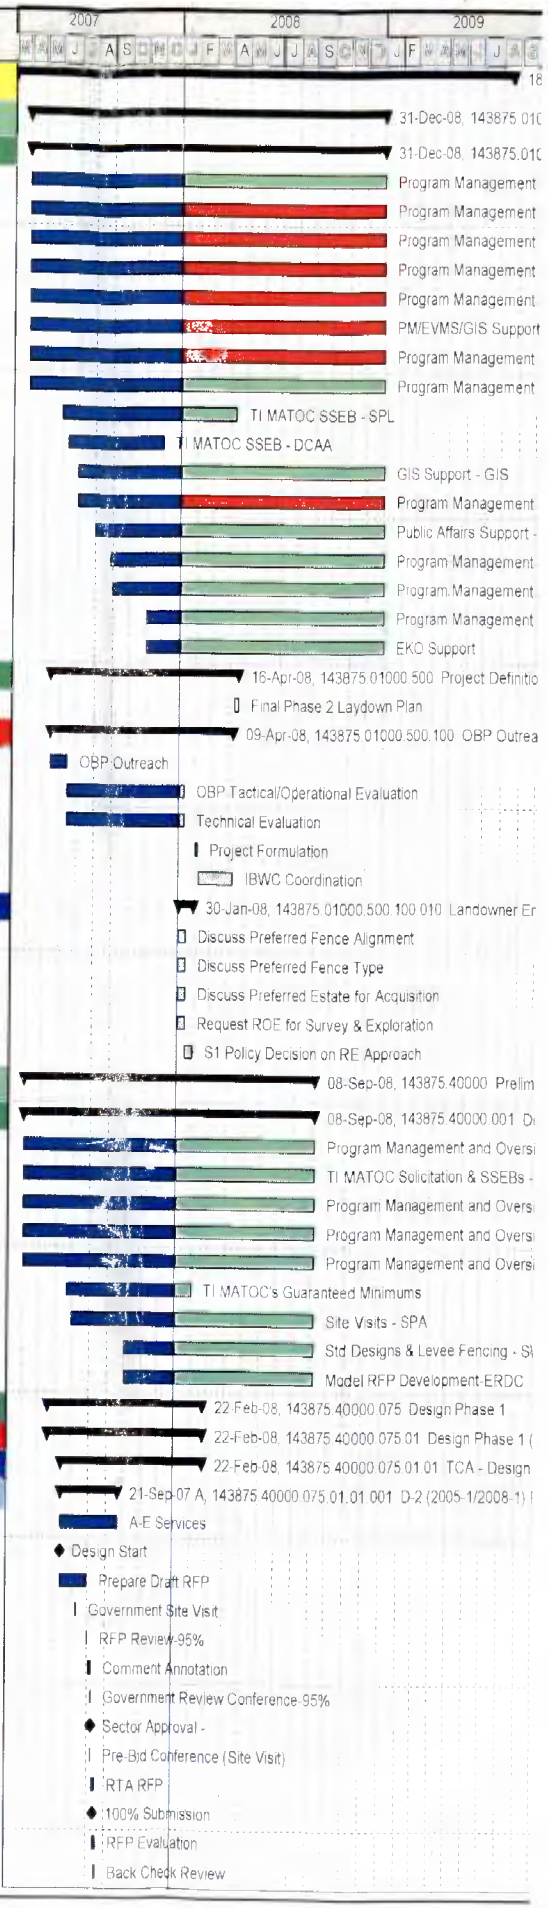

PF-225

PF225

04-Jan-08 11 (

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES6550	RTA	DES6620, REO41200, REO41080	0.0d	0.0d	100%			16-Aug-07	16-Aug-07 A
DES6620	RTA RFP (Corrected Finals)	DES6610	1.0d	0.0d	100%	16-Aug-07	16-Aug-07 A	16-Aug-07	16-Aug-07 A
DES6635	Issue RFP	DES6630, REO41200, REO41080	0.0d	0.0d	100%			17-Aug-07	17-Aug-07 A
DES6640	Proposal Preparation	DES6635	30.0d	0.0d	100%	18-Aug-07	18-Aug-07 A	14-Sep-07	14-Sep-07 A
DES6642	Final Site Visit -	DES6640	5.0d	0.0d	100%	01-Sep-07	01-Sep-07 A	05-Sep-07	05-Sep-07 A
DES6645	Proposal Evaluation	DES6640	5.0d	0.0d	100%	17-Sep-07	17-Sep-07 A	21-Sep-07	21-Sep-07 A
DES6650	Award Task Order	DES6645, ENV16750	0.0d	0.0d	100%			21-Sep-07	21-Sep-07 A
143875.40000.075.01.01.002	**D-5A (2010-1) RFP#1B (2.00 Miles) SEA Nogales Station**		77.0d	0.0d		12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES7175	A-E Services	DES7060	28.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES7060	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES7080	Prepare Draft RFP	DES7060	56.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	18-Jun-07	18-Jun-07 A
DES7090	RFP Review-95%	DES7080	3.0d	0.0d	100%	19-Jun-07	19-Jun-07 A	21-Jun-07	21-Jun-07 A
DES7095	Comment Annotation	DES7090	4.0d	0.0d	100%	22-Jun-07	22-Jun-07 A	25-Jun-07	25-Jun-07 A
DES7100	Government Review Conference-95%	DES7095	1.0d	0.0d	100%	26-Jun-07	26-Jun-07 A	26-Jun-07	26-Jun-07 A
DES7050	Pre-Bid Conference (Site Visit)	DES7100	1.0d	0.0d	100%	27-Jun-07	27-Jun-07 A	27-Jun-07	27-Jun-07 A
DES7105	Sector Approval	DES7100	0.0d	0.0d	100%			27-Jun-07	27-Jun-07 A
DES7110	RTA RFP	DES7050	5.0d	0.0d	100%	28-Jun-07	28-Jun-07 A	02-Jul-07	02-Jul-07 A
DES7120	100% Submission	DES7110	0.0d	0.0d	100%			03-Jul-07	03-Jul-07 A
DES7130	Back Check Review	DES7120	2.0d	0.0d	100%	04-Jul-07	04-Jul-07 A	05-Jul-07	05-Jul-07 A
DES7150	RFP Evaluation	DES7120	4.0d	0.0d	100%	04-Jul-07	04-Jul-07 A	23-Aug-07	23-Aug-07 A
DES7140	RTA RFP (Corrected Finals)	DES7130	1.0d	0.0d	100%	06-Jul-07	06-Jul-07 A	06-Jul-07	06-Jul-07 A
DES7085	Government Site Visit	DES7060	1.0d	0.0d	100%	13-Jul-07	13-Jul-07 A	13-Jul-07	13-Jul-07 A
DES7070	RTA	DES7140, REO17000	0.0d	0.0d	100%			23-Aug-07	23-Aug-07 A
DES7155	Issue RFP	DES7150, REO17000	0.0d	0.0d	100%			24-Aug-07	24-Aug-07 A
DES7160	Proposal Preparation	DES7155	30.0d	0.0d	100%	25-Aug-07	25-Aug-07 A	21-Sep-07	21-Sep-07 A
DES7162	Final Site Visit	DES7160	5.0d	0.0d	100%	01-Sep-07	01-Sep-07 A	05-Sep-07	05-Sep-07 A
DES7165	Proposal Evaluation	DES7160	5.0d	0.0d	100%	24-Sep-07	24-Sep-07 A	28-Sep-07	28-Sep-07 A
DES7170	Award Task Order	DES7165, ENV16880	0.0d	0.0d	100%			28-Sep-07	28-Sep-07 A
143875.40000.075.01.01.003	**E-2B (2011-1) RFP#2B (6.90 Miles) SEA Naco Station**		85.0d	0.0d		01-Aug-07	01-Aug-07 A	20-Aug-07	20-Aug-07 A
DES7045	A-E Services		125.0d	0.0d	100%	01-Aug-07	01-Aug-07 A	20-Aug-07	20-Aug-07 A
DES7040	Award Task Order	ENV13990	0.0d	0.0d	100%			20-Aug-07	20-Aug-07 A
143875.40000.075.01.01.004	**E-3 (2011-2) RFP# 3 (5.10 Miles) SEA Naco Station**		73.0d	0.0d		12-Jun-07	12-Jun-07 A	24-Sep-07	24-Sep-07 A
DES6695	Government Site Visit	DES6690	1.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	12-Jun-07	12-Jun-07 A
DES6670	Design Start	DES6695	0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES6690	Prepare Draft RFP		49.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	30-Jul-07	30-Jul-07 A
DES6785	A-E Services	DES6670	24.0d	0.0d	100%	17-Jun-07	17-Jun-07 A	24-Sep-07	24-Sep-07 A
DES6700	RFP Review-95%	DES6690	3.0d	0.0d	100%	31-Jul-07	31-Jul-07 A	02-Aug-07	02-Aug-07 A
DES6705	Comment Annotation	DES6700	5.0d	0.0d	100%	03-Aug-07	03-Aug-07 A	07-Aug-07	07-Aug-07 A
DES6710	Government Review Conference-95%	DES6705	1.0d	0.0d	100%	08-Aug-07	08-Aug-07 A	08-Aug-07	08-Aug-07 A
DES6715	Sector Approval	DES6710	0.0d	0.0d	100%			08-Aug-07	08-Aug-07 A
DES6660	Pre-Bid Conference (Site Visit)	DES6710	0.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	09-Aug-07	09-Aug-07 A
DES6720	RTA RFP	DES6660	5.0d	0.0d	100%	10-Aug-07	10-Aug-07 A	14-Aug-07	14-Aug-07 A
DES6730	100% Submission	DES6720	0.0d	0.0d	100%			14-Aug-07	14-Aug-07 A
DES6740	Back Check Review	DES6730	2.0d	0.0d	100%	15-Aug-07	15-Aug-07 A	16-Aug-07	16-Aug-07 A
DES6760	RFP Evaluation	DES6730	6.0d	0.0d	100%	15-Aug-07	15-Aug-07 A	20-Aug-07	20-Aug-07 A
DES6750	RTA RFP (Corrected Finals)	DES6740	1.0d	0.0d	100%	17-Aug-07	17-Aug-07 A	17-Aug-07	17-Aug-07 A
DES6680	RTA	DES6750, REO30000	0.0d	0.0d	100%			17-Aug-07	17-Aug-07 A
DES6765	Issue RFP	DES6760, REO30000	0.0d	0.0d	100%			20-Aug-07	20-Aug-07 A
DES6770	Proposal Preparation	DES6765	30.0d	0.0d	100%	21-Aug-07	21-Aug-07 A	17-Sep-07	17-Sep-07 A
DES6772	Final Site Visit	DES6770	5.0d	0.0d	100%	01-Sep-07	01-Sep-07 A	05-Sep-07	05-Sep-07 A
DES6775	Proposal Evaluation	DES6770	5.0d	0.0d	100%	18-Sep-07	18-Sep-07 A	24-Sep-07	24-Sep-07 A
DES6780	Award Task Order	DES6775, ENV13990	0.0d	0.0d	100%			24-Sep-07	24-Sep-07 A
143875.40000.075.01.01.005	**F-1 (2012-1) RFP#4 (2.42 Miles) SEA Douglas Station - Cancelled**		175.0d	36.0d		12-Jun-07	12-Jun-07 A		22-Feb-08
DES13290	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES13300	Prepare Draft RFP	DES13290	39.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	20-Jul-07	20-Jul-07 A
DES13288	Government Site Visit	DES13290	1.0d	0.0d	100%	12-Jul-07	12-Jul-07 A	12-Jul-07	12-Jul-07 A
DES13305	RFP Review-95%	DES13300	3.0d	0.0d	100%	23-Jul-07	23-Jul-07 A	25-Jul-07	25-Jul-07 A
DES13310	Comment Annotation	DES13305	2.0d	0.0d	100%	26-Jul-07	26-Jul-07 A	27-Jul-07	27-Jul-07 A
DES13315	Government Review Conference-95%	DES13310	4.0d	0.0d	100%	28-Jul-07	28-Jul-07 A	31-Jul-07	31-Jul-07 A
DES13365	A-E Services	DES13290	48.0d	49.0d	0%	01-Oct-07	01-Oct-07 A		19-Feb-08
DES13285	Pre-Bid Conference (Site Visit)	DES13315	1.0d	1.0d	0%		02-Jan-08		02-Jan-08
DES13360	Award Task Order	DES13355, ENV13630	0.0d	0.0d	0%				02-Jan-08*
DES13318	Sector Approval	DES13315	0.0d	0.0d	0%				02-Jan-08

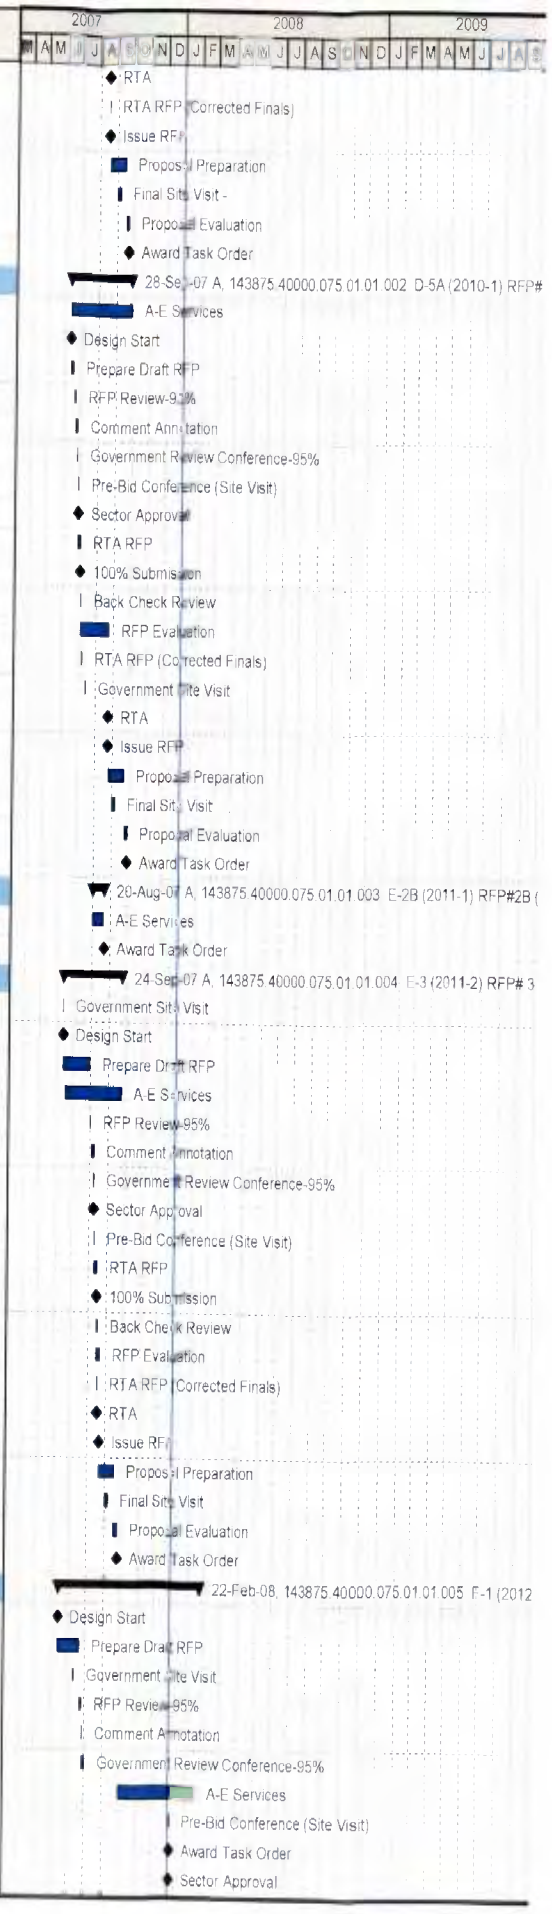

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13320	RTA RFP	DES13285	5.0d	5.0d	0%		03-Jan-08		07-Jan-08
DES13325	100% Submission	DES13320	0.0d	0.0d	0%				07-Jan-08
DES13330	Back Check Review	DES13325	2.0d	2.0d	0%		08-Jan-08		09-Jan-08
DES13340	RFP Evaluation	DES13325	7.0d	7.0d	0%		08-Jan-08		14-Jan-08
DES13335	RTA RFP (Corrected Finals)	DES13330	1.0d	1.0d	0%		10-Jan-08		10-Jan-08
DES13295	RTA	DES13335, REO40000	0.0d	0.0d	0%				10-Jan-08
DES13345	Issue RFP	DES13340, REO40000	0.0d	0.0d	0%				18-Jan-08
DES13350	Proposal Preparation	DES13345	30.0d	30.0d	0%		19-Jan-08		17-Feb-08
DES13358	Final Site Visit	DES13350	5.0d	5.0d	0%		24-Jan-08		28-Jan-08
DES13355	Proposal Evaluation	DES13350	5.0d	5.0d	0%		18-Feb-08		22-Feb-08
143875.40000.075.01.02 EPT - Design Phase 1			158.0d	19.0d		12-Jun-07	12-Jun-07 A		29-Jan-08
143875.40000.075.01.02.001 I-1A (2013-2) RFP#5 (2.50 Miles) SEA Deming Station			77.0d	0.0d		12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES5745	A-E Services	DES5630	27.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES5630	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES5650	Prepare Draft RFP	DES5630	49.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	30-Jul-07	30-Jul-07 A
DES5655	Government Site Visit	DES5650	1.0d	0.0d	100%	09-Jul-07	09-Jul-07 A	09-Jul-07	09-Jul-07 A
DES5660	RFP Review-95%	DES5650	3.0d	0.0d	100%	31-Jul-07	31-Jul-07 A	02-Aug-07	02-Aug-07 A
DES5665	Comment Annotation	DES5660	4.0d	0.0d	100%	03-Aug-07	03-Aug-07 A	06-Aug-07	06-Aug-07 A
DES5670	Government Review Conference-95%	DES5665	1.0d	0.0d	100%	07-Aug-07	07-Aug-07 A	07-Aug-07	07-Aug-07 A
DES5675	Sector Approval	DES5670	0.0d	0.0d	100%			07-Aug-07	07-Aug-07 A
DES5620	Pre-Bid Conference (Site Visit)	DES5670	1.0d	0.0d	100%	08-Aug-07	08-Aug-07 A	08-Aug-07	08-Aug-07 A
DES5680	RTA RFP	DES5620	4.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	12-Aug-07	12-Aug-07 A
DES5690	100% Submission	DES5680	0.0d	0.0d	100%			12-Aug-07	12-Aug-07 A
DES5700	Back Check Review	DES5690	2.0d	0.0d	100%	13-Aug-07	13-Aug-07 A	14-Aug-07	14-Aug-07 A
DES5720	RFP Evaluation	DES5690	5.0d	0.0d	100%	13-Aug-07	13-Aug-07 A	17-Aug-07	17-Aug-07 A
DES5710	RTA RFP (Corrected Finals)	DES5700	1.0d	0.0d	100%	15-Aug-07	15-Aug-07 A	15-Aug-07	15-Aug-07 A
DES5640	RTA	DES5710	0.0d	0.0d	100%			15-Aug-07	15-Aug-07 A
DES5725	Issue RFP	DES5720, REO19000	0.0d	0.0d	100%			23-Aug-07	23-Aug-07 A
DES5730	Proposal Preparation	DES5725	30.0d	0.0d	100%	24-Aug-07	24-Aug-07 A	28-Aug-07	28-Aug-07 A
DES5735	Proposal Evaluation	DES5730	5.0d	0.0d	100%	17-Sep-07	17-Sep-07 A	19-Sep-07	19-Sep-07 A
DES5732	Final Site Visit	DES5730	5.0d	0.0d	100%	17-Sep-07	17-Sep-07 A	21-Sep-07	21-Sep-07 A
DES5740	Award Task Order	DES5735, ENV17010	0.0d	0.0d	100%			28-Sep-07	28-Sep-07 A
143875.40000.075.01.02.002 J-I/J-3 (2014-1/2/3) RFP#6 (3.29 Miles) SEA Santa Theresa Station			98.0d	0.0d		12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES6135	A-E Services	DES6020	60.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	28-Sep-07	28-Sep-07 A
DES6020	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES6040	Prepare Draft RFP	DES6020	49.0d	0.0d	100%	12-Jun-07	12-Jun-07 A	30-Jul-07	30-Jul-07 A
DES6045	Government Site Visit	DES6115	1.0d	0.0d	100%	09-Jul-07	09-Jul-07 A	09-Jul-07	09-Jul-07 A
DES6120	Proposal Preparation	DES6040	30.0d	0.0d	100%	25-Jul-07	25-Jul-07 A	24-Aug-07	24-Aug-07 A
DES6050	RFP Review-95%	DES6050	3.0d	0.0d	100%	31-Jul-07	31-Jul-07 A	02-Aug-07	02-Aug-07 A
DES6055	Comment Annotation	DES6055	4.0d	0.0d	100%	03-Aug-07	03-Aug-07 A	06-Aug-07	06-Aug-07 A
DES6060	Government Review Conference-95%	DES6060	1.0d	0.0d	100%	07-Aug-07	07-Aug-07 A	07-Aug-07	07-Aug-07 A
DES6065	Sector Approval	DES6060	0.0d	0.0d	100%			07-Aug-07	07-Aug-07 A
DES6010	Pre-Bid Conference (Site Visit)	DES6010	1.0d	0.0d	100%	08-Aug-07	08-Aug-07 A	08-Aug-07	08-Aug-07 A
DES6070	RTA RFP	DES6120	6.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	14-Aug-07	14-Aug-07 A
DES6122	Final Site Visit	DES6070	5.0d	0.0d	100%	11-Aug-07	11-Aug-07 A	15-Aug-07	15-Aug-07 A
DES6080	100% Submission	DES6080	0.0d	0.0d	100%			14-Aug-07	14-Aug-07 A
DES6090	Back Check Review	DES6090	2.0d	0.0d	100%	15-Aug-07	15-Aug-07 A	16-Aug-07	16-Aug-07 A
DES6110	RFP Evaluation	DES6080	6.0d	0.0d	100%	15-Aug-07	15-Aug-07 A	20-Aug-07	20-Aug-07 A
DES6100	RTA RFP (Corrected Finals)	DES6100, REO23000, REO22000, REO21000	1.0d	0.0d	100%	17-Aug-07	17-Aug-07 A	17-Aug-07	17-Aug-07 A
DES6030	RTA	DES6110, REO21000, REO22000, REO23000	0.0d	0.0d	100%			20-Aug-07	20-Aug-07 A
DES6115	Issue RFP	DES6120	0.0d	0.0d	100%			24-Aug-07	24-Aug-07 A
DES6125	Proposal Evaluation	DES6125, ENV17140	5.0d	0.0d	100%	19-Sep-07	19-Sep-07 A	21-Sep-07	21-Sep-07 A
DES6130	Award Task Order		0.0d	0.0d	100%			28-Sep-07	28-Sep-07 A
143875.40000.075.01.02.003 K-1 (2015-1/2/3) RFP#7 (3.59 Miles) SEA El Paso Station			158.0d	19.0d		12-Jun-07	12-Jun-07 A		29-Jan-08
DES6005	A-E Services	DES5890	80.0d	28.0d	80%	12-Jun-07	12-Jun-07 A		29-Jan-08
DES5890	Design Start		0.0d	0.0d	100%	12-Jun-07	12-Jun-07 A		
DES5910	Prepare Draft RFP	DES5890	49.0d	6.0d	0%	12-Jun-07	12-Jun-07 A		07-Jan-08
DES5915	Government Site Visit	DES5910	1.0d	0.0d	100%	10-Jul-07	10-Jul-07 A	10-Jul-07	10-Jul-07 A
DES5990	Proposal Preparation	DES5985	17.0d	17.0d	0%		02-Jan-08*		18-Jan-08
DES6000	Award Task Order	DES5995, ENV17270	0.0d	0.0d	0%				02-Jan-08*
DES5992	Final Site Visit	DES5990	5.0d	5.0d	0%		07-Jan-08		11-Jan-08
DES5920	RFP Review-95%	DES5910	5.0d	5.0d	0%		08-Jan-08		12-Jan-08
DES5925	Comment Annotation	DES5920	2.0d	2.0d	0%		13-Jan-08		14-Jan-08

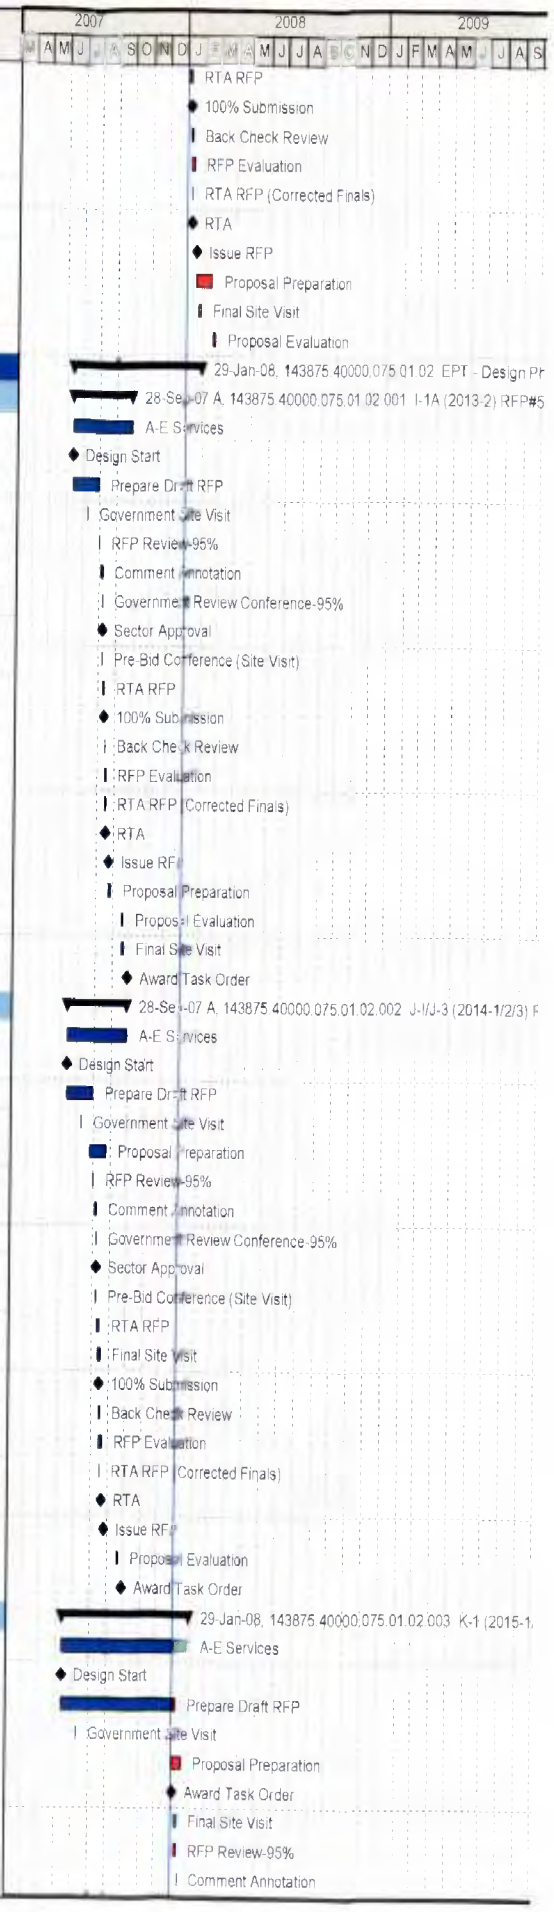

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES5930	Government Review Conference-95%	DES5925	1.0d	1.0d	0%		15-Jan-08		15-Jan-08
DES5935	Sector Approval	DES5930	0.0d	0.0d	0%				15-Jan-08
DES5880	Pre-Bid Conference (Site Visit)	DES5930	2.0d	2.0d	0%		16-Jan-08		17-Jan-08
DES5940	RTA RFP	DES5880	5.0d	5.0d	0%		18-Jan-08		22-Jan-08
DES5995	Proposal Evaluation	DES5990	8.0d	8.0d	0%		19-Jan-08		26-Jan-08
DES5950	100% Submission	DES5940	0.0d	0.0d	0%				22-Jan-08
DES5960	Back Check Review	DES5950	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
DES5980	RFP Evaluation	DES5950	4.0d	4.0d	0%		23-Jan-08		26-Jan-08
DES5970	RTA RFP (Corrected Finals)	DES5960	1.0d	1.0d	0%		25-Jan-08		25-Jan-08
DES5900	RTA	DES5970, REO46025, REO46035, REO46045	0.0d	0.0d	0%				25-Jan-08
DES5985	Issue RFP	DES5980, REO46025, REO46035, REO46045	0.0d	0.0d	0%				25-Jan-08
143875.40000.075.01.xx Not Used			0.0d	0.0d		18-May-07	18-May-07 A	18-May-07	18-May-07 A
143875.40000.150 Design Phase 2			[illegible]	173.0d		01-Oct-07	01-Oct-07 A		[illegible]
143875.40000.150.01 Design Phase 2 (176.46 miles)			567.0d	173.0d		01-Oct-07	01-Oct-07 A		05-Sep-08
143875.40000.150.01.01 SDC (14.01 miles)-Design Phase 2			[illegible]	140.0d		01-Oct-07	01-Oct-07 A		21-Jul-08
143875.40000.150.01.01.001 A-1 (3.58 miles)			195.0d	9.0d		01-Oct-07	01-Oct-07 A		14-Jan-08
DES13160	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES13282	A-E Services	DES13160	149.0d	9.0d	1.3%	01-Oct-07	01-Oct-07 A		14-Jan-08
DES13162	Gov Site Review Meeting	DES13160	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13164	Prepare Draft RFP	DES13162	194.0d	0.0d	100%	03-Dec-07	03-Dec-07 A	14-Dec-07	14-Dec-07 A
DES13166	Submit Draft RFP	DES13164	0.0d	0.0d	100%			14-Dec-07	14-Dec-07 A
DES13168	RFP Review-95%	DES13166	1.0d	0.0d	100%	17-Dec-07	17-Dec-07 A	19-Dec-07	19-Dec-07 A
DES13170	Review Conference-95%	DES13168	1.0d	0.0d	100%	19-Dec-07	19-Dec-07 A	19-Dec-07	19-Dec-07 A
DES13172	Prepare Final RFP	DES13170	2.0d	0.0d	100%	20-Dec-07	20-Dec-07 A	20-Dec-07	20-Dec-07 A
DES13174	Submit Final RFP	DES13172	0.0d	0.0d	100%			21-Dec-07	21-Dec-07 A
DES13176	Issue RFP	DES13174	1.0d	0.0d	100%	21-Dec-07	21-Dec-07 A	21-Dec-07	21-Dec-07 A
DES13178	Contractor Proposal Preparation	DES13176	4.0d	4.0d	0%		02-Jan-08		07-Jan-08
DES13180	Contractor Proposal Evaluation	DES13178	2.0d	2.0d	0%		09-Jan-08*		10-Jan-08
DES13182	Contract Prep	DES13180	2.0d	2.0d	0%		11-Jan-08		14-Jan-08
DES13184	Contract Award for 3.58 miles PF	DES13182, DES13282	0.0d	0.0d	0%				14-Jan-08
143875.40000.150.01.01.002 A-2 (10.43 miles)			195.0d	140.0d		01-Oct-07	01-Oct-07 A		21-Jul-08
DES13212	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES18530	A-E Services	DES13212	149.0d	133.0d	1.3%	01-Oct-07	01-Oct-07 A		10-Jul-08
DES13214	Gov Site Review Meeting	DES13212	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13216	Prepare Draft RFP	DES13214	194.0d	93.0d	0%	03-Oct-07	03-Oct-07 A		13-May-08
DES13218	Submit Draft RFP	DES13216	0.0d	0.0d	0%				13-May-08
DES13220	RFP Review-95%	DES13218	7.0d	7.0d	0%		14-May-08		22-May-08
DES13222	Review Conference-95%	DES13220	1.0d	1.0d	0%		23-May-08		23-May-08
DES13224	Prepare Final RFP	DES13222	6.0d	6.0d	0%		27-May-08		03-Jun-08
DES13226	Submit Final RFP	DES13224	0.0d	0.0d	0%				03-Jun-08
DES13228	Issue RFP	DES13226	1.0d	1.0d	0%		04-Jun-08		04-Jun-08
DES13230	Contractor Proposal Preparation	DES13228	20.0d	20.0d	0%		05-Jun-08		02-Jul-08
DES13232	Contractor Proposal Evaluation	DES13230, DES18530	5.0d	5.0d	0%		03-Jul-08		10-Jul-08
DES13234	Contract Prep	DES13232	7.0d	7.0d	0%		11-Jul-08		21-Jul-08
DES13236	Contract Award for 10.43 miles PF	DES13234	0.0d	0.0d	0%				21-Jul-08
143875.40000.150.01.02 ELC (11.44 miles)-Design Phase 2			195.0d	73.0d		01-Oct-07	01-Oct-07 A		15-Apr-08
143875.40000.150.01.02.001 B-4 (8.59 miles)			195.0d	73.0d		01-Oct-07	01-Oct-07 A		15-Apr-08
DES13186	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7302	A-E Services	DES13186	159.0d	60.0d	0%	01-Oct-07	01-Oct-07 A		27-Mar-08
DES13188	Gov Site Review Meeting	DES13186	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13190	Prepare Draft RFP	DES13188	194.0d	26.0d	0%	03-Oct-07	03-Oct-07 A		07-Feb-08
DES13192	Submit Draft RFP	DES13190	0.0d	0.0d	0%				07-Feb-08
DES13194	RFP Review-95%	DES13192	7.0d	7.0d	0%		08-Feb-08		19-Feb-08
DES13196	Review Conference-95%	DES13194	1.0d	1.0d	0%		20-Feb-08		20-Feb-08
DES13198	Prepare Final RFP	DES13196	6.0d	6.0d	0%		21-Feb-08		28-Feb-08
DES13200	Submit Final RFP	DES13198	0.0d	0.0d	0%				28-Feb-08
DES13202	Issue RFP	DES13200	1.0d	1.0d	0%		29-Feb-08		29-Feb-08
DES13204	Contractor Proposal Preparation	DES13202	20.0d	20.0d	0%		03-Mar-08		28-Mar-08
DES13206	Contractor Proposal Evaluation	DES13204	5.0d	5.0d	0%		31-Mar-08		04-Apr-08
DES13208	Contract Prep	DES13206	7.0d	7.0d	0%		07-Apr-08		15-Apr-08
DES13210	Contract Award for 11.44 miles PF	DES13208, DES7302	0.0d	0.0d	0%				15-Apr-08
143875.40000.150.01.02.002 B-5B (2.85 miles)			195.0d	73.0d		01-Oct-07	01-Oct-07 A		15-Apr-08
DES14070	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		

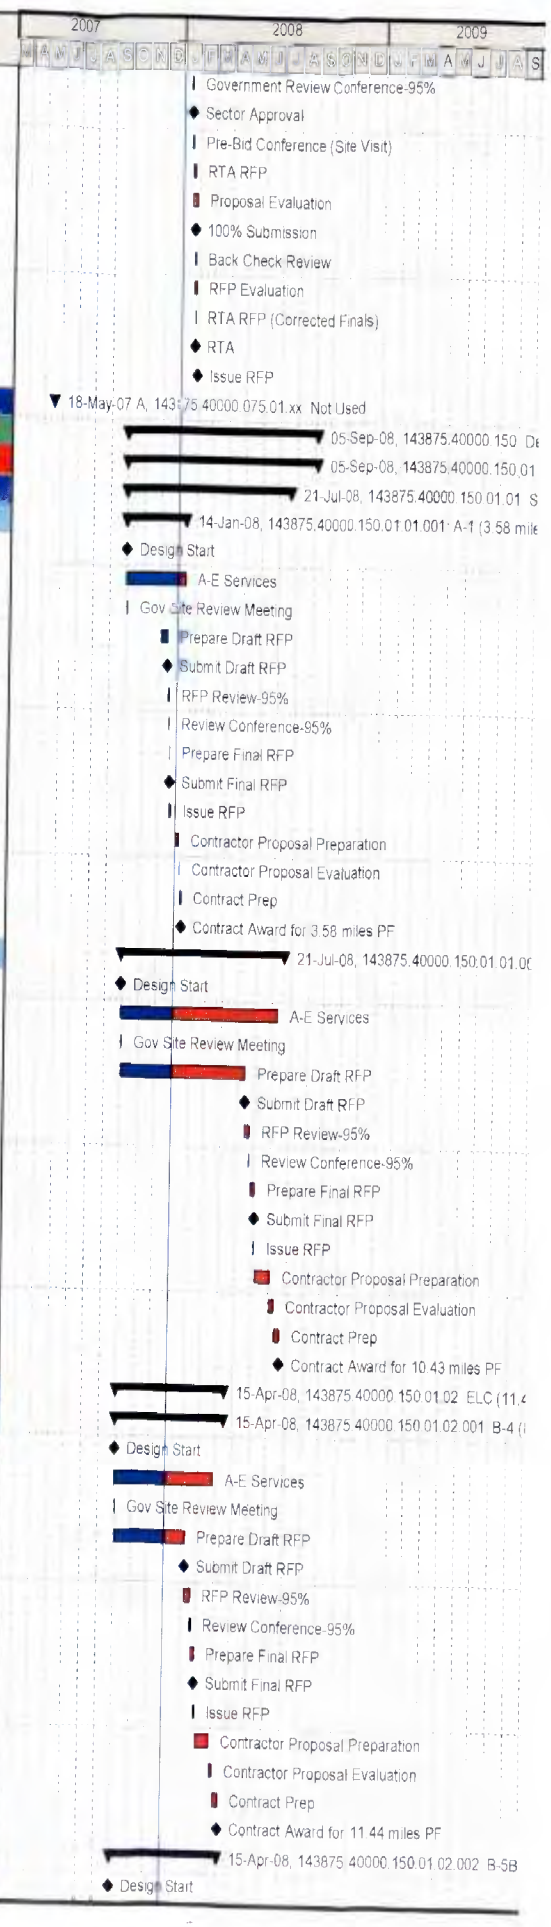

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES7304	A-E Services	DES14070	159.0d	60.0d	0%	01-Oct-07	01-Oct-07 A		27-Mar-08
DES14068	Gov Site Review Meeting	DES14070	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14072	Prepare Draft RFP	DES14068	194.0d	26.0d	0%	03-Oct-07	03-Oct-07 A		07-Feb-08
DES14086	Submit Draft RFP	DES14072	0.0d	0.0d	0%				07-Feb-08
DES14074	RFP Review-95%	DES14086	7.0d	7.0d	0%		08-Feb-08		19-Feb-08
DES14076	Review Conference-95%	DES14074	1.0d	1.0d	0%		20-Feb-08		20-Feb-08
DES14078	Prepare Final RFP	DES14076	6.0d	6.0d	0%		21-Feb-08		28-Feb-08
DES14080	Submit Final RFP	DES14078	0.0d	0.0d	0%				28-Feb-08
DES14082	Issue RFP	DES14080	1.0d	1.0d	0%		29-Feb-08		29-Feb-08
DES14088	Contractor Proposal Preparation	DES14082, DES7304	20.0d	20.0d	0%		03-Mar-08		28-Mar-08
DES14090	Contractor Proposal Evaluation	DES14088	5.0d	5.0d	0%		31-Mar-08		04-Apr-08
DES14092	Contract Prep	DES14090	7.0d	7.0d	0%		07-Apr-08		15-Apr-08
DES14084	Contract Award for 2.85 miles PF	DES14092	0.0d	0.0d	0%				15-Apr-08
143875.40000.150.01.03 YUM (13.98 miles)-Design Phase 2			195.0d	92.0d		01-Oct-07	01-Oct-07 A		12-May-08
143875.40000.150.01.03.001 C-1 (10.28 miles)			195.0d	92.0d		01-Oct-07	01-Oct-07 A		12-May-08
DES13238	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7562	A-E Services	DES13238	149.0d	79.0d	2%	01-Oct-07	01-Oct-07 A		23-Apr-08
DES13240	Gov Site Review Meeting	DES13238	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13242	Prepare Draft RFP	DES13240	194.0d	44.0d	0%	03-Oct-07	03-Oct-07 A		05-Mar-08
DES13244	Submit Draft RFP	DES13242	0.0d	0.0d	0%				05-Mar-08
DES13246	RFP Review-95%	DES13244	7.0d	7.0d	0%		06-Mar-08		14-Mar-08
DES13248	Review Conference-95%	DES13246	1.0d	1.0d	0%		17-Mar-08		17-Mar-08
DES13250	Prepare Final RFP	DES13248	6.0d	6.0d	0%		18-Mar-08		25-Mar-08
DES13252	Submit Final RFP	DES13250	0.0d	0.0d	0%				25-Mar-08
DES13254	Issue RFP	DES13252	1.0d	1.0d	0%		26-Mar-08		26-Mar-08
DES13256	Contractor Proposal Preparation	DES13254, DES7562	21.0d	21.0d	0%		27-Mar-08		24-Apr-08
DES13258	Contractor Proposal Evaluation	DES13256	5.0d	5.0d	0%		25-Apr-08		01-May-08
DES13260	Contract Prep	DES13258	7.0d	7.0d	0%		02-May-08		12-May-08
DES13262	Contract Award for 10.28 miles PF	DES13260	0.0d	0.0d	0%				12-May-08
143875.40000.150.01.03.002 C-2B (3.70 miles)			195.0d	84.0d		01-Oct-07	01-Oct-07 A		30-Apr-08
DES13264	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7692	A-E Services	DES13264	160.0d	72.0d	2%	01-Oct-07	01-Oct-07 A		14-Apr-08
DES13266	Gov Site Review Meeting	DES13264	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13268	Prepare Draft RFP	DES13266	194.0d	37.0d	0%	03-Oct-07	03-Oct-07 A		25-Feb-08
DES13270	Submit Draft RFP	DES13268	0.0d	0.0d	0%				25-Feb-08
DES13272	RFP Review-95%	DES13270	7.0d	7.0d	0%		26-Feb-08		05-Mar-08
DES13274	Review Conference-95%	DES13272	1.0d	1.0d	0%		06-Mar-08		06-Mar-08
DES13276	Prepare Final RFP	DES13274	6.0d	6.0d	0%		07-Mar-08		14-Mar-08
DES13278	Submit Final RFP	DES13276	0.0d	0.0d	0%				14-Mar-08
DES13280	Issue RFP	DES13278	1.0d	1.0d	0%		17-Mar-08		17-Mar-08
DES13284	Contractor Proposal Preparation	DES13280, DES7692	20.0d	20.0d	0%		18-Mar-08		14-Apr-08
DES13286	Contractor Proposal Evaluation	DES13284	5.0d	5.0d	0%		15-Apr-08		21-Apr-08
DES13292	Contract Prep	DES13286	7.0d	7.0d	0%		22-Apr-08		30-Apr-08
DES13294	Contract Award for 3.70 miles PF	DES13292	0.0d	0.0d	0%				30-Apr-08
143875.40000.150.01.04 TCA (7.39 miles)-Design Phase 2			544.0d	102.0d		01-Oct-07	01-Oct-07 A		27-May-08
143875.40000.150.01.04.001 D-5B (5.16 miles)			544.0d	102.0d		01-Oct-07	01-Oct-07 A		27-May-08
DES13296	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7952	A-E Services	DES13296	544.0d	90.0d	1.3%	01-Oct-07	01-Oct-07 A		08-May-08
DES13298	Gov Site Review Meeting	DES13296	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13302	Prepare Draft RFP	DES13298	194.0d	54.0d	0%	03-Oct-07	03-Oct-07 A		19-Mar-08
DES13304	Submit Draft RFP	DES13302	0.0d	0.0d	0%				19-Mar-08
DES13306	RFP Review-95%	DES13304	7.0d	7.0d	0%		20-Mar-08		28-Mar-08
DES13308	Review Conference-95%	DES13306	1.0d	1.0d	0%		31-Mar-08		31-Mar-08
DES13312	Prepare Final RFP	DES13308	6.0d	6.0d	0%		01-Apr-08		08-Apr-08
DES13314	Submit Final RFP	DES13312	0.0d	0.0d	0%				08-Apr-08
DES13316	Issue RFP	DES13314	1.0d	1.0d	0%		09-Apr-08		09-Apr-08
DES13322	Contractor Proposal Preparation	DES13316, DES7952	21.0d	21.0d	0%		10-Apr-08		08-May-08
DES13324	Contractor Proposal Evaluation	DES13322	5.0d	5.0d	0%		09-May-08		15-May-08
DES13326	Contract Prep	DES13324	7.0d	7.0d	0%		16-May-08		27-May-08
DES13328	Contract Award for 5.16 miles PF	DES13326	0.0d	0.0d	0%				27-May-08
143875.40000.150.01.04.002 D-6 (2.23 miles)			544.0d	102.0d		01-Oct-07	01-Oct-07 A		27-May-08
DES14096	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7954	A-E Services	DES14096	544.0d	90.0d	1.3%	01-Oct-07	01-Oct-07 A		08-May-08

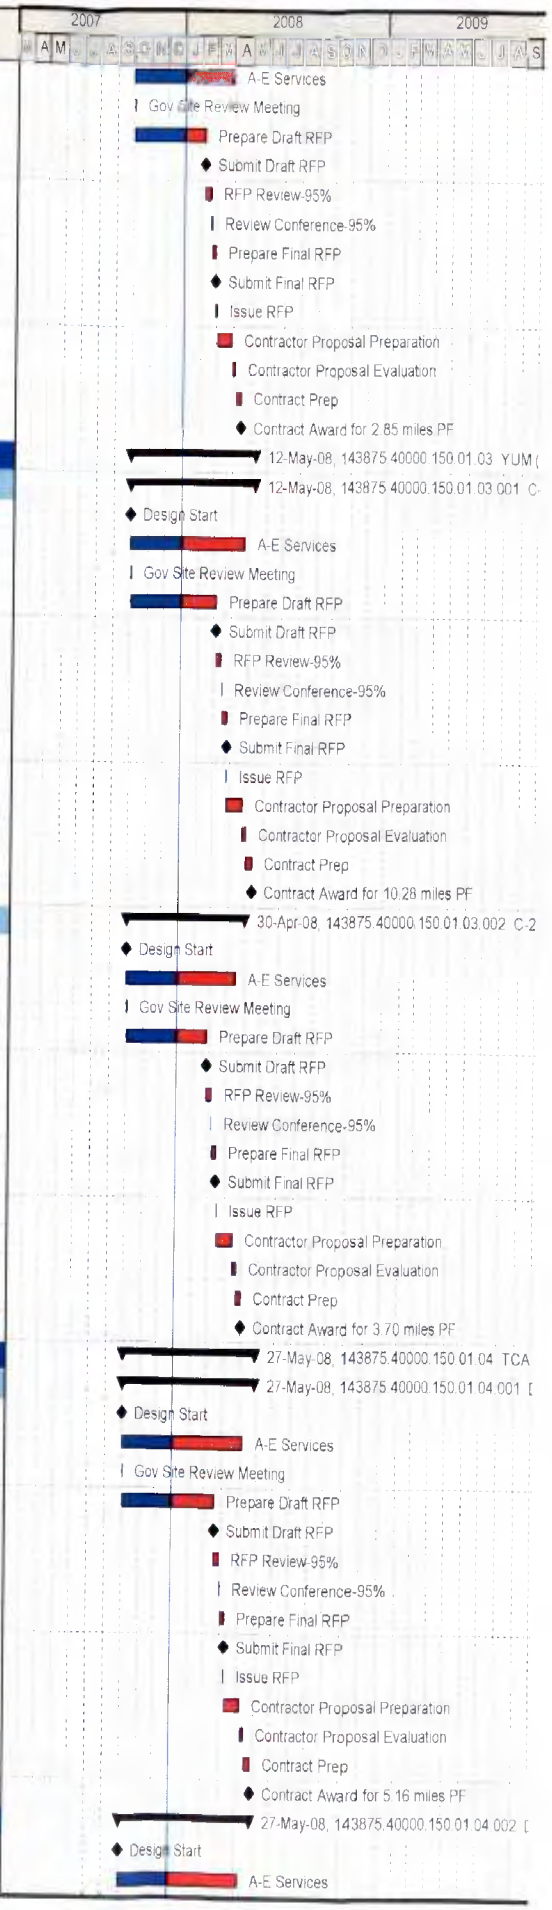

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES14094	Gov Site Review Meeting	DES14096	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14098	Prepare Draft RFP	DES14094	194.0d	54.0d	0%	03-Oct-07	03-Oct-07 A		19-Mar-08
DES14112	Submit Draft RFP	DES14098	0.0d	0.0d	0%				19-Mar-08
DES14100	RFP Review-95%	DES14112	7.0d	7.0d	0%		20-Mar-08		28-Mar-08
DES14102	Review Conference-95%	DES14100	1.0d	1.0d	0%		31-Mar-08		31-Mar-08
DES14104	Prepare Final RFP	DES14102	6.0d	6.0d	0%		01-Apr-08		08-Apr-08
DES14106	Submit Final RFP	DES14104	0.0d	0.0d	0%				08-Apr-08
DES14108	Issue RFP	DES14106	1.0d	1.0d	0%		09-Apr-08		09-Apr-08
DES14114	Contractor Proposal Preparation	DES14108, DES7954	21.0d	21.0d	0%		10-Apr-08		08-May-08
DES14116	Contractor Proposal Evaluation	DES14114	5.0d	5.0d	0%		09-May-08		15-May-08
DES14118	Contract Prep	DES14116	7.0d	7.0d	0%		16-May-08		27-May-08
DES14110	Contract Award for 2.23 miles PF	DES14118	0.0d	0.0d	0%				27-May-08
143875.40000.150.01.05 EPT (44.74) miles)-Design Phase 2			567.0d	128.0d		01-Oct-07	01-Oct-07 A		02-Jul-08
143875.40000.150.01.05.001 J-2 (3.49 miles)			544.0d	93.0d		01-Oct-07	01-Oct-07 A		13-May-08
DES14148	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7958	A-E Services	DES14166	544.0d	53.0d	1.3%	01-Oct-07	01-Oct-07 A		02-May-08
DES14146	Gov Site Review Meeting	DES14148, DES14148	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14150	Prepare Draft RFP	DES14146, DES14146	194.0d	19.0d	0%	03-Oct-07	03-Oct-07 A		29-Jan-08
DES14164	Submit Draft RFP	DES14150, DES14150	0.0d	0.0d	0%				29-Jan-08
DES14152	RFP Review-95%	DES14164, DES14164	6.0d	6.0d	0%		30-Jan-08		06-Feb-08
DES14154	Review Conference-95%	DES14152, DES14152	1.0d	1.0d	0%		07-Feb-08		07-Feb-08
DES14156	Prepare Final RFP	DES14154, DES14154	6.0d	6.0d	0%		08-Feb-08		15-Feb-08
DES14158	Submit Final RFP	DES14156, DES14156	0.0d	0.0d	0%				15-Feb-08
DES14160	Issue RFP	DES14158, DES14158	1.0d	1.0d	0%		19-Feb-08		19-Feb-08
DES14166	Contractor Proposal Preparation	DES14160, DES14160	21.0d	21.0d	0%		20-Feb-08		19-Mar-08
DES14168	Contractor Proposal Evaluation	DES14166, DES7958	5.0d	5.0d	0%		28-Apr-08		02-May-08
DES14170	Contract Prep	DES14168	7.0d	7.0d	0%		05-May-08		13-May-08
DES14162	Contract Award for 3.49 miles PF	DES14170	0.0d	0.0d	0%				13-May-08
143875.40000.150.01.05.002 K-2A (9.60 miles)			544.0d	110.0d		01-Oct-07	01-Oct-07 A		06-Jun-08
DES14122	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7956	A-E Services	DES14122	544.0d	98.0d	1.3%	01-Oct-07	01-Oct-07 A		20-May-08
DES14120	Gov Site Review Meeting	DES14122	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14124	Prepare Draft RFP	DES14120	194.0d	64.0d	0%	03-Oct-07	03-Oct-07 A		02-Apr-08
DES14138	Submit Draft RFP	DES14124	0.0d	0.0d	0%				02-Apr-08
DES14126	RFP Review-95%	DES14138	6.0d	6.0d	0%		03-Apr-08		10-Apr-08
DES14128	Review Conference-95%	DES14126	1.0d	1.0d	0%		11-Apr-08		11-Apr-08
DES14130	Prepare Final RFP	DES14128	5.0d	5.0d	0%		14-Apr-08		18-Apr-08
DES14132	Submit Final RFP	DES14130	0.0d	0.0d	0%				18-Apr-08
DES14134	Issue RFP	DES14132	1.0d	1.0d	0%		21-Apr-08		21-Apr-08
DES14140	Contractor Proposal Preparation	DES14134, DES7956	21.0d	21.0d	0%		22-Apr-08		20-May-08
DES14142	Contractor Proposal Evaluation	DES14140	5.0d	5.0d	0%		21-May-08		28-May-08
DES14144	Contract Prep	DES14142	7.0d	7.0d	0%		29-May-08		06-Jun-08
DES14136	Contract Award for 9.60 miles PF	DES14144	0.0d	0.0d	0%				06-Jun-08
143875.40000.150.01.05.003 K-2B&C (19.42 miles)			195.0d	113.0d		01-Oct-07	01-Oct-07 A		11-Jun-08
DES13332	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES8212	A-E Services	DES13332	160.0d	101.0d	2%	01-Oct-07	01-Oct-07 A		23-May-08
DES13334	Gov Site Review Meeting	DES13332	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13336	Prepare Draft RFP	DES13334	194.0d	67.0d	0%	03-Oct-07	03-Oct-07 A		07-Apr-08
DES13338	Submit Draft RFP	DES13336	0.0d	0.0d	0%				07-Apr-08
DES13342	RFP Review-95%	DES13338	6.0d	6.0d	0%		08-Apr-08		15-Apr-08
DES13344	Review Conference-95%	DES13342	1.0d	1.0d	0%		16-Apr-08		16-Apr-08
DES13346	Prepare Final RFP	DES13344	5.0d	5.0d	0%		17-Apr-08		23-Apr-08
DES13348	Submit Final RFP	DES13346	0.0d	0.0d	0%				23-Apr-08
DES13352	Issue RFP	DES13348	1.0d	1.0d	0%		24-Apr-08		24-Apr-08
DES13354	Contractor Proposal Preparation	DES13352, DES8212	21.0d	21.0d	0%		25-Apr-08		23-May-08
DES13356	Contractor Proposal Evaluation	DES13354	5.0d	5.0d	0%		27-May-08		02-Jun-08
DES13362	Contract Prep	DES13356	7.0d	7.0d	0%		03-Jun-08		11-Jun-08
DES13364	Contract Award for 19.42 miles PF	DES13362	0.0d	0.0d	0%				11-Jun-08
143875.40000.150.01.05.004 K-3 (9.02 miles)			218.0d	109.0d		01-Oct-07	01-Oct-07 A		05-Jun-08
DES13366	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES8992	A-E Services	DES13366	139.0d	97.0d	0%	01-Oct-07	01-Oct-07 A		19-May-08
DES13368	Gov Site Review Meeting	DES13366	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13370	Prepare Draft RFP	DES13368	194.0d	63.0d	0%	03-Oct-07	03-Oct-07 A		01-Apr-08

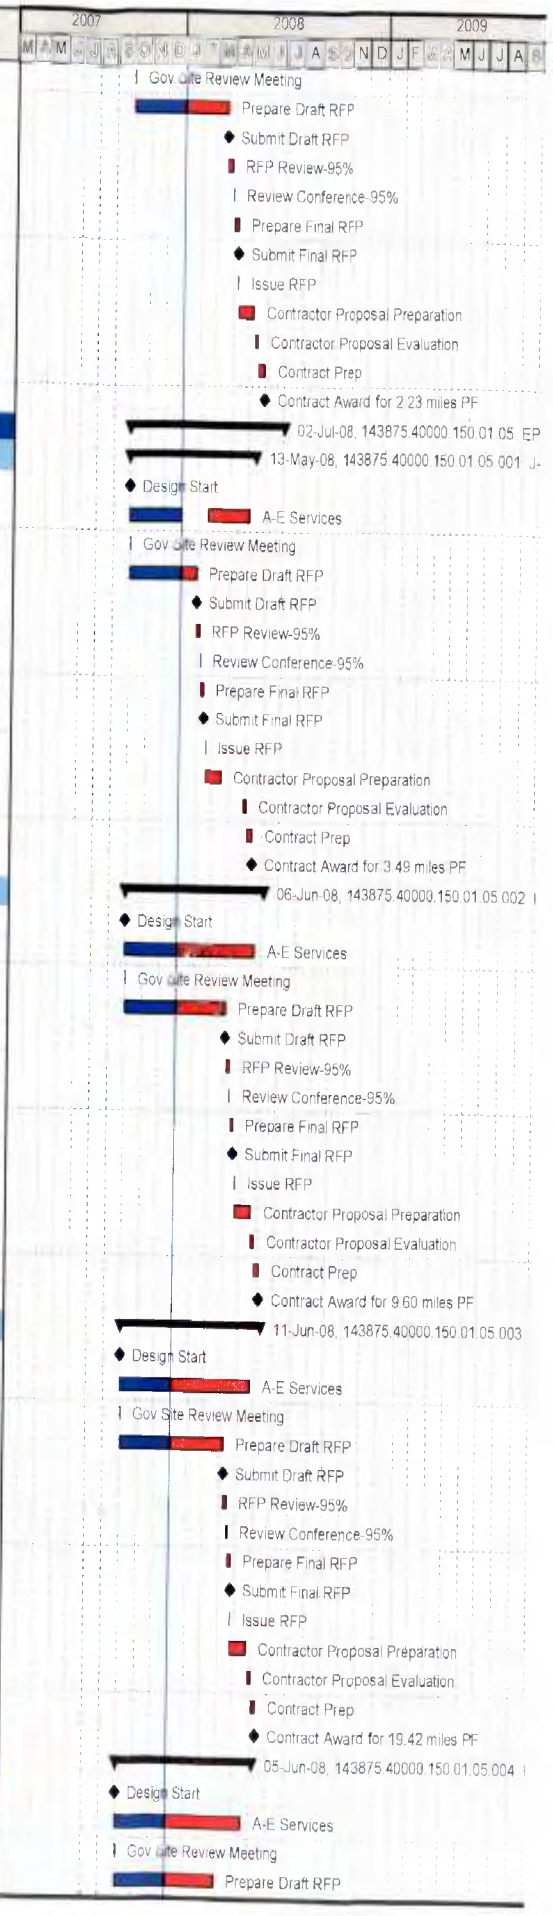

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13372	Submit Draft RFP	DES13370	0.0d	0.0d	0%				01-Apr-08
DES13374	RFP Review-95%	DES13372	6.0d	6.0d	0%		02-Apr-08		09-Apr-08
DES13376	Review Conference-95%	DES13374	1.0d	1.0d	0%		10-Apr-08		10-Apr-08
DES13378	Prepare Final RFP	DES13376	5.0d	5.0d	0%		11-Apr-08		17-Apr-08
DES13380	Submit Final RFP	DES13378	0.0d	0.0d	0%				17-Apr-08
DES13382	Issue RFP	DES13380	1.0d	1.0d	0%		18-Apr-08		18-Apr-08
DES13384	Contractor Proposal Preparation	DES13382, DES8992	21.0d	21.0d	0%		21-Apr-08		19-May-08
DES13386	Contractor Proposal Evaluation	DES13384	5.0d	5.0d	0%		20-May-08		27-May-08
DES13388	Contract Prep	DES13386	7.0d	7.0d	0%		28-May-08		05-Jun-08
DES13390	Contract Award for 9.02 miles PF	DES13388	0.0d	0.0d	0%				05-Jun-08
143875.40000.150.01.05.005 K-5 (5.21 miles)			195.0d	128.0d		01-Oct-07	01-Oct-07 A		02-Jul-08
DES13392	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES8862	A-E Services	DES13392	160.0d	117.0d	2%	01-Oct-07	01-Oct-07 A		17-Jun-08
DES13394	Gov Site Review Meeting	DES13392	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13396	Prepare Draft RFP	DES13394	194.0d	81.0d	0%	03-Oct-07	03-Oct-07 A		25-Apr-08
DES13398	Submit Draft RFP	DES13396	0.0d	0.0d	0%				25-Apr-08
DES13400	RFP Review-95%	DES13398	7.0d	7.0d	0%		28-Apr-08		06-May-08
DES13402	Review Conference-95%	DES13400	1.0d	1.0d	0%		07-May-08		07-May-08
DES13404	Prepare Final RFP	DES13402	6.0d	6.0d	0%		08-May-08		15-May-08
DES13406	Submit Final RFP	DES13404	0.0d	0.0d	0%				15-May-08
DES13408	Issue RFP	DES13406	1.0d	1.0d	0%		16-May-08		16-May-08
DES13410	Contractor Proposal Preparation	DES13408, DES8862	21.0d	21.0d	0%		19-May-08		17-Jun-08
DES13412	Contractor Proposal Evaluation	DES13410	5.0d	5.0d	0%		18-Jun-08		24-Jun-08
DES13414	Contract Prep	DES13412	6.0d	6.0d	0%		25-Jun-08		02-Jul-08
DES13416	Contract Award for 5.21 miles PF	DES13414	0.0d	0.0d	0%				02-Jul-08
143875.40000.150.01.06 MAR (10.78 miles)-Design Phase 2			229.0d	167.0d		01-Oct-07	01-Oct-07 A		27-Aug-08
143875.40000.150.01.06.001 L-1 (4.63 miles)			206.0d	167.0d		01-Oct-07	01-Oct-07 A		27-Aug-08
DES14174	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES7960	A-E Services	DES14174	200.0d	155.0d	1.3%	01-Oct-07	01-Oct-07 A		11-Aug-08
DES14172	Gov Site Review Meeting	DES14174	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14176	Prepare Draft RFP	DES14172	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES14190	Submit Draft RFP	DES14176	0.0d	0.0d	0%				23-Jun-08
DES14178	RFP Review-95%	DES14190	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES14180	Review Conference-95%	DES14178	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES14182	Prepare Final RFP	DES14180	5.0d	5.0d	0%		07-Jul-08		11-Jul-08
DES14184	Submit Final RFP	DES14182	0.0d	0.0d	0%				11-Jul-08
DES14186	Issue RFP	DES14184	1.0d	1.0d	0%		14-Jul-08		14-Jul-08
DES14192	Contractor Proposal Preparation	DES14186, DES7960	20.0d	20.0d	0%		15-Jul-08		11-Aug-08
DES14194	Contractor Proposal Evaluation	DES14192	5.0d	5.0d	0%		12-Aug-08		18-Aug-08
DES14196	Contract Prep	DES14194	7.0d	7.0d	0%		19-Aug-08		27-Aug-08
DES14188	Contract Award for 4.63 miles PF	DES14196	0.0d	0.0d	0%				27-Aug-08
143875.40000.150.01.06.002 L-1A (3.28 miles)			195.0d	118.0d		01-Oct-07	01-Oct-07 A		18-Jun-08
DES13418	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES8214	A-E Services	DES13418	160.0d	106.0d	2%	01-Oct-07	01-Oct-07 A		02-Jun-08
DES13420	Gov Site Review Meeting	DES13418	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13422	Prepare Draft RFP	DES13420	194.0d	72.0d	0%	03-Oct-07	03-Oct-07 A		14-Apr-08
DES13424	Submit Draft RFP	DES13422	0.0d	0.0d	0%				14-Apr-08
DES13426	RFP Review-95%	DES13424	6.0d	6.0d	0%		15-Apr-08		22-Apr-08
DES13428	Review Conference-95%	DES13426	1.0d	1.0d	0%		23-Apr-08		23-Apr-08
DES13430	Prepare Final RFP	DES13428	5.0d	5.0d	0%		24-Apr-08		30-Apr-08
DES13432	Submit Final RFP	DES13430	0.0d	0.0d	0%				30-Apr-08
DES13434	Issue RFP	DES13432	1.0d	1.0d	0%		01-May-08		01-May-08
DES13436	Contractor Proposal Preparation	DES13434, DES8214	21.0d	21.0d	0%		02-May-08		02-Jun-08
DES13438	Contractor Proposal Evaluation	DES13436	5.0d	5.0d	0%		03-Jun-08		09-Jun-08
DES13440	Contract Prep	DES13438	7.0d	7.0d	0%		10-Jun-08		18-Jun-08
DES13442	Contract Award for 3.28 miles PF	DES13440	0.0d	0.0d	0%				18-Jun-08
143875.40000.150.01.06.003 L-1B (2.87 miles)			218.0d	118.0d		01-Oct-07	01-Oct-07 A		18-Jun-08
DES13444	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES9252	A-E Services	DES13444	148.0d	106.0d	0%	01-Oct-07	01-Oct-07 A		02-Jun-08
DES13446	Gov Site Review Meeting	DES13444	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13448	Prepare Draft RFP	DES13446	194.0d	72.0d	0%	03-Oct-07	03-Oct-07 A		14-Apr-08
DES13450	Submit Draft RFP	DES13448	0.0d	0.0d	0%				14-Apr-08
DES13452	RFP Review-95%	DES13450	6.0d	6.0d	0%		15-Apr-08		22-Apr-08

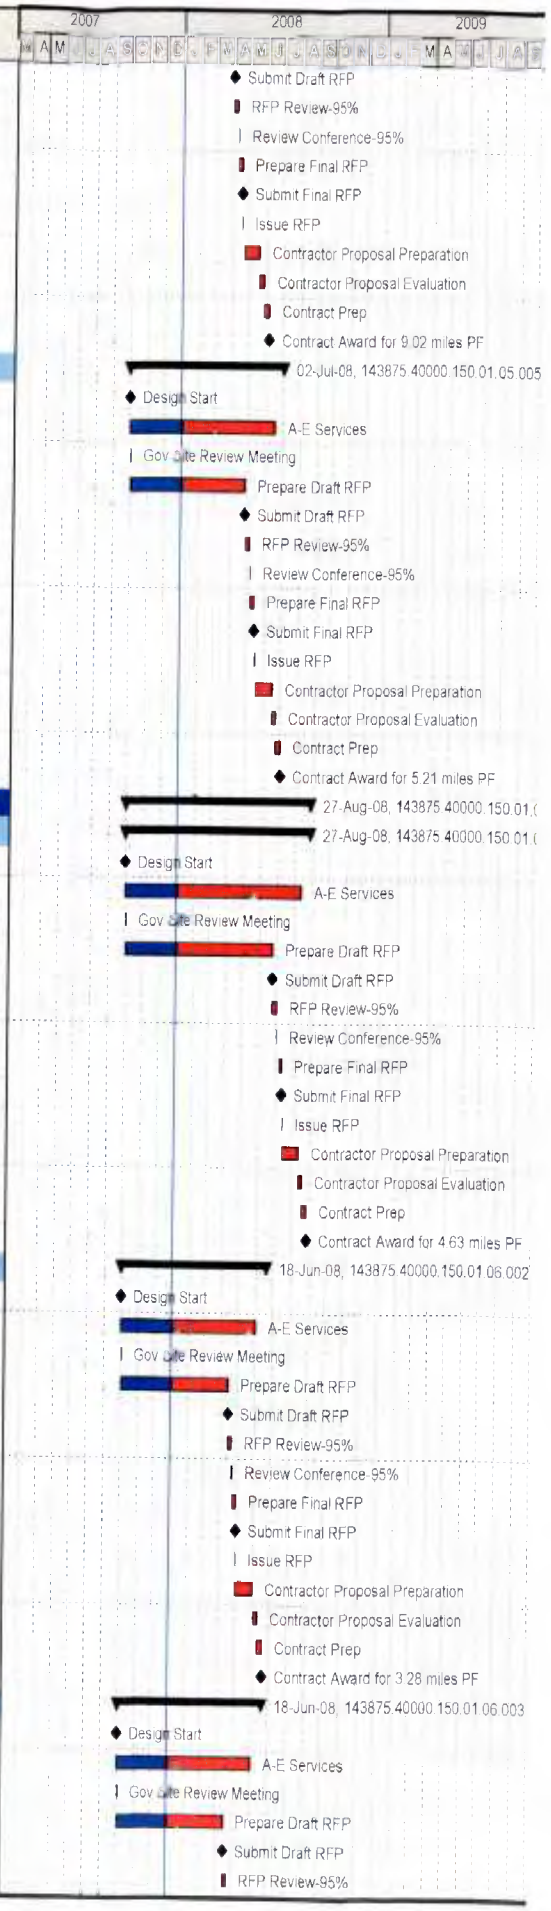

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13454	Review Conference-95%	DES13452	1.0d	1.0d	0%		23-Apr-08		23-Apr-08
DES13456	Prepare Final RFP	DES13454	5.0d	5.0d	0%		24-Apr-08		30-Apr-08
DES13458	Submit Final RFP	DES13456	0.0d	0.0d	0%				30-Apr-08
DES13460	Issue RFP	DES13458	1.0d	1.0d	0%		01-May-08		01-May-08
DES13462	Contractor Proposal Preparation	DES13460, DES9252	21.0d	21.0d	0%		02-May-08		02-Jun-08
DES13464	Contractor Proposal Evaluation	DES13462	5.0d	5.0d	0%		03-Jun-08		09-Jun-08
DES13466	Contract Prep	DES13464	7.0d	7.0d	0%		10-Jun-08		18-Jun-08
DES13468	Contract Award for 2.87 miles PF	DES13466	0.0d	0.0d	0%				18-Jun-08
143875.40000.150.01.07 DRT (4.17 miles)-Design Phase-2			218.0d	150.0d		01-Oct-07	01-Oct-07 A		04-Aug-08
143875.40000.150.01.07.001 M-1 (2.36 miles)			218.0d	110.0d		01-Oct-07	01-Oct-07 A		06-Jun-08
DES13470	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES12892	A-E Services	DES13470	140.0d	98.0d	0%	01-Oct-07	01-Oct-07 A		20-May-08
DES13472	Gov Site Review Meeting	DES13470	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13474	Prepare Draft RFP	DES13472	194.0d	62.0d	0%	03-Oct-07	03-Oct-07 A		31-Mar-08
DES13476	Submit Draft RFP	DES13474	0.0d	0.0d	0%				31-Mar-08
DES13478	RFP Review-95%	DES13476	7.0d	7.0d	0%		01-Apr-08		09-Apr-08
DES13480	Review Conference-95%	DES13478	1.0d	1.0d	0%		10-Apr-08		10-Apr-08
DES13482	Prepare Final RFP	DES13480	6.0d	6.0d	0%		11-Apr-08		18-Apr-08
DES13484	Submit Final RFP	DES13482	0.0d	0.0d	0%				18-Apr-08
DES13486	Issue RFP	DES13484	1.0d	1.0d	0%		21-Apr-08		21-Apr-08
DES13488	Contractor Proposal Preparation	DES13486	21.0d	21.0d	0%		22-Apr-08		20-May-08
DES13490	Contractor Proposal Evaluation	DES13488, DES12892	5.0d	5.0d	0%		21-May-08		28-May-08
DES13492	Contract Prep	DES13490	7.0d	7.0d	0%		29-May-08		06-Jun-08
DES13494	Contract Award for 2.36 miles PF	DES13492	0.0d	0.0d	0%				06-Jun-08
143875.40000.150.01.07.002 M-2A (0.75 miles)			218.0d	150.0d		01-Oct-07	01-Oct-07 A		04-Aug-08
DES13496	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES12894	A-E Services	DES13496	140.0d	139.0d	0%	01-Oct-07	01-Oct-07 A		18-Jul-08
DES13498	Gov Site Review Meeting	DES13496	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13500	Prepare Draft RFP	DES13498	194.0d	104.0d	0%	03-Oct-07	03-Oct-07 A		29-May-08
DES13502	Submit Draft RFP	DES13500	0.0d	0.0d	0%				29-May-08
DES13504	RFP Review-95%	DES13502	7.0d	7.0d	0%		30-May-08		09-Jun-08
DES13506	Review Conference-95%	DES13504	1.0d	1.0d	0%		10-Jun-08		10-Jun-08
DES13508	Prepare Final RFP	DES13506	6.0d	6.0d	0%		11-Jun-08		18-Jun-08
DES13510	Submit Final RFP	DES13508	0.0d	0.0d	0%				18-Jun-08
DES13512	Issue RFP	DES13510	1.0d	1.0d	0%		19-Jun-08		19-Jun-08
DES13514	Contractor Proposal Preparation	DES13512, DES12894	20.0d	20.0d	0%		20-Jun-08		18-Jul-08
DES13516	Contractor Proposal Evaluation	DES13514	5.0d	5.0d	0%		21-Jul-08		25-Jul-08
DES13518	Contract Prep	DES13516	6.0d	6.0d	0%		28-Jul-08		04-Aug-08
DES13520	Contract Award for 0.75 miles PF	DES13518	0.0d	0.0d	0%				04-Aug-08
143875.40000.150.01.07.003 M-2B (1.06 miles)			218.0d	150.0d		01-Oct-07	01-Oct-07 A		04-Aug-08
DES14200	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES12896	A-E Services	DES14200	140.0d	139.0d	0%	01-Oct-07	01-Oct-07 A		18-Jul-08
DES14198	Gov Site Review Meeting	DES14200	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14202	Prepare Draft RFP	DES14198	194.0d	104.0d	0%	03-Oct-07	03-Oct-07 A		29-May-08
DES14216	Submit Draft RFP	DES14202	0.0d	0.0d	0%				29-May-08
DES14204	RFP Review-95%	DES14216	7.0d	7.0d	0%		30-May-08		09-Jun-08
DES14206	Review Conference-95%	DES14204	1.0d	1.0d	0%		10-Jun-08		10-Jun-08
DES14208	Prepare Final RFP	DES14206	6.0d	6.0d	0%		11-Jun-08		18-Jun-08
DES14210	Submit Final RFP	DES14208	0.0d	0.0d	0%				18-Jun-08
DES14212	Issue RFP	DES14210	1.0d	1.0d	0%		19-Jun-08		19-Jun-08
DES14218	Contractor Proposal Preparation	DES14212, DES12896	20.0d	20.0d	0%		20-Jun-08		18-Jul-08
DES14220	Contractor Proposal Evaluation	DES14218	5.0d	5.0d	0%		21-Jul-08		25-Jul-08
DES14222	Contract Prep	DES14220	6.0d	6.0d	0%		28-Jul-08		04-Aug-08
DES14214	Contract Award for 1.06 miles PF	DES14222	0.0d	0.0d	0%				04-Aug-08
143875.40000.150.01.08 RGV (69.95 miles)-Design Phase- 2			235.0d	173.0d		01-Oct-07	01-Oct-07 A		05-Sep-08
143875.40000.150.01.08.001 O-1 (3.76 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13522	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46945	A-E Services	DES13522	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13524	Gov Site Review Meeting	DES13522	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13526	Prepare Draft RFP	DES13524	168.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13528	Submit Draft RFP	DES13526	0.0d	0.0d	0%				24-Jun-08
DES13530	RFP Review-95%	DES13528	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13532	Review Conference-95%	DES13530	1.0d	1.0d	0%		07-Jul-08		07-Jul-08

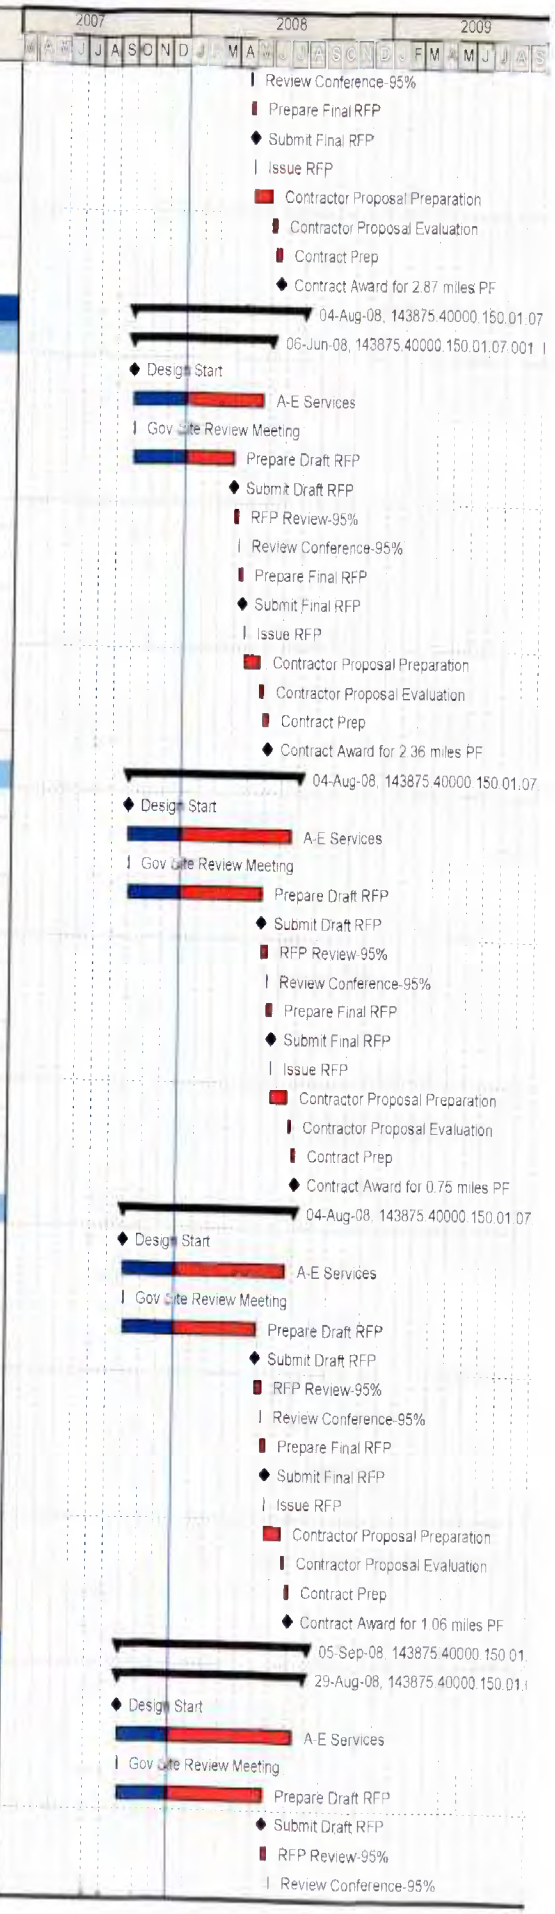

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13534	Prepare Final RFP	DES13532	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13536	Submit Final RFP	DES13534	0.0d	0.0d	0%				15-Jul-08
DES13538	Issue RFP	DES13536	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13540	Contractor Proposal Preparation	DES13538, DES46945	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13542	Contractor Proposal Evaluation	DES13540	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13544	Contract Prep	DES13542	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13546	Contract Award for 3.76 miles PF	DES13544	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.002 O-2 (8.75 miles)			233.0d	171.0d		01-Oct-07	01-Oct-07 A		03-Sep-08
DES13548	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46947	A-E Services	DES13548	212.0d	159.0d	0%	01-Oct-07	01-Oct-07 A		15-Aug-08
DES13550	Gov Site Review Meeting	DES13548	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13552	Prepare Draft RFP	DES13550	169.0d	124.0d	0%	03-Oct-07	03-Oct-07 A		26-Jun-08
DES13554	Submit Draft RFP	DES13552	0.0d	0.0d	0%				26-Jun-08
DES13556	RFP Review-95%	DES13554	7.0d	7.0d	0%		27-Jun-08		08-Jul-08
DES13558	Review Conference-95%	DES13556	1.0d	1.0d	0%		09-Jul-08		09-Jul-08
DES13560	Prepare Final RFP	DES13558	6.0d	6.0d	0%		10-Jul-08		17-Jul-08
DES13562	Submit Final RFP	DES13560	0.0d	0.0d	0%				17-Jul-08
DES13564	Issue RFP	DES13562	1.0d	1.0d	0%		18-Jul-08		18-Jul-08
DES13566	Contractor Proposal Preparation	DES13564, DES46947	20.0d	20.0d	0%		21-Jul-08		15-Aug-08
DES13568	Contractor Proposal Evaluation	DES13566	5.0d	5.0d	0%		18-Aug-08		22-Aug-08
DES13570	Contract Prep	DES13568	7.0d	7.0d	0%		25-Aug-08		03-Sep-08
DES13572	Contract Award for 8.75 miles PF	DES13570	0.0d	0.0d	0%				03-Sep-08
143875.40000.150.01.08.003 O-3 (1.85 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13574	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46949	A-E Services	DES13574	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13576	Gov Site Review Meeting	DES13574	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13578	Prepare Draft RFP	DES13576	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13580	Submit Draft RFP	DES13578	0.0d	0.0d	0%				23-Jun-08
DES13582	RFP Review-95%	DES13580	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13584	Review Conference-95%	DES13582	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13586	Prepare Final RFP	DES13584	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13588	Submit Final RFP	DES13586	0.0d	0.0d	0%				14-Jul-08
DES13590	Issue RFP	DES13588	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13592	Contractor Proposal Preparation	DES13590, DES46949	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13594	Contractor Proposal Evaluation	DES13592	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13596	Contract Prep	DES13594	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13598	Contract Award for 1.85 miles PF	DES13596	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.004 O-4 (4.35 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13600	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46985	A-E Services	DES13600	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13602	Gov Site Review Meeting	DES13600	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13604	Prepare Draft RFP	DES13602	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13606	Submit Draft RFP	DES13604	0.0d	0.0d	0%				24-Jun-08
DES13608	RFP Review-95%	DES13606	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13610	Review Conference-95%	DES13608	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13612	Prepare Final RFP	DES13610	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13614	Submit Final RFP	DES13612	0.0d	0.0d	0%				15-Jul-08
DES13616	Issue RFP	DES13614	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13618	Contractor Proposal Preparation	DES13616, DES46985	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13620	Contractor Proposal Evaluation	DES13618	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13622	Contract Prep	DES13620	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13624	Contract Award for 4.35 miles PF	DES13622	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.005 O-5 (1.73 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13626	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46983	A-E Services	DES13626	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13628	Gov Site Review Meeting	DES13626	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13630	Prepare Draft RFP	DES13628	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13632	Submit Draft RFP	DES13630	0.0d	0.0d	0%				23-Jun-08
DES13634	RFP Review-95%	DES13632	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13636	Review Conference-95%	DES13634	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13638	Prepare Final RFP	DES13636	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13640	Submit Final RFP	DES13638	0.0d	0.0d	0%				14-Jul-08
DES13642	Issue RFP	DES13640	1.0d	1.0d	0%		15-Jul-08		15-Jul-08

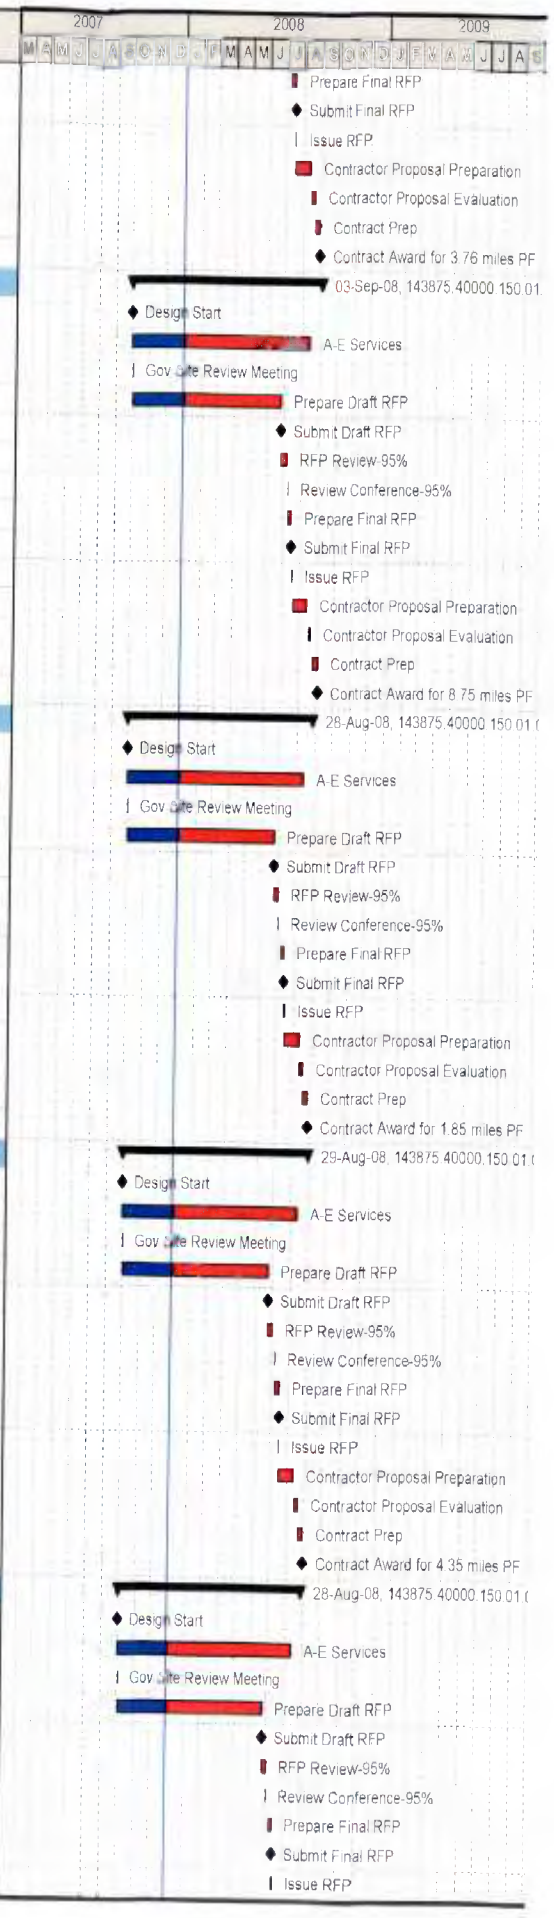

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13644	Contractor Proposal Preparation	DES13642, DES46983	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13646	Contractor Proposal Evaluation	DES13644	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13648	Contract Prep	DES13646	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13650	Contract Award for 1.73 miles PF	DES13648	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.006 O-6 (3.86 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13652	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46981	A-E Services	DES13652	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13654	Gov Site Review Meeting	DES13652	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13656	Prepare Draft RFP	DES13654	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13658	Submit Draft RFP	DES13656	0.0d	0.0d	0%				24-Jun-08
DES13660	RFP Review-95%	DES13658	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13662	Review Conference-95%	DES13660	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13664	Prepare Final RFP	DES13662	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13666	Submit Final RFP	DES13664	0.0d	0.0d	0%				15-Jul-08
DES13668	Issue RFP	DES13666	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13670	Contractor Proposal Preparation	DES13668, DES46981	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13672	Contractor Proposal Evaluation	DES13670	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13674	Contract Prep	DES13672	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13676	Contract Award for 3.86 miles PF	DES13674	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.007 O-7 (0.90 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13678	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46979	A-E Services	DES13678	208.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13680	Gov Site Review Meeting	DES13678	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13682	Prepare Draft RFP	DES13680	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13684	Submit Draft RFP	DES13682	0.0d	0.0d	0%				24-Jun-08
DES13686	RFP Review-95%	DES13684	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13688	Review Conference-95%	DES13686	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13690	Prepare Final RFP	DES13688	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13692	Submit Final RFP	DES13690	0.0d	0.0d	0%				15-Jul-08
DES13694	Issue RFP	DES13692	0.0d	0.0d	0%		16-Jul-08		16-Jul-08
DES13696	Contractor Proposal Preparation	DES13694, DES46979	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13698	Contractor Proposal Evaluation	DES13696	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13700	Contract Prep	DES13698	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13702	Contract Award for 0.90 miles PF	DES13700	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.008 O-8 (3.24 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13704	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46977	A-E Services	DES13704	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13706	Gov Site Review Meeting	DES13704	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13708	Prepare Draft RFP	DES13706	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13710	Submit Draft RFP	DES13708	0.0d	0.0d	0%				24-Jun-08
DES13712	RFP Review-95%	DES13710	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13714	Review Conference-95%	DES13712	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13716	Prepare Final RFP	DES13714	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13718	Submit Final RFP	DES13716	0.0d	0.0d	0%				15-Jul-08
DES13720	Issue RFP	DES13718	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13722	Contractor Proposal Preparation	DES13720, DES46977	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13724	Contractor Proposal Evaluation	DES13722	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13726	Contract Prep	DES13724	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13728	Contract Award for 3.24 miles PF	DES13726	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.009 O-9 (3.86 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13730	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46975	A-E Services	DES13730	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13732	Gov Site Review Meeting	DES13730	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13734	Prepare Draft RFP	DES13732	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13736	Submit Draft RFP	DES13734	0.0d	0.0d	0%				24-Jun-08
DES13738	RFP Review-95%	DES13736	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13740	Review Conference-95%	DES13738	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13742	Prepare Final RFP	DES13740	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13744	Submit Final RFP	DES13742	0.0d	0.0d	0%				15-Jul-08
DES13746	Issue RFP	DES13744	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13748	Contractor Proposal Preparation	DES13746, DES46975	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13750	Contractor Proposal Evaluation	DES13748	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13752	Contract Prep	DES13750	7.0d	7.0d	0%		21-Aug-08		29-Aug-08

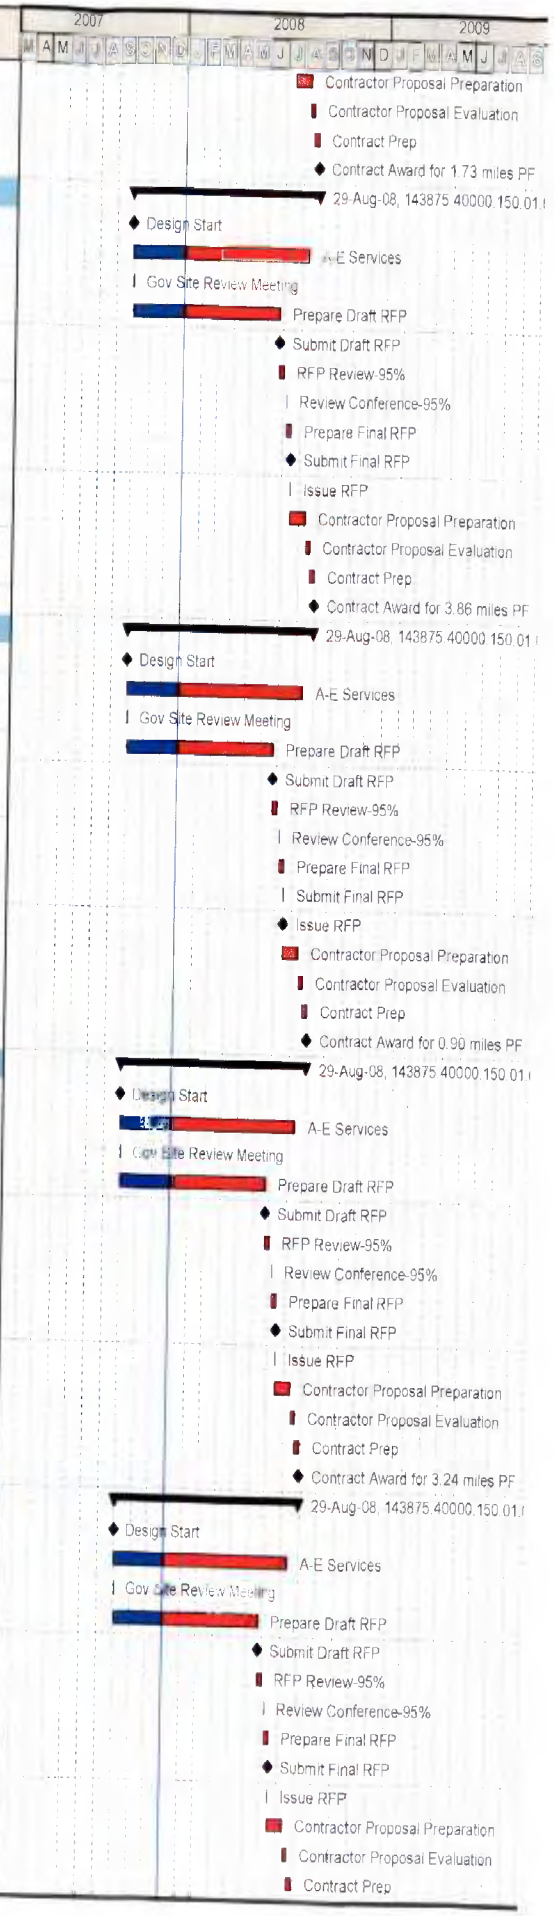

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13754	Contract Award for 3.86 miles PF	DES13752	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.010 O-10 (2.33 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13756	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46973	A-E Services	DES13756	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13758	Gov Site Review Meeting	DES13756	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13760	Prepare Draft RFP	DES13758	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13762	Submit Draft RFP	DES13760	0.0d	0.0d	0%				23-Jun-08
DES13764	RFP Review-95%	DES13762	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13766	Review Conference-95%	DES13764	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13768	Prepare Final RFP	DES13766	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13770	Submit Final RFP	DES13768	0.0d	0.0d	0%				14-Jul-08
DES13772	Issue RFP	DES13770	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13774	Contractor Proposal Preparation	DES13772, DES46973	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13776	Contractor Proposal Evaluation	DES13774	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13778	Contract Prep	DES13776	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13780	Contract Award for 2.33 miles PF	DES13778	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.011 O-11 (2.33 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13782	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46971	A-E Services	DES13782	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13784	Gov Site Review Meeting	DES13782	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13786	Prepare Draft RFP	DES13784	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13788	Submit Draft RFP	DES13786	0.0d	0.0d	0%				23-Jun-08
DES13790	RFP Review-95%	DES13788	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13792	Review Conference-95%	DES13790	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13794	Prepare Final RFP	DES13792	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13796	Submit Final RFP	DES13794	0.0d	0.0d	0%		15-Jul-08		15-Jul-08
DES13798	Issue RFP	DES13796	0.0d	0.0d	0%				15-Jul-08
DES13800	Contractor Proposal Preparation	DES13798, DES46971	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13802	Contractor Proposal Evaluation	DES13800	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13804	Contract Prep	DES13802	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13806	Contract Award for 2.33 miles PF	DES13804	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.012 O-12 (0.96 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13808	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46969	A-E Services	DES13808	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13810	Gov Site Review Meeting	DES13808	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13812	Prepare Draft RFP	DES13810	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13814	Submit Draft RFP	DES13812	0.0d	0.0d	0%				23-Jun-08
DES13816	RFP Review-95%	DES13814	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13818	Review Conference-95%	DES13816	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13820	Prepare Final RFP	DES13818	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13822	Submit Final RFP	DES13820	0.0d	0.0d	0%				14-Jul-08
DES13824	Issue RFP	DES13822	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13826	Contractor Proposal Preparation	DES13824, DES46969	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13828	Contractor Proposal Evaluation	DES13826	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13830	Contract Prep	DES13828	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13832	Contract Award for 0.96 miles PF	DES13830	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.013 O-13 (1.59 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13834	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46967	A-E Services	DES13834	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13836	Gov Site Review Meeting	DES13834	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13838	Prepare Draft RFP	DES13836	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13840	Submit Draft RFP	DES13838	0.0d	0.0d	0%				23-Jun-08
DES13842	RFP Review-95%	DES13840	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13844	Review Conference-95%	DES13842	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13846	Prepare Final RFP	DES13844	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13848	Submit Final RFP	DES13846	0.0d	0.0d	0%				14-Jul-08
DES13850	Issue RFP	DES13848	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13852	Contractor Proposal Preparation	DES13850, DES46967	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13854	Contractor Proposal Evaluation	DES13852	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13856	Contract Prep	DES13854	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13858	Contract Award for 1.59 miles PF	DES13856	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.014 O-14 (3.59 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13860	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		

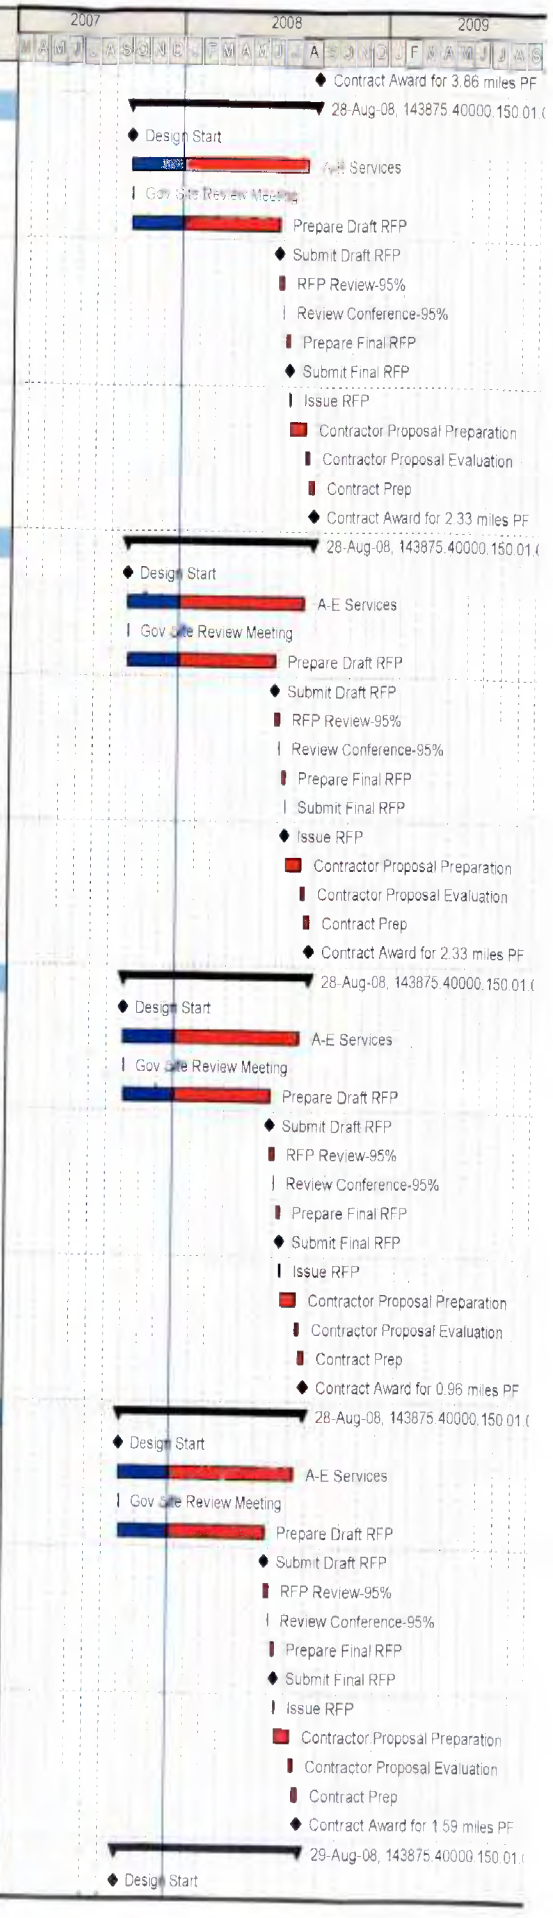

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES46965	A-E Services	DES13860	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13862	Gov Site Review Meeting	DES13860	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13864	Prepare Draft RFP	DES13862	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08
DES13866	Submit Draft RFP	DES13864	0.0d	0.0d	0%				24-Jun-08
DES13868	RFP Review-95%	DES13866	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13870	Review Conference-95%	DES13868	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13872	Prepare Final RFP	DES13870	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13874	Submit Final RFP	DES13872	0.0d	0.0d	0%				15-Jul-08
DES13876	Issue RFP	DES13874	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13878	Contractor Proposal Preparation	DES13876, DES46965	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13880	Contractor Proposal Evaluation	DES13878	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13882	Contract Prep	DES13880	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13884	Contract Award for 3.59 miles PF	DES13882	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.015 O-15 (1.93 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13886	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46963	A-E Services	DES13886	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13888	Gov Site Review Meeting	DES13886	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13890	Prepare Draft RFP	DES13888	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13892	Submit Draft RFP	DES13890	0.0d	0.0d	0%				23-Jun-08
DES13894	RFP Review-95%	DES13892	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13896	Review Conference-95%	DES13894	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13898	Prepare Final RFP	DES13896	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13900	Submit Final RFP	DES13898	0.0d	0.0d	0%				14-Jul-08
DES13902	Issue RFP	DES13900	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13904	Contractor Proposal Preparation	DES13902, DES46963	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13906	Contractor Proposal Evaluation	DES13904	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13908	Contract Prep	DES13906	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13910	Contract Award for 1.93 miles PF	DES13908	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.016 O-16 (2.45 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13914	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46961	A-E Services	DES13914	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13912	Gov Site Review Meeting	DES13914	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13916	Prepare Draft RFP	DES13912	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13930	Submit Draft RFP	DES13916	0.0d	0.0d	0%				23-Jun-08
DES13918	RFP Review-95%	DES13930	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13920	Review Conference-95%	DES13918	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13922	Prepare Final RFP	DES13920	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13924	Submit Final RFP	DES13922	0.0d	0.0d	0%				14-Jul-08
DES13926	Issue RFP	DES13924	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13932	Contractor Proposal Preparation	DES13926, DES46961	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13934	Contractor Proposal Evaluation	DES13932	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13936	Contract Prep	DES13934	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13928	Contract Award for 2.45 miles PF	DES13936	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.017 O-17 (1.63 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13940	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46959	A-E Services	DES13940	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13938	Gov Site Review Meeting	DES13940	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13942	Prepare Draft RFP	DES13938	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES13956	Submit Draft RFP	DES13942	0.0d	0.0d	0%				23-Jun-08
DES13944	RFP Review-95%	DES13956	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13946	Review Conference-95%	DES13944	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES13948	Prepare Final RFP	DES13946	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES13950	Submit Final RFP	DES13948	0.0d	0.0d	0%				14-Jul-08
DES13952	Issue RFP	DES13950	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES13958	Contractor Proposal Preparation	DES13952, DES46959	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES13960	Contractor Proposal Evaluation	DES13958	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES13962	Contract Prep	DES13960	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES13954	Contract Award for 1.63 miles PF	DES13962	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.018 O-18 (3.58 miles)			231.0d	169.0d		01-Oct-07	01-Oct-07 A		29-Aug-08
DES13966	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46957	A-E Services	DES13966	212.0d	157.0d	0%	01-Oct-07	01-Oct-07 A		13-Aug-08
DES13964	Gov Site Review Meeting	DES13966	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13968	Prepare Draft RFP	DES13964	194.0d	122.0d	0%	03-Oct-07	03-Oct-07 A		24-Jun-08

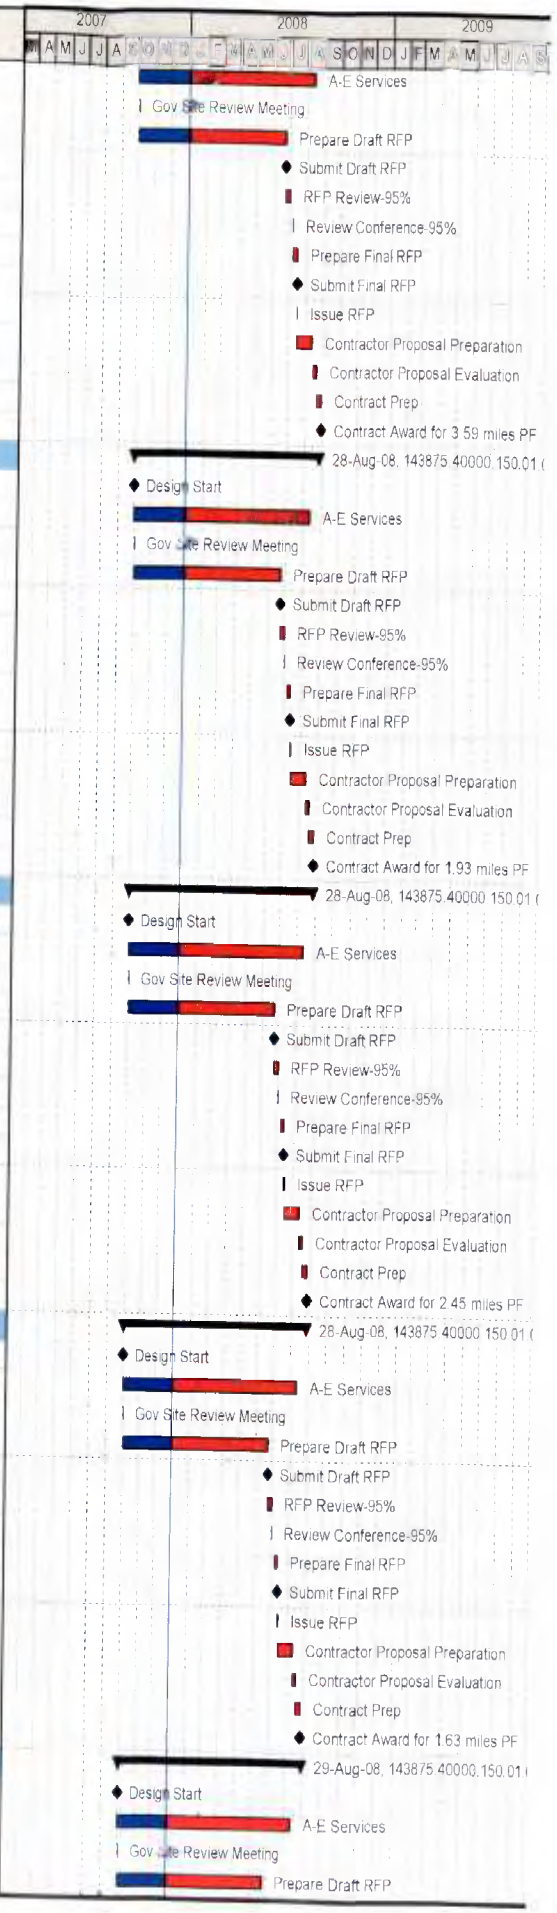

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
DES13982	Submit Draft RFP	DES13968	0.0d	0.0d	0%				24-Jun-08
DES13970	RFP Review-95%	DES13982	7.0d	7.0d	0%		25-Jun-08		03-Jul-08
DES13972	Review Conference-95%	DES13970	1.0d	1.0d	0%		07-Jul-08		07-Jul-08
DES13974	Prepare Final RFP	DES13972	6.0d	6.0d	0%		08-Jul-08		15-Jul-08
DES13976	Submit Final RFP	DES13974	0.0d	0.0d	0%				15-Jul-08
DES13978	Issue RFP	DES13976	1.0d	1.0d	0%		16-Jul-08		16-Jul-08
DES13984	Contractor Proposal Preparation	DES13978, DES46957	20.0d	20.0d	0%		17-Jul-08		13-Aug-08
DES13986	Contractor Proposal Evaluation	DES13984	5.0d	5.0d	0%		14-Aug-08		20-Aug-08
DES13988	Contract Prep	DES13986	7.0d	7.0d	0%		21-Aug-08		29-Aug-08
DES13980	Contract Award for 3.58 miles PF	DES13988	0.0d	0.0d	0%				29-Aug-08
143875.40000.150.01.08.019 O-19 (3.37 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES13992	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46955	A-E Services	DES13992	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES13990	Gov Site Review Meeting	DES13992	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES13994	Prepare Draft RFP	DES13990	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES14008	Submit Draft RFP	DES13994	0.0d	0.0d	0%				23-Jun-08
DES13996	RFP Review-95%	DES14008	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES13998	Review Conference-95%	DES13996	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES14000	Prepare Final RFP	DES13998	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES14002	Submit Final RFP	DES14000	0.0d	0.0d	0%				14-Jul-08
DES14004	Issue RFP	DES14002	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES14010	Contractor Proposal Preparation	DES14004, DES46955	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES14012	Contractor Proposal Evaluation	DES14010	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES14014	Contract Prep	DES14012	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES14006	Contract Award for 3.37 miles PF	DES14014	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.020 O-20 (0.91 miles)			230.0d	168.0d		01-Oct-07	01-Oct-07 A		28-Aug-08
DES14018	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46953	A-E Services	DES14018	212.0d	156.0d	0%	01-Oct-07	01-Oct-07 A		12-Aug-08
DES14016	Gov Site Review Meeting	DES14018	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14020	Prepare Draft RFP	DES14016	194.0d	121.0d	0%	03-Oct-07	03-Oct-07 A		23-Jun-08
DES14034	Submit Draft RFP	DES14020	0.0d	0.0d	0%				23-Jun-08
DES14022	RFP Review-95%	DES14034	7.0d	7.0d	0%		24-Jun-08		02-Jul-08
DES14024	Review Conference-95%	DES14022	1.0d	1.0d	0%		03-Jul-08		03-Jul-08
DES14026	Prepare Final RFP	DES14024	6.0d	6.0d	0%		07-Jul-08		14-Jul-08
DES14028	Submit Final RFP	DES14026	0.0d	0.0d	0%				14-Jul-08
DES14030	Issue RFP	DES14028	1.0d	1.0d	0%		15-Jul-08		15-Jul-08
DES14036	Contractor Proposal Preparation	DES14030, DES46953	20.0d	20.0d	0%		16-Jul-08		12-Aug-08
DES14038	Contractor Proposal Evaluation	DES14036	5.0d	5.0d	0%		13-Aug-08		19-Aug-08
DES14040	Contract Prep	DES14038	7.0d	7.0d	0%		20-Aug-08		28-Aug-08
DES14032	Contract Award for 0.91 miles PF	DES14040	0.0d	0.0d	0%				28-Aug-08
143875.40000.150.01.08.021 O-21 (12.98 miles)			235.0d	173.0d		01-Oct-07	01-Oct-07 A		05-Sep-08
DES14044	Design Start		0.0d	0.0d	100%	01-Oct-07	01-Oct-07 A		
DES46951	A-E Services	DES14044	212.0d	161.0d	0%	01-Oct-07	01-Oct-07 A		19-Aug-08
DES14042	Gov Site Review Meeting	DES14044	2.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	02-Oct-07	02-Oct-07 A
DES14046	Prepare Draft RFP	DES14042	194.0d	126.0d	0%	03-Oct-07	03-Oct-07 A		30-Jun-08
DES14060	Submit Draft RFP	DES14046	0.0d	0.0d	0%				30-Jun-08
DES14048	RFP Review-95%	DES14060	7.0d	7.0d	0%		01-Jul-08		10-Jul-08
DES14050	Review Conference-95%	DES14048	1.0d	1.0d	0%		11-Jul-08		11-Jul-08
DES14052	Prepare Final RFP	DES14050	6.0d	6.0d	0%		14-Jul-08		21-Jul-08
DES14054	Submit Final RFP	DES14052	0.0d	0.0d	0%				21-Jul-08
DES14056	Issue RFP	DES14054	1.0d	1.0d	0%		22-Jul-08		22-Jul-08
DES14062	Contractor Proposal Preparation	DES14056, DES46951	20.0d	20.0d	0%		23-Jul-08		19-Aug-08
DES14064	Contractor Proposal Evaluation	DES14062	5.0d	5.0d	0%		20-Aug-08		26-Aug-08
DES14066	Contract Prep	DES14064	7.0d	7.0d	0%		27-Aug-08		05-Sep-08
DES14058	Contract Award for 12.98 miles PF	DES14066	0.0d	0.0d	0%				05-Sep-08
143875.40000.42000 Value Engineering/Value Mg			0.0d	0.0d					02-Jan-08
VE305	Conduct Value Engineering Study		0.0d	0.0d	0%		02-Jan-08		02-Jan-08
VE300	Travel - VE		0.0d	0.0d	0%		02-Jan-08		02-Jan-08
143875.60000 Construction Phase (CBP 1745-7000-5)			516.0d	411.0d		31-Jul-07	31-Jul-07 A		18-Aug-09
PC1000	Project Closeout	PMO1000, PMO1010, PMO1020, PMO1001, PMO1040	0.0d	0.0d	0%				18-Aug-09*
143875.60000.61000 Construction - Phase 1 & Phase 2			367.0d	252.0d		01-Sep-07	01-Sep-07 A		31-Dec-08
143875.60000.61	5 Construction Management (CBP 1745-7000-6)								

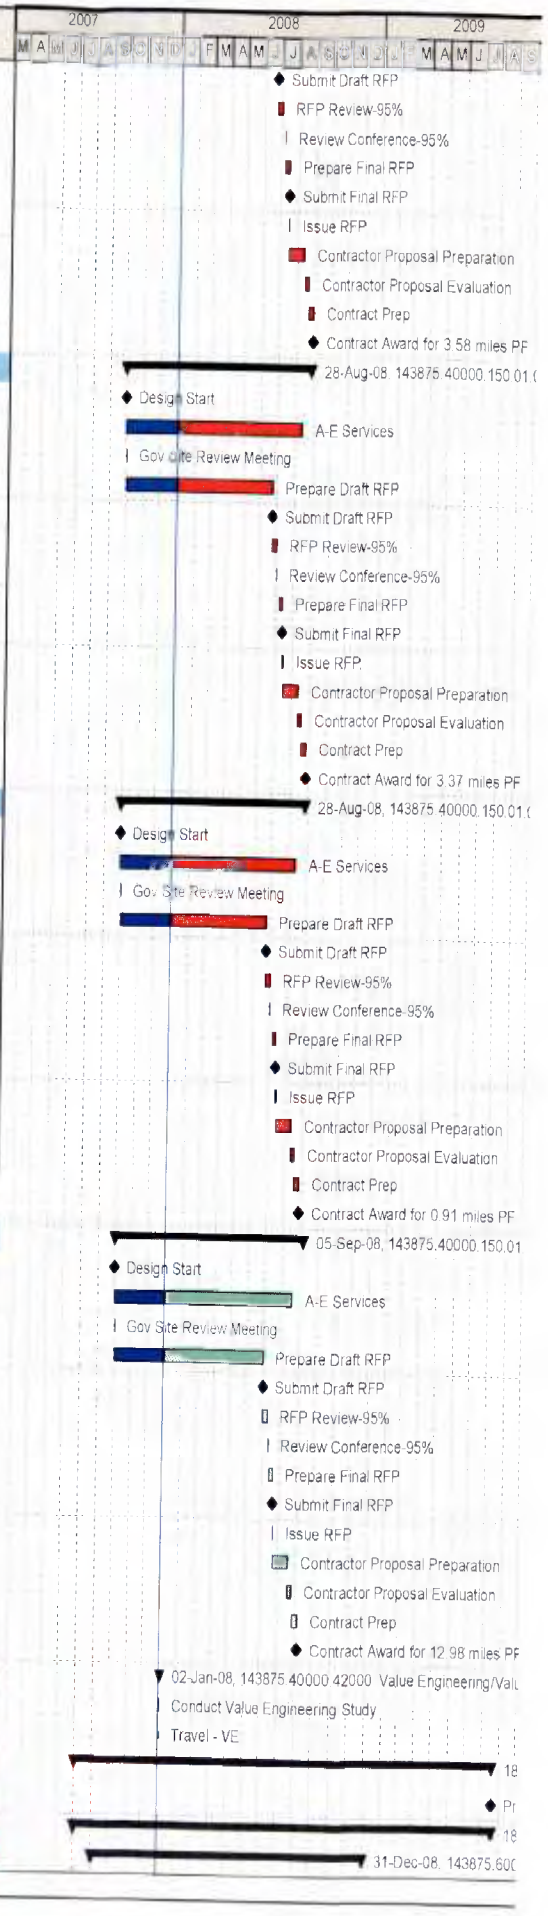

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON701	Construction Oversight - SWG		478.0d	365.0d	9%	01-Sep-07	01-Sep-07 A		31-Dec-08
CON500	Construction Management - SPL		478.0d	365.0d	8%	01-Oct-07	01-Oct-07 A		31-Dec-08
CON600	Construction Management - SWF		478.0d	365.0d	8%	01-Oct-07	01-Oct-07 A		31-Dec-08
CON700	Construction Management - SWG		478.0d	365.0d	8%	01-Oct-07	01-Oct-07 A		31-Dec-08
CON800	Construction Management Phase 1- SPA		478.0d	365.0d	8%	01-Oct-07	01-Oct-07 A		31-Dec-08
CON510	LRE CM Support to SPL		478.0d	365.0d	8%	01-Oct-07	01-Oct-07 A		31-Dec-08
CON900	Construction Management - HQ		478.0d	365.0d	58%	01-Oct-07	01-Oct-07 A		31-Dec-08
143875.60000.61000.075 Construction Phase 1 of 2 for Early CEP 1745-2080-5.2			30.0d	0.0d	100%	01-Nov-07	01-Nov-07 A	31-Nov-07	01-Nov-07 A
143875.60000.61000.075.02 TCA (21.62 miles)			453.0d	367.0d		20-Aug-07	20-Aug-07 A		11-Jun-09
143875.60000.61000.075.02.001 D-2 (2008-1) RFP#1 (3.10 Miles) SEA Ajo Station			348.0d	258.0d		20-Aug-07	20-Aug-07 A		09-Jan-09
CON1840	TCA-AJO-1-Contract Award	DES6650	269.0d	223.0d		30-Sep-07	30-Sep-07 A		18-Nov-08
CON1850	TCA-AJO-1-Contract for 3.10 miles PF	CON1840	0.0d	0.0d	100%			30-Sep-07	30-Sep-07 A
CON1860	TCA-AJO-1-Supervision & Administration	CON1840	178.0d	142.0d	0%	30-Sep-07	30-Sep-07 A		22-May-08
CON1870	TCA-AJO-1-Contingency	CON1840	178.0d	142.0d	0%	30-Sep-07	30-Sep-07 A		22-May-08
CON1880	TCA-AJO-1-Other Direct Costs	CON1840	178.0d	142.0d	0%	30-Sep-07	30-Sep-07 A		22-May-08
CON1890	TCA-AJO-1-Direct Design Costs	CON1840	178.0d	142.0d	0%	30-Sep-07	30-Sep-07 A		22-May-08
CON1851	TCA-AJO-1-Contract for 3.10 miles PF - RMS	CON1840	178.0d	142.0d	0%	30-Sep-07	30-Sep-07 A		22-May-08
CON1900	TCA-AJO-1-Design T.O. NTP	CON1840	178.0d	322.0d	0%	30-Sep-07	30-Sep-07 A		18-Nov-08
CON1910	TCA-AJO-1-Design Task Order	CON1900	0.0d	0.0d	100%	24-Oct-07	24-Oct-07 A		
CON1960	TCA-AJO-1-Submit Design for USACE Review	CON1910	71.0d	42.0d	0%	24-Oct-07	24-Oct-07 A		28-Feb-08
CON1920	TCA-AJO-1-USACE Review-SWF	CON1960	0.0d	0.0d	0%				28-Feb-08
CON1940	TCA-AJO-1-Authority for Construction Acknowledged	CON1930	10.0d	10.0d	0%		29-Feb-08		09-Mar-08
CON1930	TCA-AJO-1-Authority for Construction	CON1920, ENV16750, REO41200	0.0d	0.0d	0%		10-Mar-08		
CON1950	TCA-AJO-1-Construction Period for 3.10 miles PF	CON1940, CON1850, CON1860, CON1870, CON1880, ...	0.0d	0.0d	0%		10-Mar-08		
CON1970	TCA-AJO-1-BOD	CON1950	74.0d	74.0d	0%		10-Mar-08		22-May-08
CON1980	TCA-AJO-1-Physical Completion	CON1950	0.0d	0.0d	0%				22-May-08
CON2000	TCA-AJO-1-Construction Completion	CON1950	0.0d	0.0d	0%				22-May-08
CON2010	TCA-AJO-1-Transfer Document Date	CON1950	0.0d	0.0d	0%				22-May-08
CON2020	TCA-AJO-1-Contract Required Completion	CON1950	0.0d	0.0d	0%				22-May-08
CON2030	TCA-AJO-1-AE Evaluation Date	CON1950	0.0d	0.0d	0%				22-May-08
CON2040	TCA-AJO-1-Contractor Evaluation Date	CON1950	0.0d	0.0d	0%				22-May-08
CON1990	TCA-AJO-1-Fiscal Completion	CON1950, CON1851	0.0d	0.0d	0%				18-Nov-08
143875.60000.61000.075.02.002 D-2 (2008-2) RFP#1 (2.10 Miles) SEA Ajo Station			278.0d	246.0d		01-Nov-07	01-Nov-07 A		09-Jan-09
CON2060	TCA-AJO-2-Contract for 2.10 miles PF	CON2110	178.0d	178.0d	0%	01-Nov-07	01-Nov-07 A		13-Jul-08
CON2050	TCA-AJO-2-Contract Award	DES6650	0.0d	0.0d	0%				17-Jan-08
CON2070	TCA-AJO-2-Supervision & Administration	CON2110	178.0d	178.0d	0%		18-Jan-08		13-Jul-08
CON2080	TCA-AJO-2-Contingency	CON2110	178.0d	178.0d	0%		18-Jan-08		13-Jul-08
CON2090	TCA-AJO-2-Other Direct Costs	CON2110	178.0d	178.0d	0%		18-Jan-08		13-Jul-08
CON2100	TCA-AJO-2-Direct Design Costs	CON2110	178.0d	178.0d	0%		18-Jan-08		13-Jul-08
CON2061	TCA-AJO-2-Contract for 2.10 miles PF - RMS	CON2110	358.0d	358.0d	0%		18-Jan-08		09-Jan-09
CON2110	TCA-AJO-2-Design T.O. NTP	CON2050	0.0d	0.0d	0%		28-Jan-08		
CON2120	TCA-AJO-2-Design Task Order	CON2110	18.0d	18.0d	0%		28-Jan-08		14-Feb-08
CON2170	TCA-AJO-2-Submit Design for USACE Review	CON2120	0.0d	0.0d	0%				14-Feb-08
CON2130	TCA-AJO-2-USACE Review-SWF	CON2170	10.0d	10.0d	0%		15-Feb-08		24-Feb-08
CON2150	TCA-AJO-2-Authority for Construction Acknowledged	CON2140	0.0d	0.0d	0%		25-Feb-08		
CON2140	TCA-AJO-2-Authority for Construction	CON2130, ENV16750, REO41080	0.0d	0.0d	0%		25-Feb-08		
CON2160	TCA-AJO-2-Construction Period for 2.10 miles PF	CON2060, CON2150, CON2070, CON2080, CON2090, ...	140.0d	140.0d	0%		25-Feb-08		13-Jul-08
CON2180	TCA-AJO-2-BOD	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2190	TCA-AJO-2-Physical Completion	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2210	TCA-AJO-2-Construction Completion	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2220	TCA-AJO-2-Transfer Document Date	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2230	TCA-AJO-2-Contract Required Completion	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2240	TCA-AJO-2-AE Evaluation Date	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2250	TCA-AJO-2-Contractor Evaluation Date	CON2160	0.0d	0.0d	0%				13-Jul-08
CON2200	TCA-AJO-2-Fiscal Completion	CON2160, CON2061	0.0d	0.0d	0%				09-Jan-09
143875.60000.61000.075.02.003 D-5A (2010-1) RFP#1B (2.00 Miles) SEA Nogales Station			248.0d	218.0d		28-Sep-07	28-Sep-07 A		10-Nov-08
CON2260	TCA-NGL-1-Contract Award	DES7170	0.0d	0.0d	100%			28-Sep-07	28-Sep-07 A
CON2270	TCA-NGL-1-Contract for 2.00 miles PF	CON2260	328.0d	134.0d	0%	28-Sep-07	28-Sep-07 A		14-May-08
CON2280	TCA-NGL-1-Supervision & Administration	CON2260	328.0d	134.0d	0%	28-Sep-07	28-Sep-07 A		14-May-08
CON2290	TCA-NGL-1-Contingency	CON2260	328.0d	134.0d	0%	28-Sep-07	28-Sep-07 A		14-May-08
CON2300	TCA-NGL-1-Other Direct Costs	CON2260	328.0d	134.0d	0%	28-Sep-07	28-Sep-07 A		14-May-08
CON2310	TCA-NGL-1-Direct Design Costs	CON2260	328.0d	134.0d	0%	28-Sep-07	28-Sep-07 A		14-May-08
CON2271	TCA-NGL-1-Contract for 2.00 miles PF - RMS	CON2260	158.0d	314.0d	0%	28-Sep-07	28-Sep-07 A		10-Nov-08

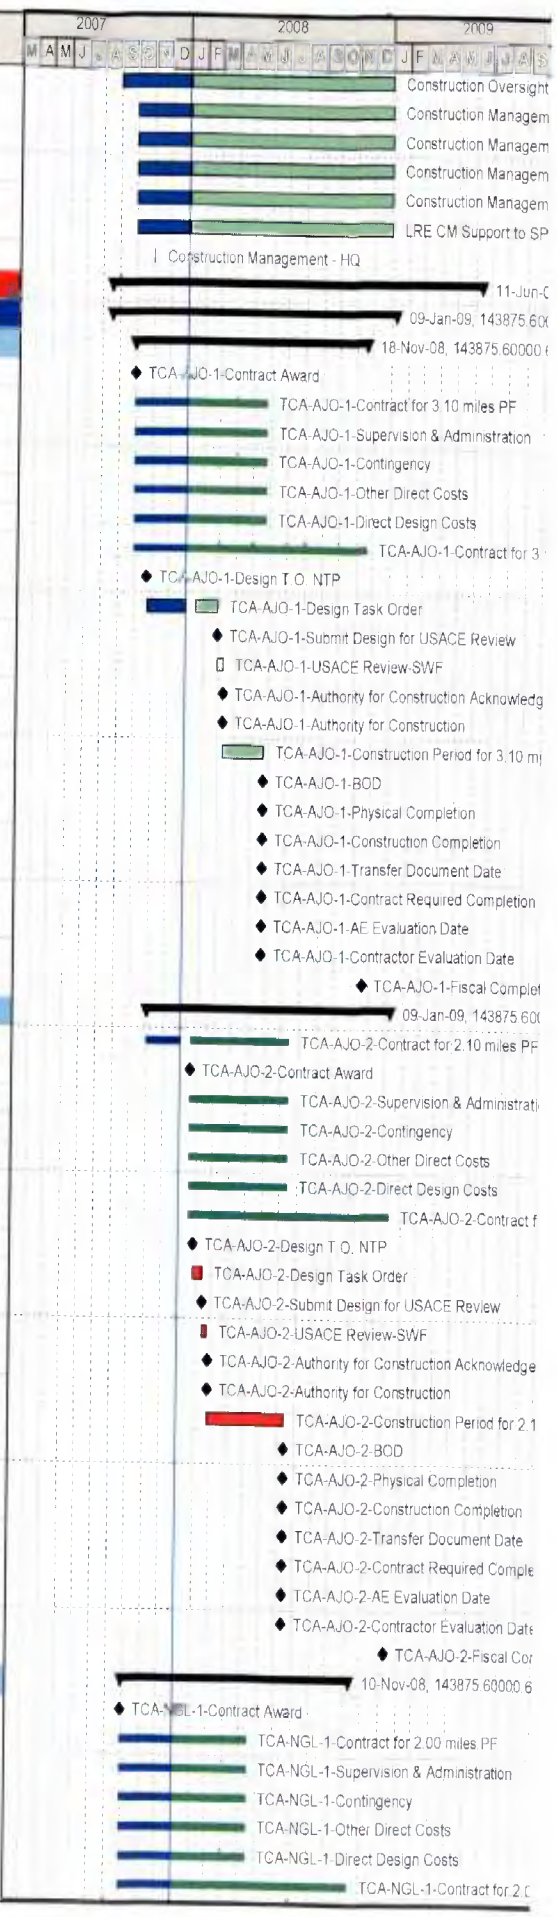

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON2320	TCA-NGL-1-Design T.O. NTP	CON2260, ENV16880	0.0d	0.0d	100%	28-Nov-07	28-Nov-07 A		
CON2330	TCA-NGL-1-Design Task Order	CON2320	28.0d	25.0d	0%	28-Nov-07	28-Nov-07 A		19-Feb-08
CON2360	TCA-NGL-1-Authority for Construction Acknowledged	CON2350	0.0d	0.0d	0%		26-Jan-08		
CON2350	TCA-NGL-1-Authority for Construction	REO17000, ENV16880	0.0d	0.0d	0%		26-Jan-08		
CON2370	TCA-NGL-1-Construction Period for 2.00 miles PF	CON2360, CON2270, CON2280, CON2290, CON2300, ...	110.0d	110.0d	0%		26-Jan-08		14-May-08
CON2380	TCA-NGL-1-Submit Design for USACE Review	CON2330	0.0d	0.0d	0%				19-Feb-08
CON2340	TCA-NGL-1-USACE Review-SWF	CON2380	10.0d	10.0d	0%		20-Feb-08		29-Feb-08
CON2390	TCA-NGL-1-BOD	CON2370	0.0d	0.0d	0%				14-May-08
CON2400	TCA-NGL-1-Physical Completion	CON2370	0.0d	0.0d	0%				14-May-08
CON2420	TCA-NGL-1-Construction Completion	CON2370	0.0d	0.0d	0%				14-May-08
CON2430	TCA-NGL-1-Transfer Document Date	CON2370	0.0d	0.0d	0%				14-May-08
CON2440	TCA-NGL-1-Contract Required Completion	CON2370	0.0d	0.0d	0%				14-May-08
CON2450	TCA-NGL-1-AE Evaluation Date	CON2370	0.0d	0.0d	0%				14-May-08
CON2460	TCA-NGL-1-Contractor Evaluation Date	CON2370	0.0d	0.0d	0%				14-May-08
CON2410	TCA-NGL-1-Fiscal Completion	CON2370, CON2271	0.0d	0.0d	0%				10-Nov-08
143875.60000.61000.075.02.004 W912BV-07-D-2024CQ01 - Naco E-2B Primary Fe			270.0d	180.0d		20-Aug-07	20-Aug-07 A		16-Sep-08
CON2560	TCA-NCO-1b-Authority for Construction	CON2550, ENV13990, REO20000	0.0d	0.0d	100%	20-Aug-07	20-Aug-07 A		
CON2480	TCA-NCO-1b-Contract for 6.90 miles PF	CON2530	50.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2490	TCA-NCO-1b-Supervision & Administration	CON2530	50.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2500	TCA-NCO-1b-Contingency	CON2530	50.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2510	TCA-NCO-1b-Other Direct Costs	CON2530	50.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2520	TCA-NCO-1b-Direct Design Costs	CON2530	50.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2481	TCA-NCO-1b-Contract for 6.90 miles PF - RMS	CON2530	50.0d	259.0d	96.4%	20-Aug-07	20-Aug-07 A		16-Sep-08*
CON2470	TCA-NCO-1b-Contract Award	DES7040	0.0d	0.0d	100%			20-Aug-07	20-Aug-07 A
CON2570	TCA-NCO-1b-Authority for Construction Acknowledged	CON2560	0.0d	0.0d	100%	21-Aug-07	21-Aug-07 A		
CON2580	TCA-NCO-1b-Construction Period for 6.90 miles PF	CON2570, CON2480, CON2490, CON2500, CON2510, ...	84.0d	0.0d	100%	24-Aug-07	24-Aug-07 A	21-Nov-07	21-Nov-07 A
CON2530	TCA-NCO-1b-Design T.O. NTP	CON2470	0.0d	0.0d	100%	30-Aug-07	30-Aug-07 A		
CON2540	TCA-NCO-1b-Design Task Order	CON2530	10.0d	7.0d	100%	30-Aug-07	30-Aug-07 A		08-Jan-08
CON2600	TCA-NCO-1b-BOD	CON2580	0.0d	0.0d	0%			21-Nov-07	21-Nov-07 A
CON2630	TCA-NCO-1b-Construction Completion	CON2580	0.0d	0.0d	0%			21-Nov-07	21-Nov-07 A
CON2610	TCA-NCO-1b-Physical Completion	CON2580	0.0d	0.0d	0%				02-Jan-08*
CON2640	TCA-NCO-1b-Transfer Document Date	CON2580	0.0d	0.0d	0%				02-Jan-08*
CON2590	TCA-NCO-1b-Submit Design for USACE Review	CON2540	0.0d	0.0d	0%				08-Jan-08
CON2550	TCA-NCO-1b-USACE Review-SWF	CON2590	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
CON2660	TCA-NCO-1b-AE Evaluation Date	CON2580	0.0d	0.0d	0%				20-Mar-08*
CON2670	TCA-NCO-1b-Contractor Evaluation Date	CON2580	0.0d	0.0d	0%				20-Mar-08*
CON2620	TCA-NCO-1b-Fiscal Completion	CON2580, CON2481	0.0d	0.0d	0%				16-Sep-08*
CON2650	TCA-NCO-1b-Contract Required Completion	CON2580	0.0d	0.0d	100%			21-Nov-07	21-Nov-07 A
143875.60000.61000.075.02.005 E-2a (2011-3) RFP#?? (6.33 miles) SEA Naco Station			142.0d	142.0d			02-Jan-08		23-Jul-08
CON2810	TCA-NCO-1a-BOD	CON2790	0.0d	0.0d	0%				02-Jan-08*
CON2820	TCA-NCO-1a-Physical Completion	CON2790	0.0d	0.0d	0%				02-Jan-08*
CON2840	TCA-NCO-1a-Construction Completion	CON2790	0.0d	0.0d	0%				02-Jan-08*
CON2850	TCA-NCO-1a-Transfer Document Date	CON2790	0.0d	0.0d	0%				02-Jan-08*
CON2860	TCA-NCO-1a-Contract Required Completion	CON2790	0.0d	0.0d	0%				02-Jan-08*
CON2680	TCA-NCO-1a-Contract Award	DES6780	0.0d	0.0d	0%				18-Jan-08
CON2690	TCA-NCO-1a-Contract for 6.33 miles PF	CON2740	181.0d	181.0d	0%		19-Jan-08		17-Jul-08
CON2700	TCA-NCO-1a-Supervision & Administration	CON2740	181.0d	181.0d	0%		19-Jan-08		17-Jul-08
CON2710	TCA-NCO-1a-Contingency	CON2740	181.0d	181.0d	0%		19-Jan-08		17-Jul-08
CON2720	TCA-NCO-1a-Other Direct Costs	CON2740	181.0d	181.0d	0%		19-Jan-08		17-Jul-08
CON2730	TCA-NCO-1a-Direct Design Costs	CON2740	181.0d	181.0d	0%		19-Jan-08		17-Jul-08
CON2691	TCA-NCO-1a-Contract for 6.33 miles PF - RMS	CON2740	187.0d	187.0d	0%		19-Jan-08		23-Jul-08*
CON2870	TCA-NCO-1a-AE Evaluation Date	CON2790	0.0d	0.0d	0%				25-Jan-08*
CON2880	TCA-NCO-1a-Contractor Evaluation Date	CON2790	0.0d	0.0d	0%				25-Jan-08*
CON2740	TCA-NCO-1a-Design T.O. NTP	CON2680	0.0d	0.0d	0%		29-Jan-08		
CON2750	TCA-NCO-1a-Design Task Order	CON2740	31.0d	31.0d	0%		29-Jan-08		28-Feb-08
CON2800	TCA-NCO-1a-Submit Design for USACE Review	CON2750	0.0d	0.0d	0%				28-Feb-08
CON2760	TCA-NCO-1a-USACE Review-SWF	CON2800	10.0d	10.0d	0%		29-Feb-08		09-Mar-08
CON2780	TCA-NCO-1a-Authority for Construction Acknowledged	CON2770	0.0d	0.0d	0%		10-Mar-08		
CON2770	TCA-NCO-1a-Authority for Construction	CON2760, ENV13990, REO30000	0.0d	0.0d	0%		10-Mar-08		
CON2790	TCA-NCO-1a-Construction Period for 6.33 miles PF	CON2690, CON2780, CON2700, CON2710, CON2720, ...	130.0d	130.0d	0%		10-Mar-08		17-Jul-08
CON2830	TCA-NCO-1a-Fiscal Completion	CON2790, CON2691	0.0d	0.0d	0%				23-Jul-08*
143875.60000.61000.075.02.006 E-3 (2011-2) RFP#3 (9.30 Miles) SEA Naco Station			246.0d	207.0d		29-Sep-07	29-Sep-07 A		26-Oct-08
CON2890	TCA-NCO-2-Contract Award	DES13360	0.0d	0.0d	100%			29-Sep-07	29-Sep-07 A

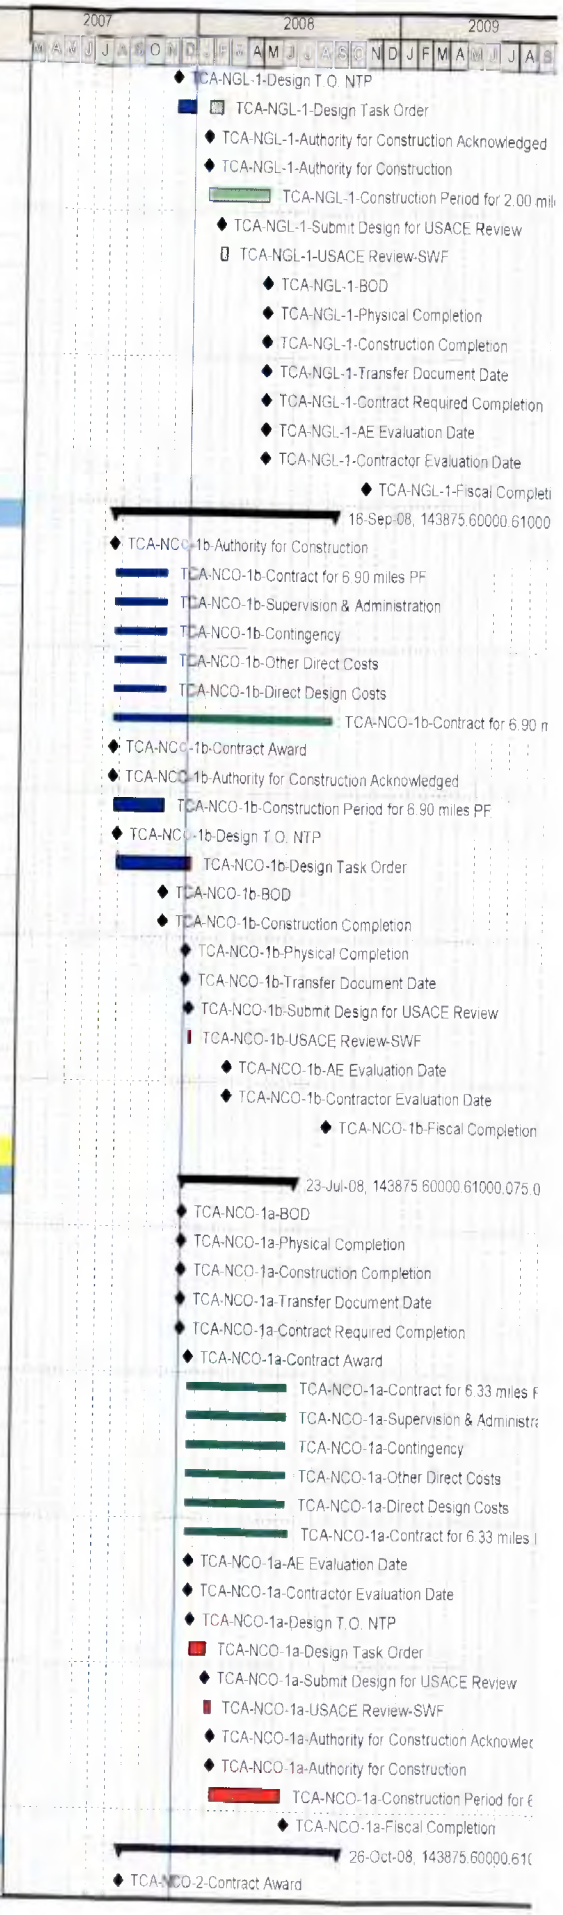

PF-225

PF225

04-Jan-08 11:(
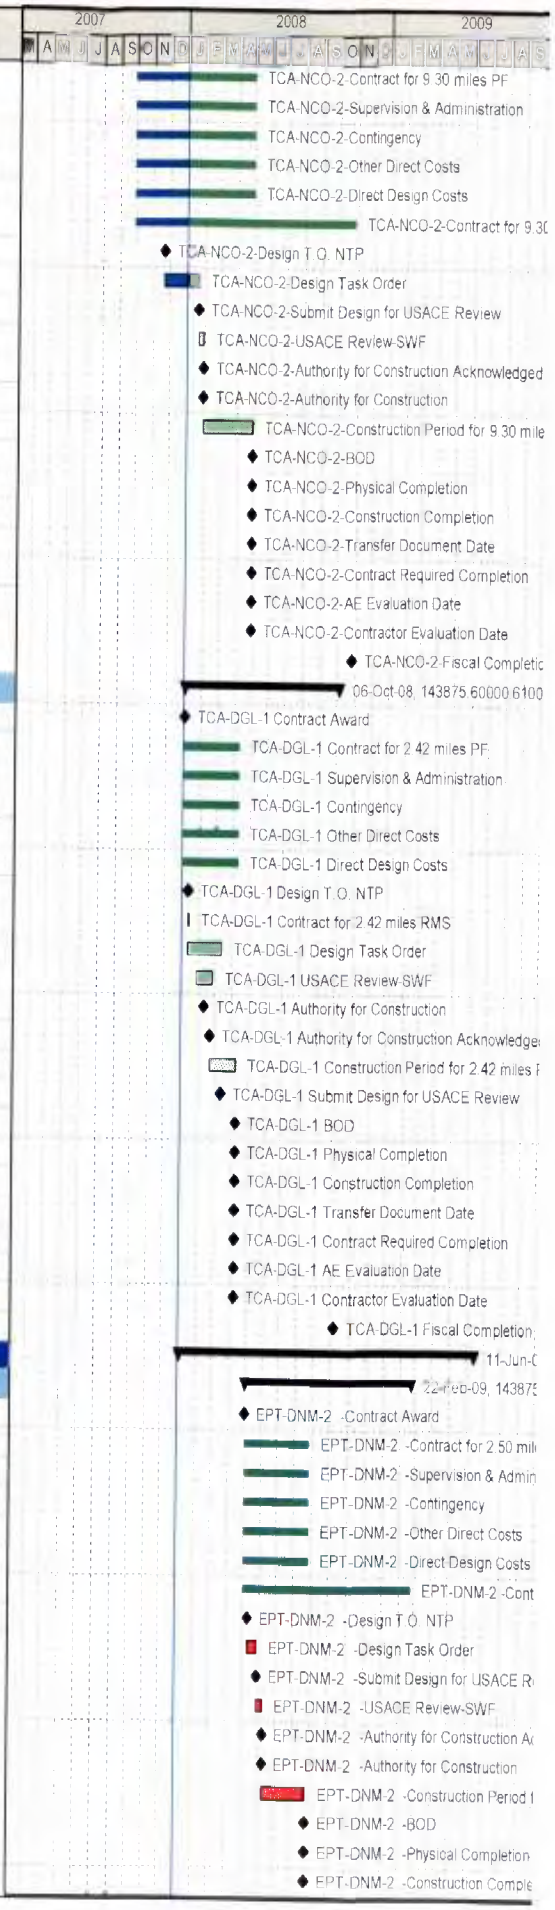
Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON2900	TCA-NCO-2-Contract for 9.30 miles PF	CON2890	128.0d	118.0d	0%	29-Sep-07	29-Sep-07 A		29-Apr-08
CON2910	TCA-NCO-2-Supervision & Administration	CON2890	128.0d	118.0d	0%	29-Sep-07	29-Sep-07 A		29-Apr-08
CON2920	TCA-NCO-2-Contingency	CON2890	128.0d	118.0d	0%	29-Sep-07	29-Sep-07 A		29-Apr-08
CON2930	TCA-NCO-2-Other Direct Costs	CON2890	128.0d	118.0d	0%	29-Sep-07	29-Sep-07 A		29-Apr-08
CON2940	TCA-NCO-2-Direct Design Costs	CON2890	128.0d	118.0d	0%	29-Sep-07	29-Sep-07 A		29-Apr-08
CON2901	TCA-NCO-2-Contract for 9.30 miles PF - RMS	CON2890	128.0d	298.0d	0%	29-Sep-07	29-Sep-07 A		26-Oct-08
CON2950	TCA-NCO-2-Design T.O. NTP	CON2890	0.0d	0.0d	100%	21-Nov-07	21-Nov-07 A		
CON2960	TCA-NCO-2-Design Task Order	CON2950	18.0d	18.0d	0%	21-Nov-07	21-Nov-07 A		20-Jan-08
CON3010	TCA-NCO-2-Submit Design for USACE Review	CON2960	0.0d	0.0d	0%				20-Jan-08
CON2970	TCA-NCO-2-USACE Review-SWF	CON3010	10.0d	10.0d	0%		20-Jan-08		30-Jan-08
CON2990	TCA-NCO-2-Authority for Construction Acknowledged	CON2980	0.0d	0.0d	0%		30-Jan-08		
CON2980	TCA-NCO-2-Authority for Construction	CON2970, ENV13630, REO40000	0.0d	0.0d	0%		30-Jan-08		
CON3000	TCA-NCO-2-Construction Period for 9.30 miles PF	CON2990, CON2900, CON2910, CON2920, CON2930, ...	90.0d	90.0d	0%		30-Jan-08		29-Apr-08
CON3020	TCA-NCO-2-BOD	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3030	TCA-NCO-2-Physical Completion	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3050	TCA-NCO-2-Construction Completion	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3060	TCA-NCO-2-Transfer Document Date	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3070	TCA-NCO-2-Contract Required Completion	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3080	TCA-NCO-2-AE Evaluation Date	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3090	TCA-NCO-2-Contractor Evaluation Date	CON3000	0.0d	0.0d	0%				29-Apr-08
CON3040	TCA-NCO-2-Fiscal Completion	CON3000, CON2901	0.0d	0.0d	0%				26-Oct-08
143875.60000.61000.075.02.007	**F-1 (2012-1) RFP#4 (2.42 Miles) SEA Douglas Station**		193.0d	193.0d			02-Jan-08		06-Oct-08
CON9400	TCA-DGL-1 Contract Award	DES13360	0.0d	0.0d	0%				02-Jan-08
CON9410	TCA-DGL-1 Contract for 2.42 miles PF	CON9460	98.0d	98.0d	0%		02-Jan-08		09-Apr-08
CON9420	TCA-DGL-1 Supervision & Administration	CON9460	98.0d	98.0d	0%		02-Jan-08		09-Apr-08
CON9430	TCA-DGL-1 Contingency	CON9460	98.0d	98.0d	0%		02-Jan-08		09-Apr-08
CON9440	TCA-DGL-1 Other Direct Costs	CON9460	98.0d	98.0d	0%		02-Jan-08		09-Apr-08
CON9450	TCA-DGL-1 Direct Design Costs	CON9460	98.0d	98.0d	0%		02-Jan-08		09-Apr-08
CON9460	TCA-DGL-1 Design T.O. NTP	CON9400	0.0d	0.0d	0%		12-Jan-08		
CON9415	TCA-DGL-1 Contract for 2.42 miles RMS	CON9460	1.0d	1.0d	0%		12-Jan-08		13-Jan-08
CON9470	TCA-DGL-1 Design Task Order	CON9460	60.0d	60.0d	0%		12-Jan-08		12-Mar-08
CON9480	TCA-DGL-1 USACE Review-SWF	CON9470	30.0d	30.0d	0%		27-Jan-08		26-Feb-08
CON9490	TCA-DGL-1 Authority for Construction	CON9480	0.0d	0.0d	0%		11-Feb-08		
CON9500	TCA-DGL-1 Authority for Construction Acknowledged	CON9490	0.0d	0.0d	0%		21-Feb-08		
CON9510	TCA-DGL-1 Construction Period for 2.42 miles PF	CON9410, CON9480, CON9500, CON9420, CON9430, ...	48.0d	48.0d	0%		21-Feb-08		09-Apr-08
CON9520	TCA-DGL-1 Submit Design for USACE Review	CON9470	0.0d	0.0d	0%				12-Mar-08
CON9530	TCA-DGL-1 BOD	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9540	TCA-DGL-1 Physical Completion	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9560	TCA-DGL-1 Construction Completion	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9570	TCA-DGL-1 Transfer Document Date	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9580	TCA-DGL-1 Contract Required Completion	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9590	TCA-DGL-1 AE Evaluation Date	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9600	TCA-DGL-1 Contractor Evaluation Date	CON9510	0.0d	0.0d	0%				09-Apr-08
CON9550	TCA-DGL-1 Fiscal Completion	CON9510, CON9415	0.0d	0.0d	0%				09-Apr-08
143875.60000.61000.075.03	**EPT (9.38 miles)**		363.0d	363.0d			02-Jan-08		06-Oct-08
143875.60000.61000.075.03.001	**I-1A (2013-2) RFP#5 (2.50 Miles) SEA Deming Station**		202.0d	202.0d			30-Apr-08		11-Jun-09
CON3940	EPT-DNM-2 -Contract Award	DES5740	0.0d	0.0d	0%				22-Feb-09
CON3950	EPT-DNM-2 -Contract for 2.50 miles PF	CON4000	118.0d	118.0d	0%		01-May-08		30-Apr-08
CON3960	EPT-DNM-2 -Supervision & Administration	CON4000	118.0d	118.0d	0%		01-May-08		26-Aug-08
CON3970	EPT-DNM-2 -Contingency	CON4000	118.0d	118.0d	0%		01-May-08		26-Aug-08
CON3980	EPT-DNM-2 -Other Direct Costs	CON4000	118.0d	118.0d	0%		01-May-08		26-Aug-08
CON3990	EPT-DNM-2 -Direct Design Costs	CON4000	118.0d	118.0d	0%		01-May-08		26-Aug-08
CON3951	EPT-DNM-2 -Contract for 2.50 miles PF - RMS	CON4000	298.0d	298.0d	0%		01-May-08		26-Aug-08
CON4000	EPT-DNM-2 -Design T.O. NTP	CON3940	0.0d	0.0d	0%		01-May-08		22-Feb-09
CON4010	EPT-DNM-2 -Design Task Order	CON4000	18.0d	18.0d	0%		11-May-08		
CON4060	EPT-DNM-2 -Submit Design for USACE Review	CON4010	0.0d	0.0d	0%		11-May-08		28-May-08
CON4020	EPT-DNM-2 -USACE Review-SWF	CON4060	10.0d	10.0d	0%				28-May-08
CON4040	EPT-DNM-2 -Authority for Construction Acknowledged	CON4030	0.0d	0.0d	0%		29-May-08		07-Jun-08
CON4030	EPT-DNM-2 -Authority for Construction	CON4020, REO19000, ENV17010	0.0d	0.0d	0%		08-Jun-08		
CON4050	EPT-DNM-2 -Construction Period for 2.50 miles PF	CON3950, CON4040, CON3960, CON3970, CON3980	80.0d	80.0d	0%		08-Jun-08		
CON4070	EPT-DNM-2 -BOD	CON4050	0.0d	0.0d	0%		08-Jun-08		26-Aug-08
CON4080	EPT-DNM-2 -Physical Completion	CON4050	0.0d	0.0d	0%				26-Aug-08
CON4100	EPT-DNM-2 -Construction Completion	CON4050	0.0d	0.0d	0%				26-Aug-08
									26-Aug-08
