PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON4110	EPT-DNM-2 -Transfer Document Date	CON4050	0.0d	0.0d	0%				26-Aug-08
CON4120	EPT-DNM-2 -Contract Required Completion	CON4050	0.0d	0.0d	0%				26-Aug-08
CON4130	EPT-DNM-2 -AE Evaluation Date	CON4050	0.0d	0.0d	0%				26-Aug-08
CON4140	EPT-DNM-2 -Contractor Evaluation Date	CON4050	0.0d	0.0d	0%				26-Aug-08
CON4090	EPT-DNM-2 -Fiscal Completion	CON4050, CON3951	0.0d	0.0d	0%				22-Feb-09
143875.60000.61000.075.03.002	**J-1 (2014-1) RFP#6 (1.11 Miles) SEA Santa Theresa Station**		**174.0d**	**174.0d**			**21-Jan-08**		**25-Sep-08**
CON4150	EPT-STN-1 -Contract Award	DES6130	0.0d	0.0d	0%				21-Jan-08
CON4160	EPT-STN-1 -Contract for 1.11 miles PF	CON4210	68.0d	68.0d	0%		22-Jan-08		29-Mar-08
CON4170	EPT-STN-1 -Supervision & Administration	CON4210	68.0d	68.0d	0%		22-Jan-08		29-Mar-08
CON4180	EPT-STN-1 -Contingency	CON4210	68.0d	68.0d	0%		22-Jan-08		29-Mar-08
CON4190	EPT-STN-1 -Other Direct Costs	CON4210	68.0d	68.0d	0%		22-Jan-08		29-Mar-08
CON4200	EPT-STN-1 -Direct Design Costs	CON4210	68.0d	68.0d	0%		22-Jan-08		29-Mar-08
CON4161	EPT-STN-1 -Contract for 1.11 miles PF - RMS	CON4210	248.0d	248.0d	0%		22-Jan-08		25-Sep-08
CON4210	EPT-STN-1 -Design T.O. NTP	CON4150	0.0d	0.0d	0%		01-Feb-08		
CON4220	EPT-STN-1 -Design Task Order	CON4210	18.0d	18.0d	0%		01-Feb-08		18-Feb-08
CON4270	EPT-STN-1 -Submit Design for USACE Review	CON4220	0.0d	0.0d	0%				18-Feb-08
CON4230	EPT-STN-1 -USACE Review-SWF	CON4270	10.0d	10.0d	0%		19-Feb-08		28-Feb-08
CON4250	EPT-STN-1 -Authority for Construction Acknowledged	CON4240	0.0d	0.0d	0%		29-Feb-08		
CON4240	EPT-STN-1 -Authority for Construction	CON4230, REO21000, ENV17140	0.0d	0.0d	0%		29-Feb-08		
CON4260	EPT-STN-1 -Construction Period for 1.11 miles PF	CON4160, CON4250, CON4170, CON4180, CON4190, ...	30.0d	30.0d	0%		29-Feb-08		29-Mar-08
CON4280	EPT-STN-1 -BOD	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4290	EPT-STN-1 -Physical Completion	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4310	EPT-STN-1 -Construction Completion	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4320	EPT-STN-1 -Transfer Document Date	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4330	EPT-STN-1 -Contract Required Completion	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4340	EPT-STN-1 -AE Evaluation Date	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4350	EPT-STN-1 -Contractor Evaluation Date	CON4260	0.0d	0.0d	0%				29-Mar-08
CON4300	EPT-STN-1 -Fiscal Completion	CON4260, CON4161	0.0d	0.0d	0%				25-Sep-08
143875.60000.61000.075.03.003	**J-1 (2014-2) RFP#6 (1.11 Miles) SEA Santa Theresa Station**		**216.0d**	**216.0d**			**21-Jan-08**		**26-Nov-08**
CON4360	EPT-STN-2 -Contract Award	DES6130	0.0d	0.0d	0%				21-Jan-08
CON4370	EPT-STN-2 -Contract for 1.11 miles PF	CON4420	130.0d	130.0d	0%		22-Jan-08		30-May-08
CON4380	EPT-STN-2 -Supervision & Administration	CON4420	130.0d	130.0d	0%		22-Jan-08		30-May-08
CON4390	EPT-STN-2 -Contingency	CON4420	130.0d	130.0d	0%		22-Jan-08		30-May-08
CON4400	EPT-STN-2 -Other Direct Costs	CON4420	130.0d	130.0d	0%		22-Jan-08		30-May-08
CON4410	EPT-STN-2 -Direct Design Costs	CON4420	130.0d	130.0d	0%		22-Jan-08		30-May-08
CON4371	EPT-STN-2 -Contract for 1.11 miles PF - RMS	CON4420	310.0d	310.0d	0%		22-Jan-08		26-Nov-08
CON4420	EPT-STN-2 -Design T.O. NTP	CON4360	0.0d	0.0d	0%		01-Feb-08		
CON4430	EPT-STN-2 -Design Task Order	CON4420	60.0d	60.0d	0%		01-Feb-08		31-Mar-08
CON4480	EPT-STN-2 -Submit Design for USACE Review	CON4430	0.0d	0.0d	0%				31-Mar-08
CON4440	EPT-STN-2 -USACE Review-SWF	CON4480	30.0d	30.0d	0%		01-Apr-08		30-Apr-08
CON4460	EPT-STN-2 -Authority for Construction Acknowledged	CON4450	0.0d	0.0d	0%		01-May-08		
CON4450	EPT-STN-2 -Authority for Construction	CON4440, REO22000, ENV17140	0.0d	0.0d	0%		01-May-08		
CON4470	EPT-STN-2 -Construction Period for 1.11 miles PF	CON4370, CON4460, CON4380, CON4390, CON4400, ...	30.0d	30.0d	0%		01-May-08		30-May-08
CON4490	EPT-STN-2 -BOD	CON4470	0.0d	0.0d	0%				30-May-08
CON4500	EPT-STN-2 -Physical Completion	CON4470	0.0d	0.0d	0%				30-May-08
CON4520	EPT-STN-2 -Construction Completion	CON4470	0.0d	0.0d	0%				30-May-08
CON4530	EPT-STN-2 -Transfer Document Date	CON4470	0.0d	0.0d	0%				30-May-08
CON4540	EPT-STN-2 -Contract Required Completion	CON4470	0.0d	0.0d	0%				30-May-08
CON4550	EPT-STN-2 -AE Evaluation Date	CON4470	0.0d	0.0d	0%				30-May-08
CON4560	EPT-STN-2 -Contractor Evaluation Date	CON4470	0.0d	0.0d	0%				30-May-08
CON4510	EPT-STN-2 -Fiscal Completion	CON4470, CON4371	0.0d	0.0d	0%				26-Nov-08
143875.60000.61000.075.03.004	**J-3 (2014-3) RFP#6 (1.07 Miles) SEA Santa Theresa Station**		**222.0d**	**222.0d**			**21-Jan-08**		**06-Dec-08**
CON4570	EPT-STN-3 -Contract Award	DES6130	0.0d	0.0d	0%				21-Jan-08
CON4580	EPT-STN-3 -Contract for 1.07 miles PF	CON4630	140.0d	140.0d	0%		22-Jan-08		09-Jun-08
CON4590	EPT-STN-3 -Supervision & Administration	CON4630	140.0d	140.0d	0%		22-Jan-08		09-Jun-08
CON4600	EPT-STN-3 -Contingency	CON4630	140.0d	140.0d	0%		22-Jan-08		09-Jun-08
CON4610	EPT-STN-3 -Other Direct Costs	CON4630	140.0d	140.0d	0%		22-Jan-08		09-Jun-08
CON4620	EPT-STN-3 -Direct Design Costs	CON4630	140.0d	140.0d	0%		22-Jan-08		09-Jun-08
CON4581	EPT-STN-3 -Contract for 1.07 miles PF - RMS	CON4630	320.0d	320.0d	0%		22-Jan-08		06-Dec-08
CON4630	EPT-STN-3 -Design T.O. NTP	CON4570	0.0d	0.0d	0%		01-Feb-08		
CON4640	EPT-STN-3 -Design Task Order	CON4630	60.0d	60.0d	0%		01-Feb-08		31-Mar-08
CON4690	EPT-STN-3 -Submit Design for USACE Review	CON4640	0.0d	0.0d	0%				31-Mar-08
CON4650	EPT-STN-3 -USACE Review-SWF	CON4690	30.0d	30.0d	0%		01-Apr-08		30-Apr-08

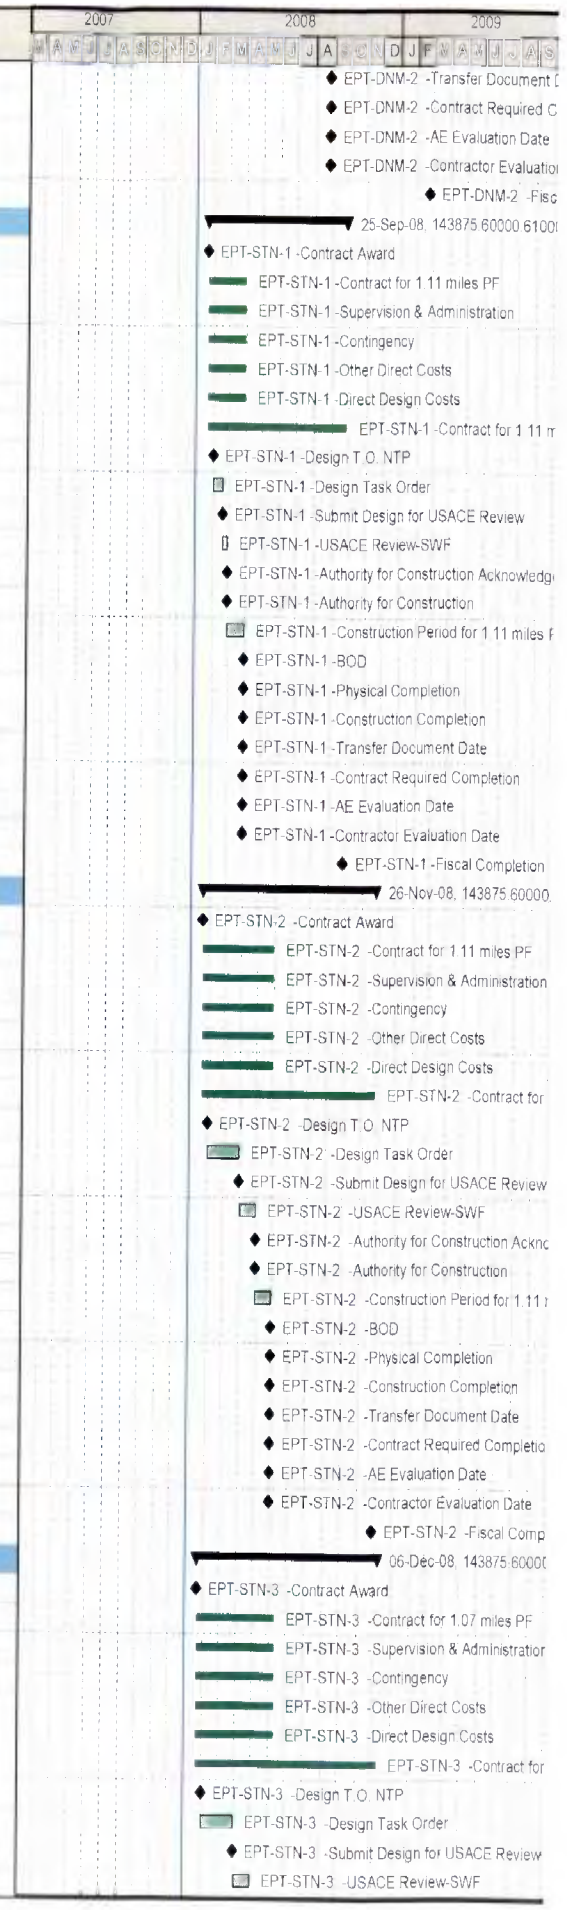

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON4670	EPT-STN-3 -Authority for Construction Acknowledged	CON4660	0.0d	0.0d	0%		01-May-08		
CON4660	EPT-STN-3 -Authority for Construction	CON4650, REO23000, ENV17140	0.0d	0.0d	0%		01-May-08		
CON4680	EPT-STN-3 -Construction Period for 1.07 miles PF	CON4580, CON4670, CON4590, CON4600, CON4610, ...	40.0d	40.0d	0%		01-May-08		
CON4700	EPT-STN-3 -BOD	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4710	EPT-STN-3 -Physical Completion	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4730	EPT-STN-3 -Construction Completion	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4740	EPT-STN-3 -Transfer Document Date	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4750	EPT-STN-3 -Contract Required Completion	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4760	EPT-STN-3 -AE Evaluation Date	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4770	EPT-STN-3 -Contractor Evaluation Date	CON4680	0.0d	0.0d	0%				09-Jun-08
CON4720	EPT-STN-3 -Fiscal Completion	CON4680, CON4581	0.0d	0.0d	0%				09-Jun-08
143875.60000.61000.075.03.005 K-1 (2015-1) RFP#7 (1.50 Miles) SEA El Paso Station			312.0d	312.0d			02-Jan-08		06-Dec-08
CON8350	EPT-EPS-1 -Contract Award	DES6000	0.0d	0.0d	0%				30-Mar-09
CON8410	EPT-EPS-1 -Design T.O. NTP	CON8350	0.0d	0.0d	0%				02-Jan-08
CON8362	EPT-EPS-1 -Contract for 1.50 miles PF - RMS	CON8350	1.0d	1.0d	0%		02-Jan-08		
CON8420	EPT-EPS-1 -Design Task Order	CON8410	28.0d	28.0d	0%		02-Jan-08		03-Jan-08
CON8360	EPT-EPS-1 -Contract for 1.50 miles PF	CON8410	274.0d	274.0d	0%		02-Jan-08		30-Jan-08
CON8370	EPT-EPS-1 -Supervision & Administration	CON8410	274.0d	274.0d	0%		02-Jan-08		01-Oct-08
CON8380	EPT-EPS-1 -Contingency	CON8410	274.0d	274.0d	0%		02-Jan-08		01-Oct-08
CON8390	EPT-EPS-1 -Other Direct Costs	CON8410	274.0d	274.0d	0%		02-Jan-08		01-Oct-08
CON8400	EPT-EPS-1 -Direct Design Costs	CON8410	274.0d	274.0d	0%		02-Jan-08		01-Oct-08
CON8470	EPT-EPS-1 -Submit Design for USACE Review	CON8420	0.0d	0.0d	0%				30-Jan-08
CON8430	EPT-EPS-1 -USACE Review-SWF	CON8470	10.0d	10.0d	0%		30-Jan-08		09-Feb-08
CON8450	EPT-EPS-1 -Authority for Construction Acknowledged	CON8440	0.0d	0.0d	0%		11-Apr-08		
CON8440	EPT-EPS-1 -Authority for Construction	CON8430, ENV19084	0.0d	0.0d	0%		11-Apr-08		
CON8460	EPT-EPS-1 -Construction Period for 1.50 miles PF	CON8430, CON8450, CON8360, CON8370, CON8380, ...	174.0d	174.0d	0%		11-Apr-08		01-Oct-08
CON8480	EPT-EPS-1 -BOD	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8490	EPT-EPS-1 -Physical Completion	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8510	EPT-EPS-1 -Construction Completion	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8520	EPT-EPS-1 -Transfer Document Date	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8530	EPT-EPS-1 -Contract Required Completion	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8540	EPT-EPS-1 -AE Evaluation Date	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8550	EPT-EPS-1 -Contractor Evaluation Date	CON8460	0.0d	0.0d	0%				01-Oct-08
CON8500	EPT-EPS-1 -Fiscal Completion	CON8460, CON8362	0.0d	0.0d	0%				30-Mar-09
143875.60000.61000.075.03.006 K-1 (2015-2) RFP#7 (0.59 Miles) SEA El Paso Station			202.0d	202.0d			02-Jan-08		18-Oct-08
CON8980	EPT-EPS-2 Contract Award	DES6000	0.0d	0.0d	0%				02-Jan-08
CON8990	EPT-EPS-2 Contract for 0.59 miles PF	CON9040	110.0d	110.0d	0%		02-Jan-08		21-Apr-08
CON9000	EPT-EPS-2 Supervision & Administration	CON9040	110.0d	110.0d	0%		02-Jan-08		21-Apr-08
CON9010	EPT-EPS-2 Contingency	CON9040	110.0d	110.0d	0%		02-Jan-08		21-Apr-08
CON9020	EPT-EPS-2 Other Direct Costs	CON9040	110.0d	110.0d	0%		02-Jan-08		21-Apr-08
CON9030	EPT-EPS-2 Direct Design Costs	CON9040	110.0d	110.0d	0%		02-Jan-08		21-Apr-08
CON8991	EPT-EPS-2 Contract for 0.59 miles PF - RMS	CON9040	290.0d	290.0d	0%		02-Jan-08		18-Oct-08
CON9040	EPT-EPS-2 Design T.O. NTP	CON8980	0.0d	0.0d	0%		12-Jan-08		
CON9050	EPT-EPS-2 Design Task Order	CON9040	60.0d	60.0d	0%		12-Jan-08		12-Mar-08
CON9060	EPT-EPS-2 USACE Review-SWF	CON9050	30.0d	30.0d	0%		27-Jan-08		26-Feb-08
CON9070	EPT-EPS-2 Authority for Construction	CON9060, ENV17270	0.0d	0.0d	0%		11-Feb-08		
CON9080	EPT-EPS-2 Authority for Construction Acknowledged	CON9070	0.0d	0.0d	0%		21-Feb-08		
CON9090	EPT-EPS-2 Construction Period for 0.59 miles PF	CON8990, CON9060, CON9080, CON9000, CON9010, ...	60.0d	60.0d	0%		21-Feb-08		21-Apr-08
CON9100	EPT-EPS-2 Submit Design for USACE Review	CON9050	0.0d	0.0d	0%				12-Mar-08
CON9110	EPT-EPS-2 BOD	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9120	EPT-EPS-2 Physical Completion	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9140	EPT-EPS-2 Construction Completion	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9150	EPT-EPS-2 Transfer Document Date	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9160	EPT-EPS-2 Contract Required Completion	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9170	EPT-EPS-2 AE Evaluation Date	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9180	EPT-EPS-2 Contractor Evaluation Date	CON9090	0.0d	0.0d	0%				21-Apr-08
CON9130	EPT-EPS-2 Fiscal Completion	CON9090, CON8991	0.0d	0.0d	0%				18-Oct-08
143875.60000.61000.075.03.007 K-1 (2015-3) RFP#7 (1.50 Miles) SEA El Paso Station			363.0d	363.0d			02-Jan-08		11-Jun-09
CON9190	EPT-EPS-3 Contract Award	DES6000	0.0d	0.0d	0%				02-Jan-08
CON9200	EPT-EPS-3 Contract for 1.50 miles PF	CON9250	346.0d	346.0d	0%		02-Jan-08		13-Dec-08
CON9210	EPT-EPS-3 Supervision & Administration	CON9250	346.0d	346.0d	0%		02-Jan-08		13-Dec-08
CON9220	EPT-EPS-3 Contingency	CON9250	346.0d	346.0d	0%		02-Jan-08		13-Dec-08
CON9230	EPT-EPS-3 Other Direct Costs	CON9250	346.0d	346.0d	0%		02-Jan-08		13-Dec-08

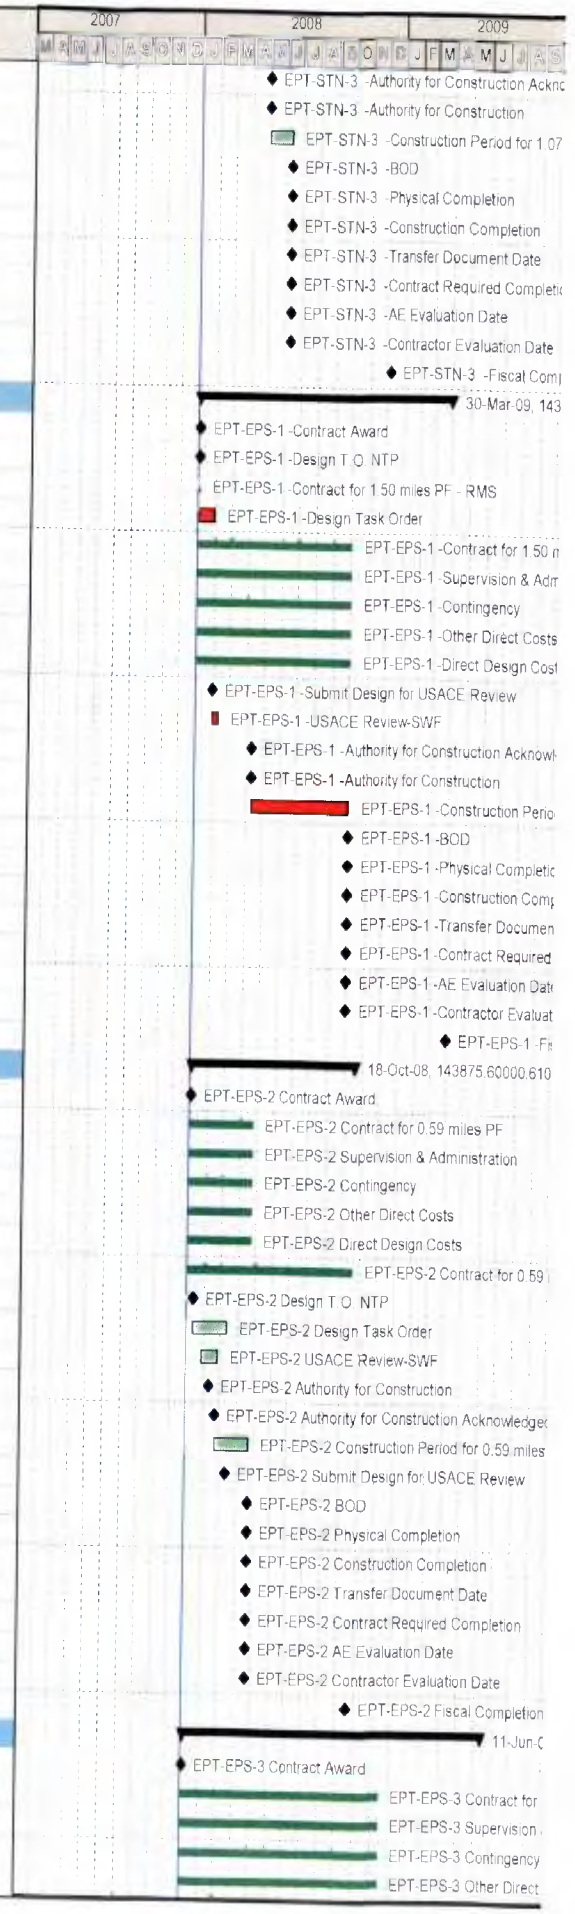

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON9240	EPT-EPS-3 Direct Design Costs	CON9250	346.0d	346.0d	0%		02-Jan-08		13-Dec-08
CON9201	EPT-EPS-3 Contract for 1.50 miles PF - RMS	CON9250	526.0d	526.0d	0%		02-Jan-08		11-Jun-09
CON9250	EPT-EPS-3 Design T.O. NTP	CON9190	0.0d	0.0d	0%		12-Jan-08		
CON9260	EPT-EPS-3 Design Task Order	CON9250	60.0d	60.0d	0%		12-Jan-08		12-Mar-08
CON9270	EPT-EPS-3 USACE Review-SWF	CON9260	30.0d	30.0d	0%		27-Jan-08		26-Feb-08
CON9280	EPT-EPS-3 Authority for Construction	CON9270, ENV17270	0.0d	0.0d	0%		11-Feb-08		
CON9290	EPT-EPS-3 Authority for Construction Acknowledged	CON9280	0.0d	0.0d	0%		21-Feb-08		
CON9300	EPT-EPS-3 Construction Period for 1.50 miles PF	CON9200, CON9270, CON9290, CON9210, CON9220,	296.0d	296.0d	0%		21-Feb-08		13-Dec-08
CON9310	EPT-EPS-3 Submit Design for USACE Review	CON9260	0.0d	0.0d	0%				12-Mar-08
CON9320	EPT-EPS-3 BOD	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9330	EPT-EPS-3 Physical Completion	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9350	EPT-EPS-3 Construction Completion	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9360	EPT-EPS-3 Transfer Document Date	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9370	EPT-EPS-3 Contract Required Completion	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9380	EPT-EPS-3 AE Evaluation Date	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9390	EPT-EPS-3 Contractor Evaluation Date	CON9300	0.0d	0.0d	0%				13-Dec-08
CON9340	EPT-EPS-3 Fiscal Completion	CON9300, CON9201	0.0d	0.0d	0%				11-Jun-09
143875.60000.61000.150	Construc[illegible] 150.2 (176.46 miles)		[illegible]	[illegible]			02-Jan-08		[illegible]
143875.60000.61000.150.01	SDC (14.01 miles)		371.0d	371.0d			14-Jan-08		06-Jul-09
143875.60000.61000.150.01.001	A-1 (2001-1) SDC-BRF-1 (3.58 miles) Pak Truck Trail		346.0d	346.0d			14-Jan-08		30-May-09
CON5410	SDC-BRF-1 -Contract Award	DES13184	0.0d	0.0d	0%				14-Jan-08
CON5470	SDC-BRF-1 -Design T.O. NTP	CON5410	0.0d	0.0d	0%		15-Jan-08		
CON5480	SDC-BRF-1 -Design Task Order	CON5470	93.0d	93.0d	0%		15-Jan-08		16-Apr-08
CON5420	SDC-BRF-1 -Contract for 3.58 miles PF	CON5410	322.0d	322.0d	0%		15-Jan-08		01-Dec-08
CON5430	SDC-BRF-1 -Supervision & Administration	CON5410	322.0d	322.0d	0%		15-Jan-08		01-Dec-08
CON5440	SDC-BRF-1 -Contingency	CON5410	322.0d	322.0d	0%		15-Jan-08		01-Dec-08
CON5450	SDC-BRF-1 -Other Direct Costs	CON5410	322.0d	322.0d	0%		15-Jan-08		01-Dec-08
CON5460	SDC-BRF-1 -Direct Design Costs	CON5410	322.0d	322.0d	0%		15-Jan-08		01-Dec-08
CON5422	SDC-BRF-1 -Contract for 3.58 miles PF - RMS	CON5410	502.0d	502.0d	0%		15-Jan-08		30-May-09
CON5510	SDC-BRF-1 -Authority for Construction Acknowledged	CON5500	0.0d	0.0d	0%		01-Feb-08		
CON5500	SDC-BRF-1 -Authority for Construction	REO40027, CON5410, ENV18826	0.0d	0.0d	0%		01-Feb-08*		
CON5520	SDC-BRF-1 -Construction Period for 3.58 miles PF	CON5510, CON5420, CON5430, CON5440, CON5450, ...	305.0d	305.0d	0%		01-Feb-08		01-Dec-08
CON5530	SDC-BRF-1 -Submit Design for USACE Review	CON5480	0.0d	0.0d	0%				16-Apr-08
CON5490	SDC-BRF-1 -USACE Review-SWF	CON5530	10.0d	10.0d	0%		17-Apr-08		26-Apr-08
CON5540	SDC-BRF-1 -BOD	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5550	SDC-BRF-1 -Physical Completion	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5570	SDC-BRF-1 -Construction Completion	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5580	SDC-BRF-1 -Transfer Document Date	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5590	SDC-BRF-1 -Contract Required Completion	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5600	SDC-BRF-1 -AE Evaluation Date	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5610	SDC-BRF-1 -Contractor Evaluation Date	CON5520	0.0d	0.0d	0%				01-Dec-08
CON5560	SDC-BRF-1 -Fiscal Completion	CON5520, CON5422	0.0d	0.0d	0%				30-May-09
143875.60000.61000.150.01.002	A-2 (2001-2) SDC-BRF-2 (0.77 miles) W of Tecate		240.0d	240.0d			21-Jul-08		06-Jul-09
CON5620	SDC-BRF-2 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON5680	SDC-BRF-2 -Design T.O. NTP	CON5620	0.0d	0.0d	0%		22-Jul-08		
CON5690	SDC-BRF-2 -Design Task Order	CON5680	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON5630	SDC-BRF-2 -Contract for 0.77 miles PF	CON5620	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON5640	SDC-BRF-2 -Supervision & Administration	CON5620	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON5650	SDC-BRF-2 -Contingency	CON5620	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON5660	SDC-BRF-2 -Other Direct Costs	CON5620	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON5670	SDC-BRF-2 -Direct Design Costs	CON5620	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON5632	SDC-BRF-2 -Contract for 0.77 miles PF - RMS	CON5620	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON5720	SDC-BRF-2 -Authority for Construction Acknowledged	CON5710	0.0d	0.0d	0%		06-Aug-08		
CON5710	SDC-BRF-2 -Authority for Construction	REO40045, CON5620, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON5730	SDC-BRF-2 -Construction Period for 0.77 miles PF	CON5720, CON5630, CON5640, CON5650, CON5660, ...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON5740	SDC-BRF-2 -Submit Design for USACE Review	CON5690	0.0d	0.0d	0%				08-Aug-08
CON5700	SDC-BRF-2 -USACE Review-SWF	CON5740	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON5750	SDC-BRF-2 -BOD	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5760	SDC-BRF-2 -Physical Completion	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5780	SDC-BRF-2 -Construction Completion	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5790	SDC-BRF-2 -Transfer Document Date	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5800	SDC-BRF-2 -Contract Required Completion	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5810	SDC-BRF-2 -AE Evaluation Date	CON5730	0.0d	0.0d	0%				07-Jan-09

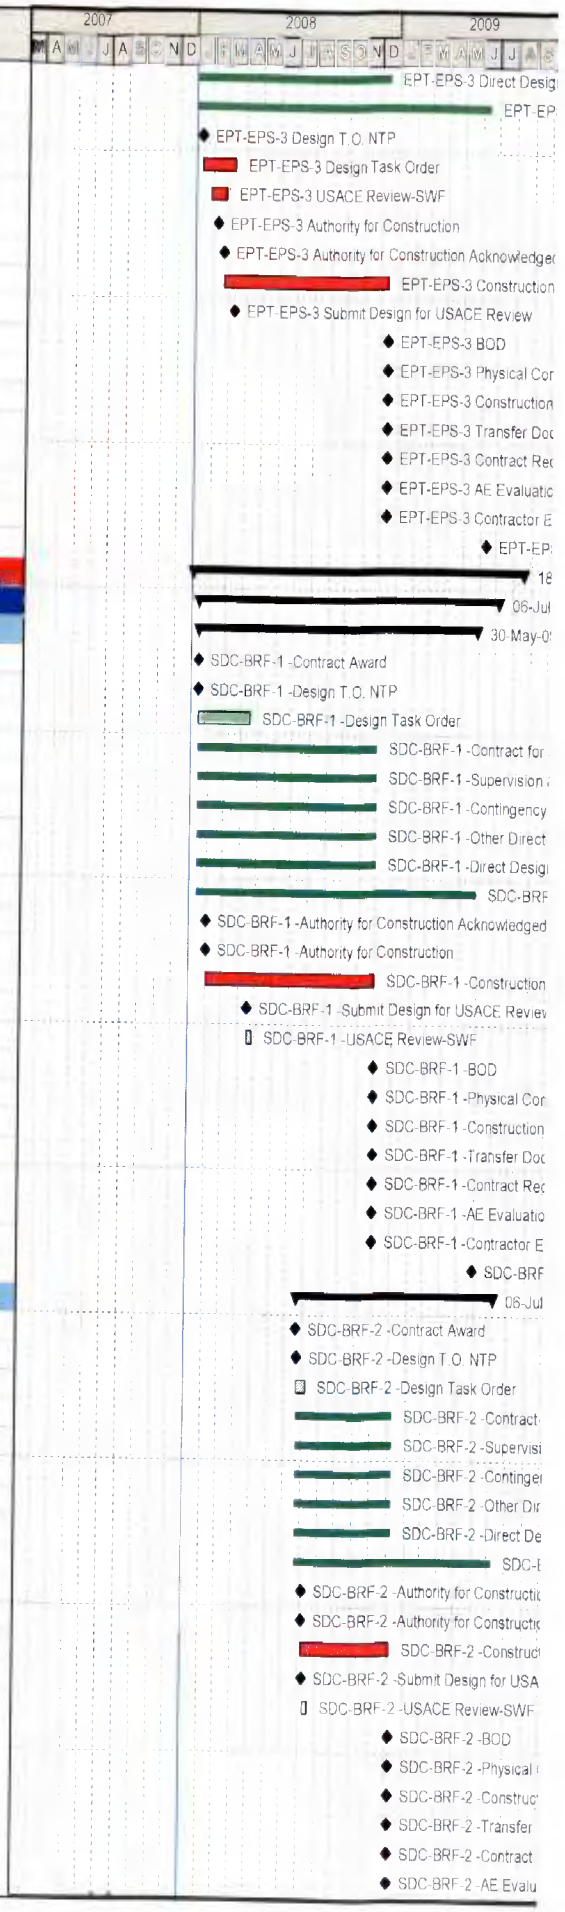

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON5820	SDC-BRF-2 -Contractor Evaluation Date	CON5730	0.0d	0.0d	0%				07-Jan-09
CON5770	SDC-BRF-2 -Fiscal Completion	CON5730, CON5632	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.003	**A-2 (2002-1) SDC-ECJ-1 (0.57 miles) Ceti's Hill**		240.0d	240.0d			21-Jul-08		06-Jul-09
CON19035	SDC-ECJ-1 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19055	SDC-ECJ-1 -Design T.O. NTP	CON19035	0.0d	0.0d	0%		22-Jul-08		
CON19060	SDC-ECJ-1 -Design Task Order	CON19055	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19040	SDC-ECJ-1 -Contract for 0.57 miles PF	CON19035	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19090	SDC-ECJ-1 -Supervision & Administration	CON19035	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19030	SDC-ECJ-1 -Contingency	CON19035	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19075	SDC-ECJ-1 -Other Direct Costs	CON19035	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19065	SDC-ECJ-1 -Direct Design Costs	CON19035	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19042	SDC-ECJ-1 -Contract for 0.57 miles PF - RMS	CON19035	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19020	SDC-ECJ-1 -Authority for Construction Acknowledged	CON19015	0.0d	0.0d	0%		06-Aug-08		
CON19015	SDC-ECJ-1 -Authority for Construction	REO40067, CON19035, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19025	SDC-ECJ-1 -Construction Period for .57 miles PF	CON19020, CON19030, CON19040, CON19065, CON19	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19085	SDC-ECJ-1 -Submit Design for USACE Review	CON19060	0.0d	0.0d	0%				08-Aug-08
CON19100	SDC-ECJ-1 -USACE Review-SWF	CON19085	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19005	SDC-ECJ-1 -BOD	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19080	SDC-ECJ-1 -Physical Completion	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19010	SDC-ECJ-1 -Construction Completion	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19095	SDC-ECJ-1 -Transfer Document Date	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19045	SDC-ECJ-1 -Contract Required Completion	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19000	SDC-ECJ-1 -AE Evaluation Date	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19050	SDC-ECJ-1 -Contractor Evaluation Date	CON19025	0.0d	0.0d	0%				07-Jan-09
CON19070	SDC-ECJ-1 -Fiscal Completion	CON19025, CON19042	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.004	**A-2 (2002-2) SDC-ECJ-2 (0.58 miles) East Brickyard to Gunsight Drainage**		240.0d	240.0d			21-Jul-08		06-Jul-09
CON19105	SDC-ECJ-2 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19110	SDC-ECJ-2 -Design T.O. NTP	CON19105	0.0d	0.0d	0%		22-Jul-08		
CON19115	SDC-ECJ-2 -Design Task Order	CON19110	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19140	SDC-ECJ-2 -Contract for 0.58 miles PF	CON19105	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19145	SDC-ECJ-2 -Supervision & Administration	CON19105	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19150	SDC-ECJ-2 -Contingency	CON19105	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19155	SDC-ECJ-2 -Other Direct Costs	CON19105	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19160	SDC-ECJ-2 -Direct Design Costs	CON19105	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19142	SDC-ECJ-2 -Contract for 0.58 miles PF - RMS	CON19105	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19130	SDC-ECJ-2 -Authority for Construction Acknowledged	CON19135	0.0d	0.0d	0%		06-Aug-08		
CON19135	SDC-ECJ-2 -Authority for Construction	REO40089, CON19105, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19165	SDC-ECJ-2 -Construction Period for .58 miles PF	CON19130, CON19140, CON19145, CON19150, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19120	SDC-ECJ-2 -Submit Design for USACE Review	CON19115	0.0d	0.0d	0%				08-Aug-08
CON19125	SDC-ECJ-2 -USACE Review-SWF	CON19120	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19170	SDC-ECJ-2 -BOD	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19175	SDC-ECJ-2 -Physical Completion	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19185	SDC-ECJ-2 -Construction Completion	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19190	SDC-ECJ-2 -Transfer Document Date	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19195	SDC-ECJ-2 -Contract Required Completion	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19200	SDC-ECJ-2 -AE Evaluation Date	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19205	SDC-ECJ-2 -Contractor Evaluation Date	CON19165	0.0d	0.0d	0%				07-Jan-09
CON19180	SDC-ECJ-2 -Fiscal Completion	CON19165, CON19142	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.005	**A-2 (2002-3) SDC-ECJ-3 (0.89 miles) W. Horseshoe Canyon**		240.0d	240.0d			21-Jul-08		06-Jul-09
CON19210	SDC-ECJ-3 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19215	SDC-ECJ-3 -Design T.O. NTP	CON19210	0.0d	0.0d	0%		22-Jul-08		
CON19220	SDC-ECJ-3 -Design Task Order	CON19215	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19245	SDC-ECJ-3 -Contract for 0.89 miles PF	CON19210	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19250	SDC-ECJ-3 -Supervision & Administration	CON19210	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19255	SDC-ECJ-3 -Contingency	CON19210	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19260	SDC-ECJ-3 -Other Direct Costs	CON19210	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19265	SDC-ECJ-3 -Direct Design Costs	CON19210	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19247	SDC-ECJ-3 -Contract for 0.89 miles PF - RMS	CON19210	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19235	SDC-ECJ-3 -Authority for Construction Acknowledged	CON19240	0.0d	0.0d	0%		06-Aug-08		
CON19240	SDC-ECJ-3 -Authority for Construction	REO40111, CON19210, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19270	SDC-ECJ-3 -Construction Period for .89 miles PF	CON19235, CON19245, CON19250, CON19255, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19225	SDC-ECJ-3 -Submit Design for USACE Review	CON19220	0.0d	0.0d	0%				08-Aug-08
CON19230	SDC-ECJ-3 -USACE Review-SWF	CON19225	10.0d	10.0d	0%		09-Aug-08		18-Aug-08

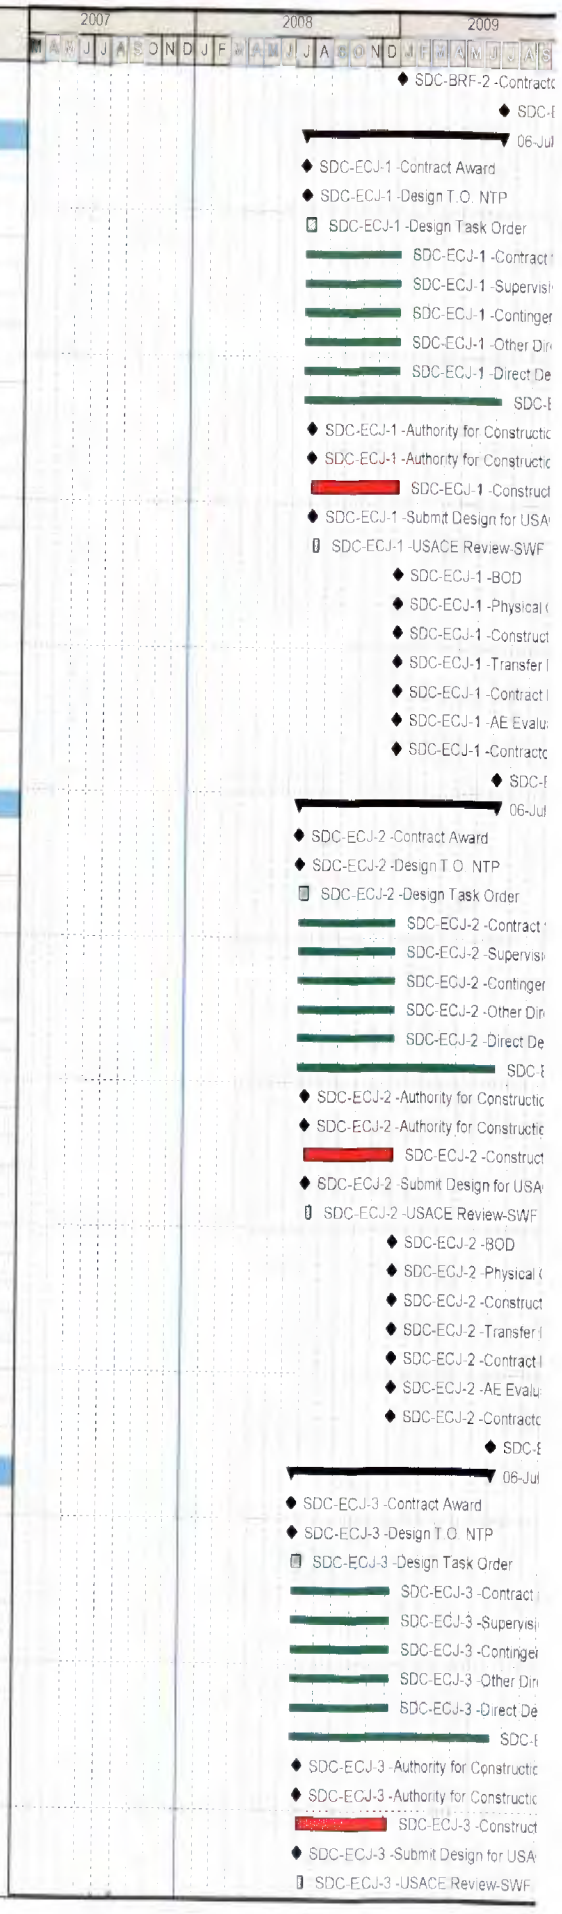

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON19275	SDC-ECJ-3 -BOD	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19280	SDC-ECJ-3 -Physical Completion	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19290	SDC-ECJ-3 -Construction Completion	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19295	SDC-ECJ-3 -Transfer Document Date	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19300	SDC-ECJ-3 -Contract Required Completion	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19305	SDC-ECJ-3 -AE Evaluation Date	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19310	SDC-ECJ-3 -Contractor Evaluation Date	CON19270	0.0d	0.0d	0%				07-Jan-09
CON19285	SDC-ECJ-3 -Fiscal Completion	CON19270, CON19247	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.006	**A-2 (2002-4) SDC-ECJ-4 (0.12 miles) East Bell Valley**		**240.0d**	**240.0d**			**21-Jul-08**		**06-Jul-09**
CON19315	SDC-ECJ-4 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19320	SDC-ECJ-4 -Design T.O. NTP	CON19315	0.0d	0.0d	0%		22-Jul-08		
CON19325	SDC-ECJ-4 -Design Task Order	CON19320	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19350	SDC-ECJ-4 -Contract for 0.12 miles PF	CON19315	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19355	SDC-ECJ-4 -Supervision & Administration	CON19315	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19360	SDC-ECJ-4 -Contingency	CON19315	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19365	SDC-ECJ-4 -Other Direct Costs	CON19315	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19370	SDC-ECJ-4 -Direct Design Costs	CON19315	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19249	SDC-ECJ-4 -Contract for 0.12 miles PF - RMS	CON19315	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19340	SDC-ECJ-4 -Authority for Construction Acknowledged	CON19345	0.0d	0.0d	0%		06-Aug-08		
CON19345	SDC-ECJ-4 -Authority for Construction	REO40133, CON19315, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19375	SDC-ECJ-4 -Construction Period for .12 miles PF	CON19340, CON19350, CON19355, CON19360, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19330	SDC-ECJ-4 -Submit Design for USACE Review	CON19325	0.0d	0.0d	0%				08-Aug-08
CON19335	SDC-ECJ-4 -USACE Review-SWF	CON19330	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19380	SDC-ECJ-4 -BOD	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19385	SDC-ECJ-4 -Physical Completion	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19395	SDC-ECJ-4 -Construction Completion	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19400	SDC-ECJ-4 -Transfer Document Date	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19405	SDC-ECJ-4 -Contract Required Completion	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19410	SDC-ECJ-4 -AE Evaluation Date	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19415	SDC-ECJ-4 -Contractor Evaluation Date	CON19375	0.0d	0.0d	0%				07-Jan-09
CON19390	SDC-ECJ-4 -Fiscal Completion	CON19375, CON19249	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.007	**A-2 (2002-5) SDC-ECJ-5 (1.02 miles) Ag Loop**		**240.0d**	**240.0d**			**21-Jul-08**		**06-Jul-09**
CON19420	SDC-ECJ-5 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19425	SDC-ECJ-5 -Design T.O. NTP	CON19420	0.0d	0.0d	0%		22-Jul-08		
CON19430	SDC-ECJ-5 -Design Task Order	CON19425	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19455	SDC-ECJ-5 -Contract for 1.02 miles PF	CON19420	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19460	SDC-ECJ-5 -Supervision & Administration	CON19420	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19465	SDC-ECJ-5 -Contingency	CON19420	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19470	SDC-ECJ-5 -Other Direct Costs	CON19420	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19475	SDC-ECJ-5 -Direct Design Costs	CON19420	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19457	SDC-ECJ-5 -Contract for 1.02 miles PF - RMS	CON19420	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19445	SDC-ECJ-5 -Authority for Construction Acknowledged	CON19450	0.0d	0.0d	0%		06-Aug-08		
CON19450	SDC-ECJ-5 -Authority for Construction	REO40155, CON19420, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19480	SDC-ECJ-5 -Construction Period for 1.02 miles PF	CON19445, CON19455, CON19460, CON19465, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19435	SDC-ECJ-5 -Submit Design for USACE Review	CON19430	0.0d	0.0d	0%				08-Aug-08
CON19440	SDC-ECJ-5 -USACE Review-SWF	CON19435	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19485	SDC-ECJ-5 -BOD	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19490	SDC-ECJ-5 -Physical Completion	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19500	SDC-ECJ-5 -Construction Completion	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19505	SDC-ECJ-5 -Transfer Document Date	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19510	SDC-ECJ-5 -Contract Required Completion	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19515	SDC-ECJ-5 -AE Evaluation Date	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19520	SDC-ECJ-5 -Contractor Evaluation Date	CON19480	0.0d	0.0d	0%				07-Jan-09
CON19495	SDC-ECJ-5 -Fiscal Completion	CON19480, CON19457	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.008	**A-2 (2003-1) SDC-CAO-1 (0.17 miles) Southwest Rim of Smith Canyon**		**240.0d**	**240.0d**			**21-Jul-08**		**06-Jul-09**
CON19525	SDC-CAO-1 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19530	SDC-CAO-1 -Design T.O. NTP	CON19525	0.0d	0.0d	0%		22-Jul-08		
CON19535	SDC-CAO-1 -Design Task Order	CON19530	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19560	SDC-CAO-1 -Contract for 0.17 miles PF	CON19525	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19565	SDC-CAO-1 -Supervision & Administration	CON19525	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19570	SDC-CAO-1 -Contingency	CON19525	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19575	SDC-CAO-1 -Other Direct Costs	CON19525	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19580	SDC-CAO-1 -Direct Design Costs	CON19525	170.0d	170.0d	0%		22-Jul-08		07-Jan-09

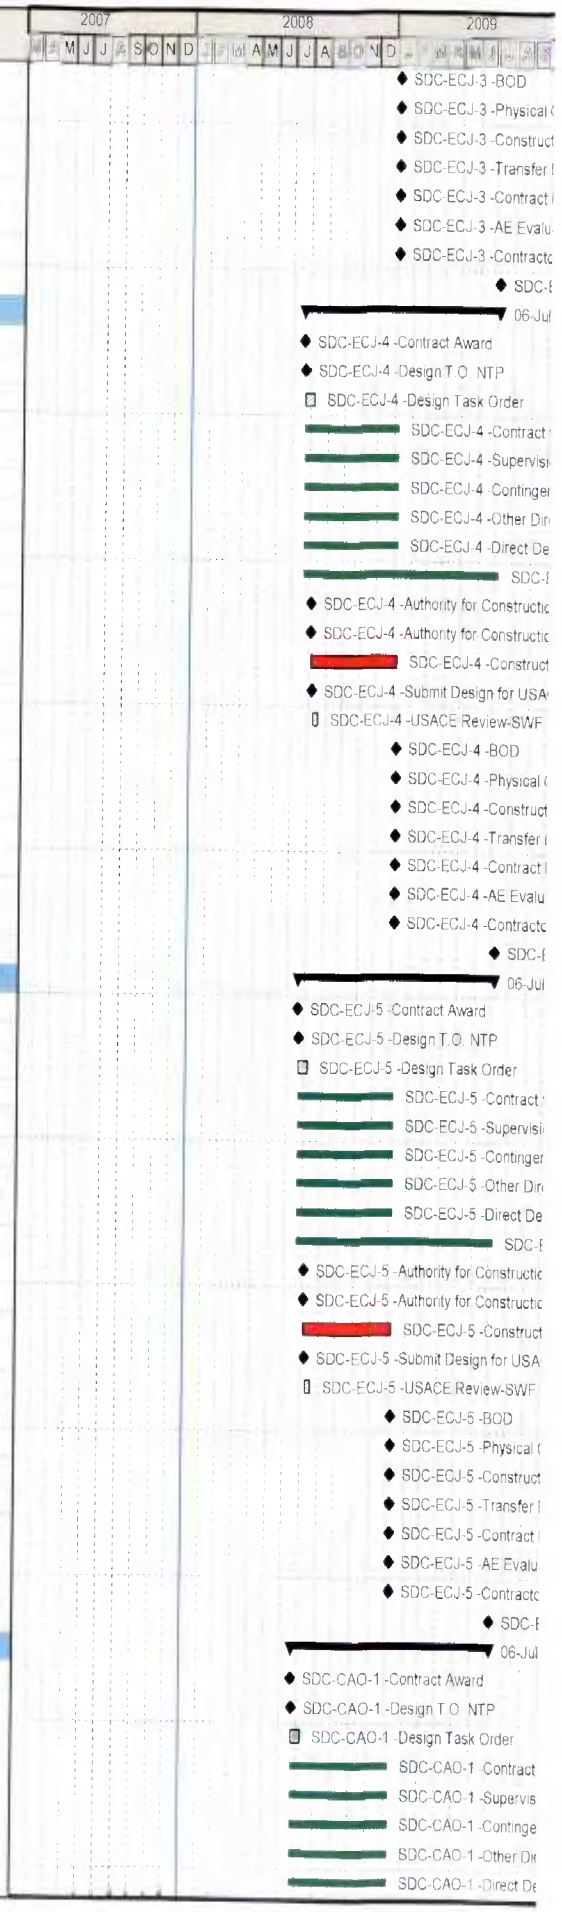

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON19562	SDC-CAO-1 -Contract for 0.17 miles PF - RMS	CON19525	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19550	SDC-CAO-1 -Authority for Construction Acknowledged	CON19555	0.0d	0.0d	0%		06-Aug-08		
CON19555	SDC-CAO-1 -Authority for Construction	REO40177, CON19525, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19585	SDC-CAO-1 -Construction Period for .17 miles PF	CON19550, CON19560, CON19565, CON19570, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19540	SDC-CAO-1 -Submit Design for USACE Review	CON19535	0.0d	0.0d	0%				08-Aug-08
CON19545	SDC-CAO-1 -USACE Review-SWF	CON19540	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19590	SDC-CAO-1 -BOD	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19595	SDC-CAO-1 -Physical Completion	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19605	SDC-CAO-1 -Construction Completion	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19610	SDC-CAO-1 -Transfer Document Date	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19615	SDC-CAO-1 -Contract Required Completion	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19620	SDC-CAO-1 -AE Evaluation Date	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19630	SDC-CAO-1 -Contractor Evaluation Date	CON19585	0.0d	0.0d	0%				07-Jan-09
CON19600	SDC-CAO-1 -Fiscal Completion	CON19585, CON19562	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.009 A-2 (2003-2) SDC-CAO-2 (1.06 miles) Rattlesnake Ridge to Larry Pierce Road			240.0d	240.0d			21-Jul-08		06-Jul-09
CON19635	SDC-CAO-2 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19640	SDC-CAO-2 -Design T.O. NTP	CON19635	0.0d	0.0d	0%		22-Jul-08		
CON19645	SDC-CAO-2 -Design Task Order	CON19640	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19670	SDC-CAO-2 -Contract for 1.06 miles PF	CON19635	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19675	SDC-CAO-2 -Supervision & Administration	CON19635	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19680	SDC-CAO-2 -Contingency	CON19635	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19685	SDC-CAO-2 -Other Direct Costs	CON19635	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19690	SDC-CAO-2 -Direct Design Costs	CON19635	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19672	SDC-CAO-2 -Contract for 1.06 miles PF - RMS	CON19635	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19660	SDC-CAO-2 -Authority for Construction Acknowledged	CON19665	0.0d	0.0d	0%		06-Aug-08		
CON19665	SDC-CAO-2 -Authority for Construction	REO40199, CON19635, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19695	SDC-CAO-2 -Construction Period for 1.06 miles PF	CON19660, CON19670, CON19675, CON19680, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19650	SDC-CAO-2 -Submit Design for USACE Review	CON19645	0.0d	0.0d	0%				08-Aug-08
CON19655	SDC-CAO-2 -USACE Review-SWF	CON19650	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19700	SDC-CAO-2 -BOD	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19705	SDC-CAO-2 -Physical Completion	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19715	SDC-CAO-2 -Construction Completion	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19720	SDC-CAO-2 -Transfer Document Date	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19725	SDC-CAO-2 -Contract Required Completion	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19730	SDC-CAO-2 -AE Evaluation Date	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19735	SDC-CAO-2 -Contractor Evaluation Date	CON19695	0.0d	0.0d	0%				07-Jan-09
CON19710	SDC-CAO-2 -Fiscal Completion	CON19695, CON19672	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.010 A-2 (2003-3) SDC-CAO-3 (0.09 miles) West edge of Boundary Peak			240.0d	240.0d			21-Jul-08		06-Jul-09
CON19740	SDC-CAO-3 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19745	SDC-CAO-3 -Design T.O. NTP	CON19740	0.0d	0.0d	0%		22-Jul-08		
CON19750	SDC-CAO-3 -Design Task Order	CON19745	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19775	SDC-CAO-3 -Contract for 0.09 miles PF	CON19740	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19780	SDC-CAO-3 -Supervision & Administration	CON19740	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19785	SDC-CAO-3 -Contingency	CON19740	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19790	SDC-CAO-3 -Other Direct Costs	CON19740	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19795	SDC-CAO-3 -Direct Design Costs	CON19740	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19777	SDC-CAO-3 -Contract for 0.09 miles PF - RMS	CON19740	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19765	SDC-CAO-3 -Authority for Construction Acknowledged	CON19770	0.0d	0.0d	0%		06-Aug-08		
CON19770	SDC-CAO-3 -Authority for Construction	REO40221, CON19740, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19800	SDC-CAO-3 -Construction Period for 0.09 miles PF	CON19765, CON19775, CON19780, CON19785, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19755	SDC-CAO-3 -Submit Design for USACE Review	CON19750	0.0d	0.0d	0%				08-Aug-08
CON19760	SDC-CAO-3 -USACE Review-SWF	CON19755	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19805	SDC-CAO-3 -BOD	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19810	SDC-CAO-3 -Physical Completion	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19820	SDC-CAO-3 -Construction Completion	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19825	SDC-CAO-3 -Transfer Document Date	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19830	SDC-CAO-3 -Contract Required Completion	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19835	SDC-CAO-3 -AE Evaluation Date	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19840	SDC-CAO-3 -Contractor Evaluation Date	CON19800	0.0d	0.0d	0%				07-Jan-09
CON19815	SDC-CAO-3 -Fiscal Completion	CON19800, CON19777	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.011 A-2 (2004-1) SDC-BLV-1 (1.63 miles) Willows Access #1			240.0d	240.0d			21-Jul-08		06-Jul-09
CON19845	SDC-BLV-1 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19850	SDC-BLV-1 -Design T.O. NTP	CON19845	0.0d	0.0d	0%		22-Jul-08		

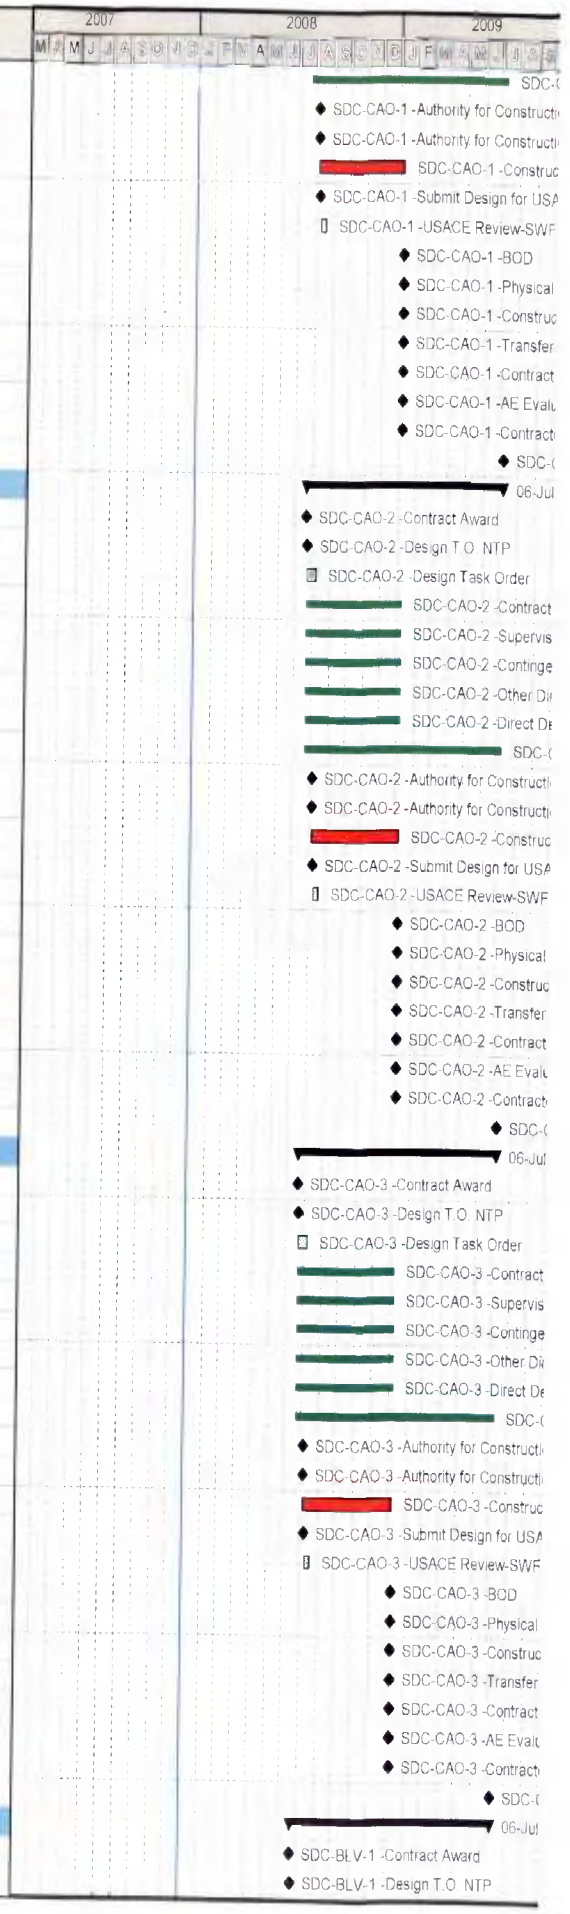

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON19855	SDC-BLV-1 -Design Task Order	CON19850	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19880	SDC-BLV-1 -Contract for 1.63 miles PF	CON19845	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19885	SDC-BLV-1 -Supervision & Administration	CON19845	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19890	SDC-BLV-1 -Contingency	CON19845	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19895	SDC-BLV-1 -Other Direct Costs	CON19845	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19900	SDC-BLV-1 -Direct Design Costs	CON19845	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19882	SDC-BLV-1 -Contract for 1.63 miles PF - RMS	CON19845	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19870	SDC-BLV-1 -Authority for Construction Acknowledged	CON19875	0.0d	0.0d	0%		06-Aug-08		
CON19875	SDC-BLV-1 -Authority for Construction	REO40243, CON19845, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON19905	SDC-BLV-1 -Construction Period for 1.63 miles PF	CON19870, CON19880, CON19885, CON19890, CON19...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19860	SDC-BLV-1 -Submit Design for USACE Review	CON19855	0.0d	0.0d	0%				08-Aug-08
CON19865	SDC-BLV-1 -USACE Review-SWF	CON19860	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON19910	SDC-BLV-1 -BOD	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19915	SDC-BLV-1 -Physical Completion	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19925	SDC-BLV-1 -Construction Completion	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19930	SDC-BLV-1 -Transfer Document Date	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19935	SDC-BLV-1 -Contract Required Completion	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19940	SDC-BLV-1 -AE Evaluation Date	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19945	SDC-BLV-1 -Contractor Evaluation Date	CON19905	0.0d	0.0d	0%				07-Jan-09
CON19920	SDC-BLV-1 -Fiscal Completion	CON19905, CON19882	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.012	**A-2 (2004-2) SDC-BLV-2 (2.01 miles) Willows Access #2**		240.0d	240.0d			21-Jul-08		06-Jul-09
CON19950	SDC-BLV-2 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON19955	SDC-BLV-2 -Design T.O. NTP	CON19950	0.0d	0.0d	0%		22-Jul-08		
CON19960	SDC-BLV-2 -Design Task Order	CON19955	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON19985	SDC-BLV-2 -Contract for 2.01 miles PF	CON19950	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19990	SDC-BLV-2 -Supervision & Administration	CON19950	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19995	SDC-BLV-2 -Contingency	CON19950	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20000	SDC-BLV-2 -Other Direct Costs	CON19950	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20005	SDC-BLV-2 -Direct Design Costs	CON19950	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON19987	SDC-BLV-2 -Contract for 2.01 miles PF - RMS	CON19950	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON19975	SDC-BLV-2 -Authority for Construction Acknowledged	CON19980	0.0d	0.0d	0%		06-Aug-08		
CON19980	SDC-BLV-2 -Authority for Construction	REO40265, CON19950, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON20010	SDC-BLV-2 -Construction Period for 2.01 miles PF	CON19975, CON19985, CON19990, CON19995, CON20	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON19965	SDC-BLV-2 -Submit Design for USACE Review	CON19960	0.0d	0.0d	0%				08-Aug-08
CON19970	SDC-BLV-2 -USACE Review-SWF	CON19965	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON20015	SDC-BLV-2 -BOD	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20020	SDC-BLV-2 -Physical Completion	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20030	SDC-BLV-2 -Construction Completion	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20035	SDC-BLV-2 -Transfer Document Date	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20040	SDC-BLV-2 -Contract Required Completion	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20045	SDC-BLV-2 -AE Evaluation Date	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20050	SDC-BLV-2 -Contractor Evaluation Date	CON20010	0.0d	0.0d	0%				07-Jan-09
CON20025	SDC-BLV-2 -Fiscal Completion	CON20010, CON19987	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.013	**A-2 (2004-3) SDC-BLV-3 (0.05 miles) Airport Mesa**		240.0d	240.0d			21-Jul-08		06-Jul-09
CON20055	SDC-BLV-3 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON20060	SDC-BLV-3 -Design T.O. NTP	CON20055	0.0d	0.0d	0%		22-Jul-08		
CON20065	SDC-BLV-3 -Design Task Order	CON20060	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON20090	SDC-BLV-3 -Contract for 0.05 miles PF	CON20055	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20095	SDC-BLV-3 -Supervision & Administration	CON20055	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20100	SDC-BLV-3 -Contingency	CON20055	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20105	SDC-BLV-3 -Other Direct Costs	CON20055	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20110	SDC-BLV-3 -Direct Design Costs	CON20055	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20092	SDC-BLV-3 -Contract for 0.05 miles PF - RMS	CON20055	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON20080	SDC-BLV-3 -Authority for Construction Acknowledged	CON20085	0.0d	0.0d	0%		06-Aug-08		
CON20085	SDC-BLV-3 -Authority for Construction	REO40287, CON20055, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON20115	SDC-BLV-3 -Construction Period for .05 miles PF	CON20080, CON20090, CON20095, CON20100, CON20...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON20070	SDC-BLV-3 -Submit Design for USACE Review	CON20065	0.0d	0.0d	0%				08-Aug-08
CON20075	SDC-BLV-3 -USACE Review-SWF	CON20070	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON20120	SDC-BLV-3 -BOD	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20125	SDC-BLV-3 -Physical Completion	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20135	SDC-BLV-3 -Construction Completion	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20140	SDC-BLV-3 -Transfer Document Date	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20145	SDC-BLV-3 -Contract Required Completion	CON20115	0.0d	0.0d	0%				07-Jan-09

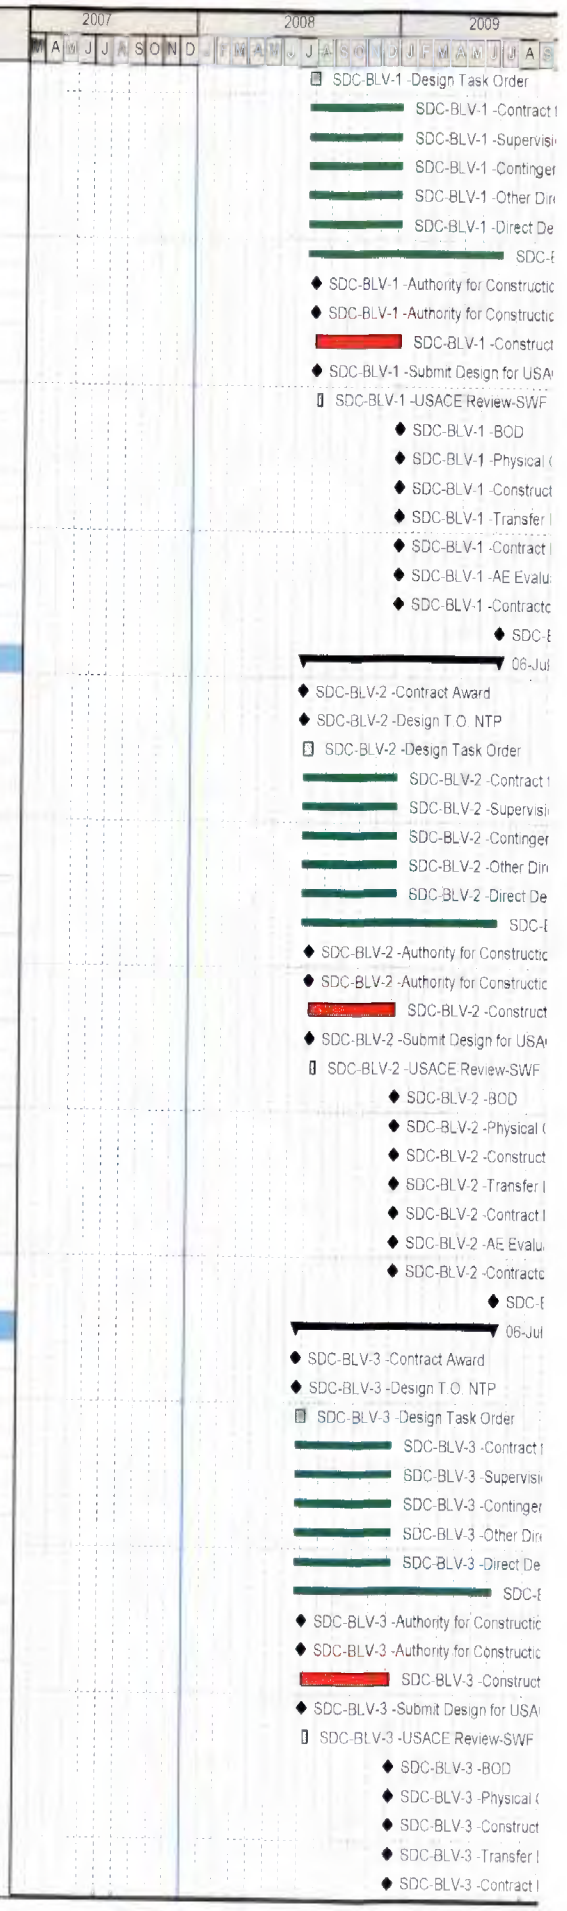

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON20150	SDC-BLV-3 -AE Evaluation Date	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20155	SDC-BLV-3 -Contractor Evaluation Date	CON20115	0.0d	0.0d	0%				07-Jan-09
CON20130	SDC-BLV-3 -Fiscal Completion	CON20115, CON20092	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.01.014 A-2 (2004-4) SDC-BLV-4 (1.47 miles) O'Neal Valley			240.0d	240.0d			21-Jul-08		06-Jul-09
CON20160	SDC-BLV-4 -Contract Award	DES13236	0.0d	0.0d	0%				21-Jul-08
CON20165	SDC-BLV-4 -Design T.O. NTP	CON20160	0.0d	0.0d	0%		22-Jul-08		
CON20170	SDC-BLV-4 -Design Task Order	CON20165	18.0d	18.0d	0%		22-Jul-08		08-Aug-08
CON20195	SDC-BLV-4 -Contract for 1.47 miles PF	CON20160	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20200	SDC-BLV-4 -Supervision & Administration	CON20160	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20205	SDC-BLV-4 -Contingency	CON20160	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20210	SDC-BLV-4 -Other Direct Costs	CON20160	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20215	SDC-BLV-4 -Direct Design Costs	CON20160	170.0d	170.0d	0%		22-Jul-08		07-Jan-09
CON20197	SDC-BLV-4 -Contract for 1.47 miles PF - RMS	CON20160	350.0d	350.0d	0%		22-Jul-08		06-Jul-09
CON20185	SDC-BLV-4 -Authority for Construction Acknowledged	CON20190	0.0d	0.0d	0%		06-Aug-08		
CON20190	SDC-BLV-4 -Authority for Construction	REO40309, CON20160, ENV19428	0.0d	0.0d	0%		06-Aug-08		
CON20220	SDC-BLV-4 -Construction Period for 1.47 miles PF	CON20185, CON20195, CON20200, CON20205, CON20...	155.0d	155.0d	0%		06-Aug-08		07-Jan-09
CON20175	SDC-BLV-4 -Submit Design for USACE Review	CON20170	0.0d	0.0d	0%				08-Aug-08
CON20180	SDC-BLV-4 -USACE Review-SWF	CON20175	10.0d	10.0d	0%		09-Aug-08		18-Aug-08
CON20225	SDC-BLV-4 -BOD	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20230	SDC-BLV-4 -Physical Completion	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20240	SDC-BLV-4 -Construction Completion	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20245	SDC-BLV-4 -Transfer Document Date	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20250	SDC-BLV-4 -Contract Required Completion	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20255	SDC-BLV-4 -AE Evaluation Date	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20260	SDC-BLV-4 -Contractor Evaluation Date	CON20220	0.0d	0.0d	0%				07-Jan-09
CON20235	SDC-BLV-4 -Fiscal Completion	CON20220, CON20197	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.02 ELC (11.44 miles)			392.0d	392.0d			02-Jan-08		22-Jul-09
143875.60000.61000.150.02.001 B-3 (2005-1) RFP#N/A (1.62 Miles) SEA El Centro Station			152.0d	152.0d			02-Jan-08		07-Aug-08
CON1630	ELC-ELS-1-Contract Award		0.0d	0.0d	0%				02-Jan-08*
CON1640	ELC-ELS-1-Contract for 1.62 miles PF	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1650	ELC-ELS-1-Supervision & Administration	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1660	ELC-ELS-1-Contingency	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1670	ELC-ELS-1-Other Direct Costs	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1680	ELC-ELS-1-Direct Design Costs	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1641	ELC-ELS-1-Contract for 1.62 miles PF - RMS	CON1690	38.0d	38.0d	0%		02-Jan-08		09-Feb-08
CON1690	ELC-ELS-1-Design T.O. NTP	CON1630	0.0d	0.0d	0%		12-Jan-08		
CON1700	ELC-ELS-1-Design Task Order	CON1690	18.0d	18.0d	0%		12-Jan-08		30-Jan-08
CON1750	ELC-ELS-1-Submit Design for USACE Review	CON1700	0.0d	0.0d	0%				30-Jan-08
CON1710	ELC-ELS-1-USACE Review-SWF	CON1750	10.0d	10.0d	0%		30-Jan-08		09-Feb-08
CON1740	ELC-ELS-1-Construction Period for 1.62 miles PF	CON1730, CON1640, CON1650, CON1660, CON1670, ...	0.0d	0.0d	0%		09-Feb-08		09-Feb-08
CON1730	ELC-ELS-1-Authority for Construction Acknowledged	CON1720	0.0d	0.0d	0%		09-Feb-08		
CON1760	ELC-ELS-1-BOD	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1770	ELC-ELS-1-Physical Completion	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1790	ELC-ELS-1-Construction Completion	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1800	ELC-ELS-1-Transfer Document Date	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1810	ELC-ELS-1-Contract Required Completion	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1820	ELC-ELS-1-AE Evaluation Date	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1830	ELC-ELS-1-Contractor Evaluation Date	CON1740	0.0d	0.0d	0%				09-Feb-08
CON1720	ELC-ELS-1-Authority for Construction	CON1710, REO16000	0.0d	0.0d	0%		09-Feb-08		
CON1780	ELC-ELS-1-Fiscal Completion	CON1740	0.0d	0.0d	0%				07-Aug-08
143875.60000.61000.150.02.002 B-4 (2006-1) ELC-CAX-1 (8.59 miles) CAX East Checks			319.0d	319.0d			15-Apr-08		22-Jul-09
CON5830	ELC-CAX-1 -Contract Award	DES13210	0.0d	0.0d	0%				15-Apr-08
CON5890	ELC-CAX-1 -Design T.O. NTP	CON5830	0.0d	0.0d	0%		16-Apr-08		
CON5900	ELC-CAX-1 -Design Task Order	CON5890	32.0d	32.0d	0%		16-Apr-08		17-May-08
CON5840	ELC-CAX-1 -Contract for 8.59 miles PF	CON5890, CON5830	283.0d	283.0d	0%		16-Apr-08		23-Jan-09
CON5850	ELC-CAX-1 -Supervision & Administration	CON5890, CON5830	283.0d	283.0d	0%		16-Apr-08		23-Jan-09
CON5860	ELC-CAX-1 -Contingency	CON5890, CON5830	283.0d	283.0d	0%		16-Apr-08		23-Jan-09
CON5870	ELC-CAX-1 -Other Direct Costs	CON5890, CON5830	283.0d	283.0d	0%		16-Apr-08		23-Jan-09
CON5880	ELC-CAX-1 -Direct Design Costs	CON5890, CON5830	283.0d	283.0d	0%		16-Apr-08		23-Jan-09
CON5842	ELC-CAX-1 -Contract for 8.59 miles PF - RMS	CON5830	463.0d	463.0d	0%		16-Apr-08		22-Jul-09
CON5950	ELC-CAX-1 -Submit Design for USACE Review	CON5900	0.0d	0.0d	0%				17-May-08
CON5910	ELC-CAX-1 -USACE Review-SWF	CON5950	10.0d	10.0d	0%		18-May-08		27-May-08
CON5930	ELC-CAX-1 -Authority for Construction Acknowledged	CON5920	0.0d	0.0d	0%		26-Jul-08		

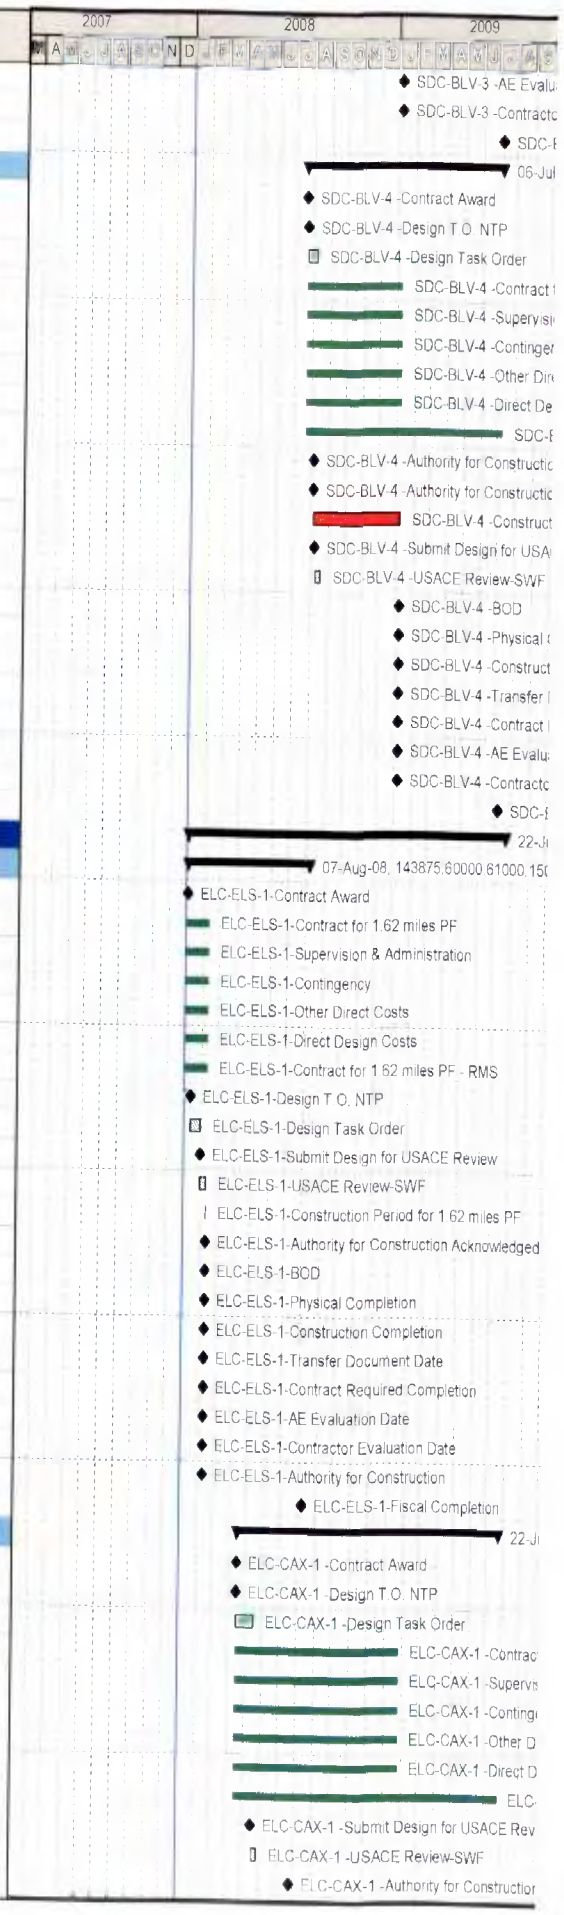

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON5920	ELC-CAX-1 -Authority for Construction	CON5830, REO40406, ENV15581	0.0d	0.0d	0%		26-Jul-08		
CON5940	ELC-CAX-1 -Construction Period for 8.59 miles PF	CON5930, CON5840, CON5850, CON5860, CON5870, ..	182.0d	182.0d	0%		26-Jul-08		23-Jan-09
CON5960	ELC-CAX-1 -BOD	CON5940	0.0d	0.0d	0%				23-Jan-09
CON5970	ELC-CAX-1 -Physical Completion	CON5940	0.0d	0.0d	0%				23-Jan-09
CON5990	ELC-CAX-1 -Construction Completion	CON5940	0.0d	0.0d	0%				23-Jan-09
CON6000	ELC-CAX-1 -Transfer Document Date	CON5940	0.0d	0.0d	0%				23-Jan-09
CON6010	ELC-CAX-1 -Contract Required Completion	CON5940	0.0d	0.0d	0%				23-Jan-09
CON6020	ELC-CAX-1 -AE Evaluation Date	CON5940	0.0d	0.0d	0%				23-Jan-09
CON6030	ELC-CAX-1 -Contractor Evaluation Date	CON5940	0.0d	0.0d	0%				23-Jan-09
CON5980	ELC-CAX-1 -Fiscal Completion	CON5940, CON5842	0.0d	0.0d	0%				22-Jul-09
143875.60000.61000.150.02.003	**B-5B (2006-2) ELC-CAX-2 (2.85 miles) East end of CAX E Checks to MON 210**		248.0d	248.0d			15-Apr-08		12-Apr-09
CON6040	ELC-CAX-2 -Contract Award	DES14084	0.0d	0.0d	0%				15-Apr-08
CON6100	ELC-CAX-2 -Design T.O. NTP	CON6040	0.0d	0.0d	0%		16-Apr-08		
CON6110	ELC-CAX-2 -Design Task Order	CON6100	32.0d	32.0d	0%		16-Apr-08		17-May-08
CON6050	ELC-CAX-2 -Contract for 2.85 miles PF	CON6040, CON6190	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6060	ELC-CAX-2 -Supervision & Administration	CON6040, CON6190	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6070	ELC-CAX-2 -Contingency	CON6040, CON6190	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6080	ELC-CAX-2 -Other Direct Costs	CON6040, CON6190	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6090	ELC-CAX-2 -Direct Design Costs	CON6040, CON6190	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6052	ELC-CAX-2 -Contract for 2.85 miles PF - RMS	CON6040	362.0d	362.0d	0%		16-Apr-08		12-Apr-09
CON6160	ELC-CAX-2 -Submit Design for USACE Review	CON6110	0.0d	0.0d	0%				17-May-08
CON6120	ELC-CAX-2 -USACE Review-SWF	CON6160	10.0d	10.0d	0%		18-May-08		27-May-08
CON6140	ELC-CAX-2 -Authority for Construction Acknowledged	CON6130	0.0d	0.0d	0%		28-May-08		
CON6130	ELC-CAX-2 -Authority for Construction	CON6120, ENV15581, REO40420	0.0d	0.0d	0%		28-May-08		
CON6150	ELC-CAX-2 -Construction Period for 2.85 miles PF	CON6050, CON6140, CON6060, CON6070, CON6080, ...	140.0d	140.0d	0%		28-May-08		14-Oct-08
CON6170	ELC-CAX-2 -BOD	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6180	ELC-CAX-2 -Physical Completion	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6200	ELC-CAX-2 -Construction Completion	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6210	ELC-CAX-2 -Transfer Document Date	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6220	ELC-CAX-2 -Contract Required Completion	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6230	ELC-CAX-2 -AE Evaluation Date	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6240	ELC-CAX-2 -Contractor Evaluation Date	CON6150	0.0d	0.0d	0%				14-Oct-08
CON6190	ELC-CAX-2 -Fiscal Completion	CON6150, CON6052	0.0d	0.0d	0%				12-Apr-09
143875.60000.61000.150.03	**YUM (13.98 miles)**		327.0d	327.0d			30-Apr-08		18-Aug-09
143875.60000.61000.150.03.001	**C-1 (2007-1) YUM-CAX/YUS-1 (10.28 miles) Andrade POE: Imperial sand dunes to CA-AZ lin**		299.0d	299.0d			12-May-08		21-Jul-09
CON15810	YUM-CAX/YUS-1 -Contract Award	DES13262	0.0d	0.0d	0%				12-May-08
CON15870	YUM-CAX/YUS-1 -Design T.O. NTP	CON15810	0.0d	0.0d	0%		13-May-08		
CON15880	YUM-CAX/YUS-1 -Design Task Order	CON15870	32.0d	32.0d	0%		13-May-08		13-Jun-08
CON15820	YUM-CAX/YUS-1 -Contract for 10.28 miles PF	CON15810	255.0d	255.0d	0%		13-May-08		22-Jan-09
CON15830	YUM-CAX/YUS-1 -Supervision & Administration	CON15810	255.0d	255.0d	0%		13-May-08		22-Jan-09
CON15840	YUM-CAX/YUS-1 -Contingency	CON15810	255.0d	255.0d	0%		13-May-08		22-Jan-09
CON15850	YUM-CAX/YUS-1 -Other Direct Costs	CON15810	255.0d	255.0d	0%		13-May-08		22-Jan-09
CON15860	YUM-CAX/YUS-1 -Direct Design Costs	CON15810	255.0d	255.0d	0%		13-May-08		22-Jan-09
CON15822	YUM-CAX/YUS-1 -Contract for 10.28 miles PF - RMS	CON15810	435.0d	435.0d	0%		13-May-08		21-Jul-09
CON15930	YUM-CAX/YUS-1 -Submit Design for USACE Review	CON15880	0.0d	0.0d	0%				13-Jun-08
CON15890	YUM-CAX/YUS-1 -USACE Review-SWF	CON15930	10.0d	10.0d	0%		14-Jun-08		23-Jun-08
CON15910	YUM-CAX/YUS-1 -Authority for Construction Acknowledged	CON15900	0.0d	0.0d	0%		26-Jul-08		
CON15900	YUM-CAX/YUS-1 -Authority for Construction	CON15880, REO40436, ENV18912	0.0d	0.0d	0%		26-Jul-08		
CON15920	YUM-CAX/YUS-1 -Construction Period for 10.28 miles PF	CON15820, CON15910, CON15830, CON15840, CON15...	181.0d	181.0d	0%		26-Jul-08		22-Jan-09
CON15940	YUM-CAX/YUS-1 -BOD	CON15920	0.0d	0.0d	0%				22-Jan-09
CON15950	YUM-CAX/YUS-1 -Physical Completion	CON15920	0.0d	0.0d	0%				22-Jan-09
CON15970	YUM-CAX/YUS-1 -Construction Completion	CON15920	0.0d	0.0d	0%				22-Jan-09
CON15980	YUM-CAX/YUS-1 -Transfer Document Date	CON15920	0.0d	0.0d	0%				22-Jan-09
CON15990	YUM-CAX/YUS-1 -Contract Required Completion	CON15920	0.0d	0.0d	0%				22-Jan-09
CON16000	YUM-CAX/YUS-1 -AE Evaluation Date	CON15920	0.0d	0.0d	0%				22-Jan-09
CON16010	YUM-CAX/YUS-1 -Contractor Evaluation Date	CON15920	0.0d	0.0d	0%				22-Jan-09
CON15960	YUM-CAX/YUS-1 -Fiscal Completion	CON15920, CON15822	0.0d	0.0d	0%				21-Jul-09
143875.60000.61000.150.03.002	**C-2B (2007-2) YUM-YUS-2 (3.70 miles) From end of P70 project to County 18**		327.0d	327.0d			30-Apr-08		18-Aug-09
CON6250	YUM-YUS-1 -Contract Award	DES13294	0.0d	0.0d	0%				30-Apr-08
CON6310	YUM-YUS-1 -Design T.O. NTP	CON6250	0.0d	0.0d	0%		01-May-08		
CON6320	YUM-YUS-1 -Design Task Order	CON6310	20.0d	20.0d	0%		01-May-08		20-May-08
CON6260	YUM-YUS-2 -Contract for 3.70 miles PF	CON6250	295.0d	295.0d	0%		01-May-08		19-Feb-09
CON6270	YUM-YUS-1 -Supervision & Administration	CON6250	295.0d	295.0d	0%		01-May-08		19-Feb-09

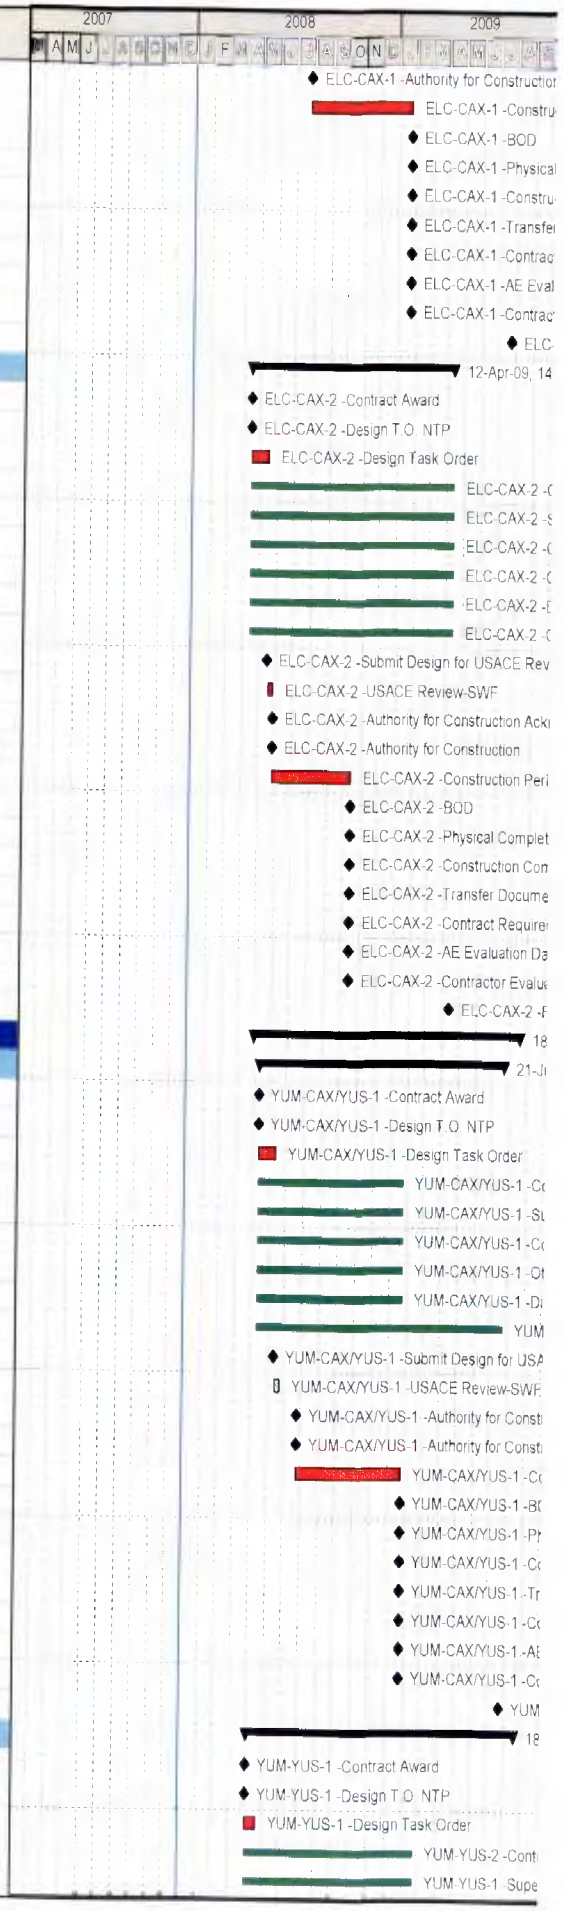

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON6280	YUM-YUS-1 -Contingency	CON6250	295.0d	295.0d	0%		01-May-08		19-Feb-09
CON6290	YUM-YUS-1 -Other Direct Costs	CON6250	295.0d	295.0d	0%		01-May-08		19-Feb-09
CON6300	YUM-YUS-1 -Direct Design Costs	CON6250	295.0d	295.0d	0%		01-May-08		19-Feb-09
CON6262	YUM-YUS-2 -Contract for 3.70 miles PF - RMS	CON6250	475.0d	475.0d	0%		01-May-08		18-Aug-09
CON6370	YUM-YUS-1 -Submit Design for USACE Review	CON6320	0.0d	0.0d	0%				20-May-08
CON6330	YUM-YUS-1 -USACE Review-SWF	CON6370	10.0d	10.0d	0%		21-May-08		30-May-08
CON6350	YUM-YUS-1 -Authority for Construction Acknowledged	CON6340	0.0d	0.0d	0%		26-Jul-08		
CON6340	YUM-YUS-1 -Authority for Construction	CON6320, REO40452, ENV18912	0.0d	0.0d	0%		26-Jul-08		
CON6360	YUM-YUS-1 -Construction Period for 3.70 miles PF	CON6350, CON6260, CON6270, CON6280, CON6300, ..	209.0d	209.0d	0%		26-Jul-08		19-Feb-09
CON6380	YUM-YUS-1 -BOD	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6390	YUM-YUS-1 -Physical Completion	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6410	YUM-YUS-1 -Construction Completion	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6420	YUM-YUS-1 -Transfer Document Date	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6430	YUM-YUS-1 -Contract Required Completion	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6440	YUM-YUS-1 -AE Evaluation Date	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6450	YUM-YUS-1 -Contractor Evaluation Date	CON6360	0.0d	0.0d	0%				19-Feb-09
CON6400	YUM-YUS-1 -Fiscal Completion	CON6360, CON6262	0.0d	0.0d	0%				18-Aug-09
143875.60000.61000.150.04 TCA (7.39 miles)			365.0d	365.0d			02-Jan-08		13-Jun-09
143875.60000.61000.150.04.001 D-5B (2010-2) TCA-NGL-2 (5.16 miles) NGL 1mi E to 6mi E of POE			365.0d	365.0d			02-Jan-08		13-Jun-09
CON6470	TCA-NGL-2 -Contract for 5.16 miles PF		349.0d	349.0d	0%		02-Jan-08		15-Dec-08
CON6480	TCA-NGL-2 -Supervision & Administration		349.0d	349.0d	0%		02-Jan-08		15-Dec-08
CON6490	TCA-NGL-2 -Contingency		349.0d	349.0d	0%		02-Jan-08		15-Dec-08
CON6500	TCA-NGL-2 -Other Direct Costs		349.0d	349.0d	0%		02-Jan-08		15-Dec-08
CON6510	TCA-NGL-2 -Direct Design Costs		349.0d	349.0d	0%		02-Jan-08		15-Dec-08
CON6460	TCA-NGL-2 -Contract Award	DES13328	0.0d	0.0d	0%				27-May-08
CON6520	TCA-NGL-2 -Design T.O. NTP	CON6460	0.0d	0.0d	0%		28-May-08		
CON6530	TCA-NGL-2 -Design Task Order	CON6520	53.0d	53.0d	0%		28-May-08		19-Jul-08
CON6472	TCA-NGL-2 -Contract for 5.16 miles PF - RMS	CON6460	382.0d	382.0d	0%		28-May-08		13-Jun-09
CON6560	TCA-NGL-2 -Authority for Construction Acknowledged	CON6550	0.0d	0.0d	0%		24-Jun-08		
CON6550	TCA-NGL-2 -Authority for Construction	CON6530, REO40331, ENV18998	0.0d	0.0d	0%		24-Jun-08		
CON6570	TCA-NGL-2 -Construction Period for 5.16 miles PF	CON6560, CON6470, CON6480, CON6490, CON6500, ..	175.0d	175.0d	0%		24-Jun-08		15-Dec-08
CON6580	TCA-NGL-2 -Submit Design for USACE Review	CON6530	0.0d	0.0d	0%				19-Jul-08
CON6540	TCA-NGL-2 -USACE Review-SWF	CON6580	10.0d	10.0d	0%		20-Jul-08		29-Jul-08
CON6590	TCA-NGL-2 -BOD	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6600	TCA-NGL-2 -Physical Completion	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6620	TCA-NGL-2 -Construction Completion	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6630	TCA-NGL-2 -Transfer Document Date	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6640	TCA-NGL-2 -Contract Required Completion	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6650	TCA-NGL-2 -AE Evaluation Date	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6660	TCA-NGL-2 Contractor Evaluation Date	CON6570	0.0d	0.0d	0%				15-Dec-08
CON6610	TCA-NGL-2 -Fiscal Completion	CON6570, CON6472	0.0d	0.0d	0%				13-Jun-09
143875.60000.61000.150.04.002 D-6 (2010-3) TCA-NGL-3 (2.23 miles) E Deconcini POE			263.0d	263.0d			27-May-08		13-Jun-09
CON9610	TCA-NGL-3 -Contract Award	DES14110	0.0d	0.0d	0%				27-May-08
CON9670	TCA-NGL-3 -Design T.O. NTP	CON9610	0.0d	0.0d	0%		28-May-08		
CON9680	TCA-NGL-3 -Design Task Order	CON9670	32.0d	32.0d	0%		28-May-08		28-Jun-08
CON9620	TCA-NGL-3 -Contract for 2.23 miles PF	CON9610	202.0d	202.0d	0%		28-May-08		15-Dec-08
CON9630	TCA-NGL-3 -Supervision & Administration	CON9610	202.0d	202.0d	0%		28-May-08		15-Dec-08
CON9640	TCA-NGL-3 -Contingency	CON9610	202.0d	202.0d	0%		28-May-08		15-Dec-08
CON9650	TCA-NGL-3 -Other Direct Costs	CON9610	202.0d	202.0d	0%		28-May-08		15-Dec-08
CON9660	TCA-NGL-3 -Direct Design Costs	CON9610	202.0d	202.0d	0%		28-May-08		15-Dec-08
CON9622	TCA-NGL-3 -Contract for 2.23 miles PF - RMS	CON9610	382.0d	382.0d	0%		28-May-08		13-Jun-09
CON9710	TCA-NGL-3 -Authority for Construction Acknowledged	CON9700	0.0d	0.0d	0%		24-Jun-08		
CON9700	TCA-NGL-3 -Authority for Construction	CON9680, REO40353, ENV18998	0.0d	0.0d	0%		24-Jun-08		
CON9720	TCA-NGL-3 -Construction Period for 2.23 miles PF	CON9710, CON9620, CON9630, CON9640, CON9650,	175.0d	175.0d	0%		24-Jun-08		15-Dec-08
CON9730	TCA-NGL-3 -Submit Design for USACE Review	CON9680	0.0d	0.0d	0%				28-Jun-08
CON9690	TCA-NGL-3 -USACE Review-SWF	CON9730	10.0d	10.0d	0%		29-Jun-08		08-Jul-08
CON9740	TCA-NGL-3 -BOD	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9750	TCA-NGL-3 -Physical Completion	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9770	TCA-NGL-3 -Construction Completion	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9780	TCA-NGL-3 -Transfer Document Date	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9790	TCA-NGL-3 -Contract Required Completion	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9800	TCA-NGL-3 -AE Evaluation Date	CON9720	0.0d	0.0d	0%				15-Dec-08
CON9810	TCA-NGL-3 -Contractor Evaluation Date	CON9720	0.0d	0.0d	0%				15-Dec-08

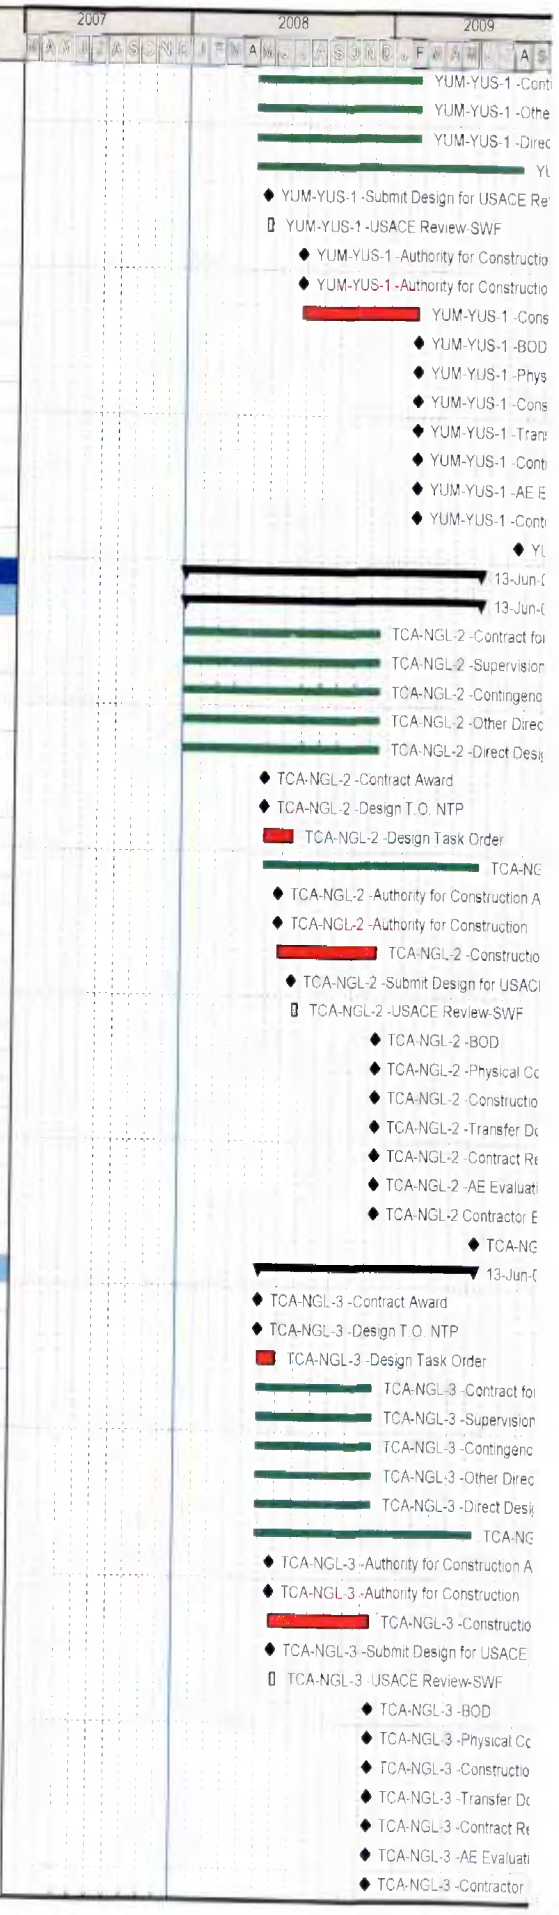

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON9760	TCA-NGL-3 -Fiscal Completion	CON9720, CON9622	0.0d	0.0d	0%				13-Jun-09
143875.60000.61000.150.05 EPT (44.74 miles)			313.0d	313.0d			13-May-08		11-Aug-09
143875.60000.61000.150.05.001 J-2 (2014-4) EPT-STN-4 (3.49 miles) West side Blackie's Gate to west side of cattlepins			301.0d	301.0d			13-May-08		26-Jul-09
CON4780	EPT-STN-4 -Contract Award	DES14162	0.0d	0.0d	0%				13-May-08
CON4850	EPT-STN-4 -Design Task Order	CON4840	0.0d	0.0d	0%		14-May-08		14-May-08
CON4840	EPT-STN-4 -Design T.O. NTP	CON4780	0.0d	0.0d	0%		14-May-08		
CON4790	EPT-STN-4 -Contract for 3.49 miles PF	CON4780	259.0d	259.0d	0%		14-May-08		27-Jan-09
CON4800	EPT-STN-4 -Supervision & Administration	CON4780	259.0d	259.0d	0%		14-May-08		27-Jan-09
CON4810	EPT-STN-4 -Contingency	CON4780	259.0d	259.0d	0%		14-May-08		27-Jan-09
CON4820	EPT-STN-4 -Other Direct Costs	CON4780	259.0d	259.0d	0%		14-May-08		27-Jan-09
CON4830	EPT-STN-4 -Direct Design Costs	CON4780	259.0d	259.0d	0%		14-May-08		27-Jan-09
CON4792	EPT-STN-4 -Contract for 3.49 miles PF - RMS	CON4780	439.0d	439.0d	0%		14-May-08		26-Jul-09
CON4860	EPT-STN-4 -USACE Review-SWF	CON4900	0.0d	0.0d	0%		14-May-08		14-May-08
CON4900	EPT-STN-4 -Submit Design for USACE Review	CON4850	0.0d	0.0d	0%				14-May-08
CON4880	EPT-STN-4 -Authority for Construction Acknowledged	CON4870	0.0d	0.0d	0%		26-Jul-08		
CON4870	EPT-STN-4 -Authority for Construction	CON4860, ENV17270, REQ40580	0.0d	0.0d	0%		26-Jul-08		
CON4890	EPT-STN-4 -Construction Period for 3.49 miles PF	CON4880, CON4790, CON4800, CON4810, CON4820, ...	186.0d	186.0d	0%		26-Jul-08		27-Jan-09
CON4910	EPT-STN-4 -BOD	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4920	EPT-STN-4 -Physical Completion	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4940	EPT-STN-4 -Construction Completion	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4950	EPT-STN-4 -Transfer Document Date	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4960	EPT-STN-4 -Contract Required Completion	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4970	EPT-STN-4 -AE Evaluation Date	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4980	EPT-STN-4 -Contractor Evaluation Date	CON4890	0.0d	0.0d	0%				27-Jan-09
CON4930	EPT-STN-4 -Fiscal Completion	CON4890, CON4792	0.0d	0.0d	0%				26-Jul-09
143875.60000.61000.150.05.002 K-2A (2016-2) EPT-YST-2 (9.60 Miles) 1mi E of US 54 to Socorro Headgates			296.0d	296.0d			06-Jun-08		11-Aug-09
CON4782	EPT-YST-2 -Contract Award	DES14136	0.0d	0.0d	0%				06-Jun-08
CON4852	EPT-YST-2 -Design Task Order	CON4842	0.0d	0.0d	0%		07-Jun-08		07-Jun-08
CON4842	EPT-YST-2 -Design T.O. NTP	CON4782	0.0d	0.0d	0%		07-Jun-08		
CON4802	EPT-YST-2 -Supervision & Administration	CON4782	251.0d	251.0d	0%		07-Jun-08		12-Feb-09
CON4812	EPT-YST-2 -Contingency	CON4782	251.0d	251.0d	0%		07-Jun-08		12-Feb-09
CON4822	EPT-YST-2 -Other Direct Costs	CON4782	251.0d	251.0d	0%		07-Jun-08		12-Feb-09
CON4832	EPT-YST-2 -Direct Design Costs	CON4782	251.0d	251.0d	0%		07-Jun-08		12-Feb-09
CON4793	EPT-YST-2 -Contract for 9.60 miles PF	CON4782	251.0d	251.0d	0%		07-Jun-08		12-Feb-09
CON4795	EPT-YST-2 -Contract for 9.60 miles PF - RMS	CON4782	431.0d	431.0d	0%		07-Jun-08		11-Aug-09
CON4862	EPT-YST-2 -USACE Review-SWF	CON4902	0.0d	0.0d	0%		07-Jun-08		07-Jun-08
CON4902	EPT-YST-2 -Submit Design for USACE Review	CON4852	0.0d	0.0d	0%				07-Jun-08
CON4882	EPT-YST-2 -Authority for Construction Acknowledged	CON4872	0.0d	0.0d	0%		26-Jul-08		
CON4872	EPT-YST-2 -Authority for Construction	CON4862, ENV19084, REQ40564	0.0d	0.0d	0%		26-Jul-08		
CON4892	EPT-YST-2 -Construction Period for 9.60 miles PF	CON4882, CON4802, CON4812, CON4822, CON4832, ...	202.0d	202.0d	0%		26-Jul-08		12-Feb-09
CON4912	EPT-YST-2 -BOD	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4922	EPT-YST-2 -Physical Completion	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4942	EPT-YST-2 -Construction Completion	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4952	EPT-YST-2 -Transfer Document Date	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4962	EPT-YST-2 -Contract Required Completion	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4972	EPT-YST-2 -AE Evaluation Date	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4982	EPT-YST-2 -Contractor Evaluation Date	CON4892	0.0d	0.0d	0%				12-Feb-09
CON4932	EPT-YST-2 -Fiscal Completion	CON4892, CON4795	0.0d	0.0d	0%				11-Aug-09
143875.60000.61000.150.05.003 K-2B&C (2016-1) EPT-YST-1 (19.42 miles) Socorro Headgates to 1mi W of Fabens POE			293.0d	293.0d			11-Jun-08		11-Aug-09
CON7300	EPT-YST-1 -Contract Award	DES13364	0.0d	0.0d	0%				11-Jun-08
CON7370	EPT-YST-1 -Design Task Order	CON7360	0.0d	0.0d	0%		12-Jun-08		12-Jun-08
CON7360	EPT-YST-1 -Design T.O. NTP	CON7300	0.0d	0.0d	0%		12-Jun-08		
CON7310	EPT-YST-1 -Contract for 19.42 miles PF	CON7300	246.0d	246.0d	0%		12-Jun-08		12-Feb-09
CON7320	EPT-YST-1 -Supervision & Administration	CON7300	246.0d	246.0d	0%		12-Jun-08		12-Feb-09
CON7330	EPT-YST-1 -Contingency	CON7300	246.0d	246.0d	0%		12-Jun-08		12-Feb-09
CON7340	EPT-YST-1 -Other Direct Costs	CON7300	246.0d	246.0d	0%		12-Jun-08		12-Feb-09
CON7350	EPT-YST-1 -Direct Design Costs	CON7300	246.0d	246.0d	0%		12-Jun-08		12-Feb-09
CON7312	EPT-YST-1 -Contract for 19.42 miles PF - RMS	CON7300	426.0d	426.0d	0%		12-Jun-08		11-Aug-09
CON7380	EPT-YST-1 -USACE Review-SWF	CON7420	0.0d	0.0d	0%		12-Jun-08		12-Jun-08
CON7420	EPT-YST-1 -Submit Design for USACE Review	CON7370	0.0d	0.0d	0%				12-Jun-08
CON7400	EPT-YST-1 -Authority for Construction Acknowledged	CON7390	0.0d	0.0d	0%		26-Jul-08		
CON7390	EPT-YST-1 -Authority for Construction	CON7380, REQ40468, ENV19084	0.0d	0.0d	0%		26-Jul-08		
CON7410	EPT-YST-1 -Construction Period for 19.42 miles PF	CON7400, CON7310, CON7320, CON7330, CON7340,	202.0d	202.0d	0%		26-Jul-08		12-Feb-09

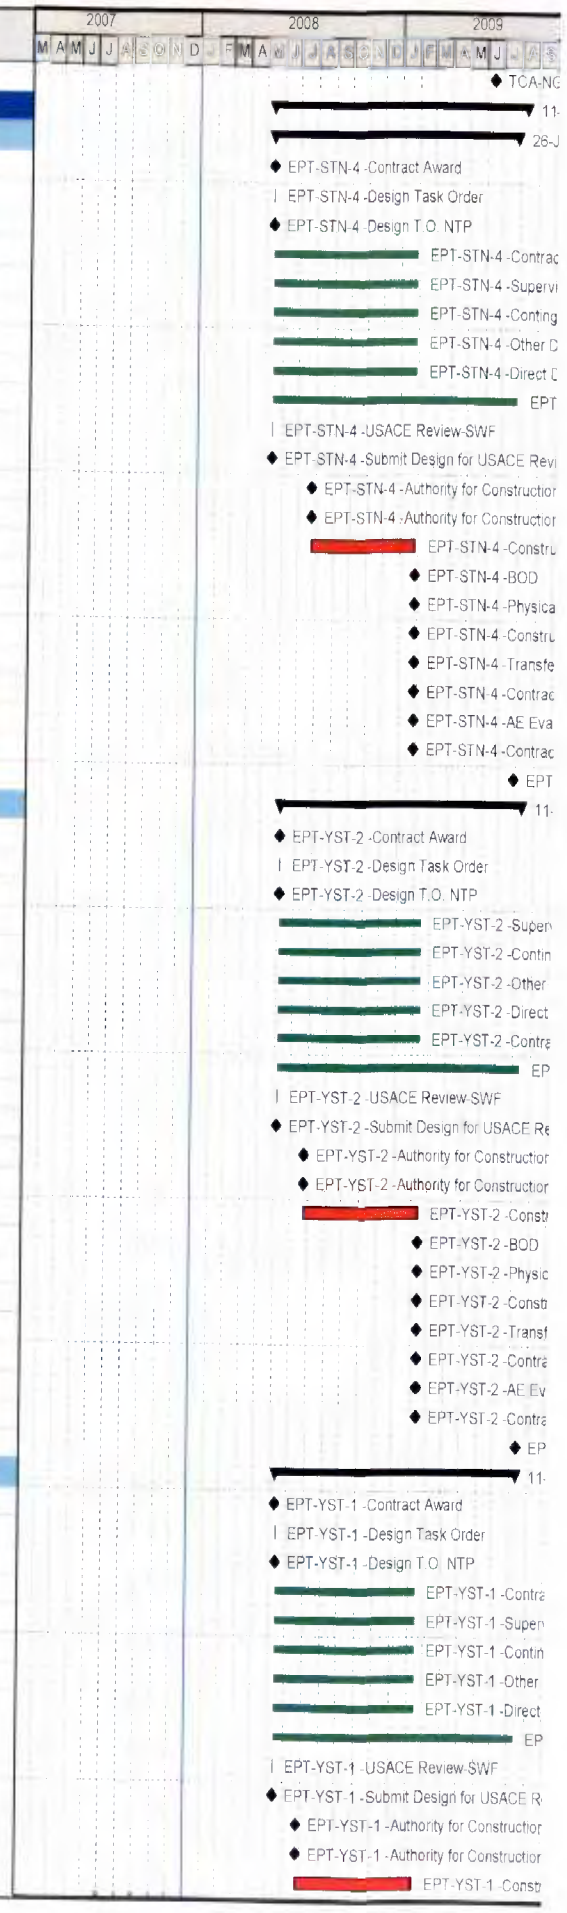

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON7430	EPT-YST-1 -BOD	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7440	EPT-YST-1 -Physical Completion	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7460	EPT-YST-1 -Construction Completion	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7470	EPT-YST-1 -Transfer Document Date	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7480	EPT-YST-1 -Contract Required Completion	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7490	EPT-YST-1 -AE Evaluation Date	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7500	EPT-YST-1 -Contractor Evaluation Date	CON7410	0.0d	0.0d	0%				12-Feb-09
CON7450	EPT-YST-1 -Fiscal Completion	CON7410, CON7312	0.0d	0.0d	0%				11-Aug-09
143875.60000.61000.150.05.004	**K-3 (2017-1) EPT-FBN-1 (9.02 miles) FAB 1mi W to 3mi E of POE**		**271.0d**	**271.0d**			**05-Jun-08**		**07-Jul-09**
CON1500	EPT-FBN-1 -Contract Award	DES13390	0.0d	0.0d	0%				05-Jun-08
CON1535	EPT-FBN-1 -Design Task Order	CON1530	0.0d	0.0d	0%		06-Jun-08		06-Jun-08
CON1530	EPT-FBN-1 -Design T.O. NTP	CON1500	0.0d	0.0d	0%		06-Jun-08		
CON1505	EPT-FBN-1 -Contract for 9.02 miles PF	CON1500	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1510	EPT-FBN-1 -Supervision & Administration	CON1500	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1515	EPT-FBN-1 -Contingency	CON1500	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1520	EPT-FBN-1 -Other Direct Costs	CON1500	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1525	EPT-FBN-1 -Direct Design Costs	CON1500	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1507	EPT-FBN-1 -Contract for 9.02 miles PF - RMS	CON1500	396.0d	396.0d	0%		06-Jun-08		07-Jul-09
CON1540	EPT-FBN-1 -USACE Review-SWF	CON1560	0.0d	0.0d	0%		06-Jun-08		06-Jun-08
CON1550	EPT-FBN-1 -Authority for Construction Acknowledged	CON1545	0.0d	0.0d	0%		06-Jun-08		
CON1560	EPT-FBN-1 -Submit Design for USACE Review	CON1535	0.0d	0.0d	0%				06-Jun-08
CON1545	EPT-FBN-1 -Authority for Construction	CON1540, REO40484, ENV19170	0.0d	0.0d	0%		06-Jun-08		
CON1555	EPT-FBN-1 -Construction Period for 9.02 miles PF	CON1550, CON1505, CON1510, CON1515, CON1520, ...	216.0d	216.0d	0%		06-Jun-08		08-Jan-09
CON1565	EPT-FBN-1 -BOD	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1570	EPT-FBN-1 -Physical Completion	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1580	EPT-FBN-1 -Construction Completion	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1585	EPT-FBN-1 -Transfer Document Date	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1590	EPT-FBN-1 -Contract Required Completion	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1595	EPT-FBN-1 -AE Evaluation Date	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1600	EPT-FBN-1 -Contractor Evaluation Date	CON1555	0.0d	0.0d	0%				08-Jan-09
CON1575	EPT-FBN-1 -Fiscal Completion	CON1555, CON1507	0.0d	0.0d	0%				07-Jul-09
143875.60000.61000.150.05.005	**K-5 (2018-1) EPT-FHT-1 (5.21 miles) FHT 1.5mi W to 1.5mi E of POE**		**209.0d**	**209.0d**			**02-Jul-08**		**05-May-09**
CON16020	EPT-FHT-1 -Contract Award	DES13416	0.0d	0.0d	0%				02-Jul-08
CON16090	EPT-FHT-1 -Design Task Order	CON16080	0.0d	0.0d	0%		03-Jul-08		03-Jul-08
CON16080	EPT-FHT-1 -Design T.O. NTP	CON16020	0.0d	0.0d	0%		03-Jul-08		
CON16030	EPT-FHT-1 -Contract for 3.36 miles PF	CON16020	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16040	EPT-FHT-1 -Supervision & Administration	CON16020	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16050	EPT-FHT-1 -Contingency	CON16020	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16060	EPT-FHT-1 -Other Direct Costs	CON16020	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16070	EPT-FHT-1 -Direct Design Costs	CON16020	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16032	EPT-FHT-1 -Contract for 3.36 miles PF - RMS	CON16020	306.0d	306.0d	0%		03-Jul-08		05-May-09
CON16100	EPT-FHT-1 -USACE Review-SWF	CON16140	0.0d	0.0d	0%		03-Jul-08		03-Jul-08
CON16120	EPT-FHT-1 -Authority for Construction Acknowledged	CON16110	0.0d	0.0d	0%		03-Jul-08		
CON16140	EPT-FHT-1 -Submit Design for USACE Review	CON16090	0.0d	0.0d	0%				03-Jul-08
CON16110	EPT-FHT-1 -Authority for Construction	CON16100, REO40375, ENV19170	0.0d	0.0d	0%		03-Jul-08		
CON16130	EPT-FHT-1 -Construction Period for 5.21 miles PF	CON16120, CON16030, CON16040, CON16050, CON16...	126.0d	126.0d	0%		03-Jul-08		06-Nov-08
CON16150	EPT-FHT-1 -BOD	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16160	EPT-FHT-1 -Physical Completion	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16180	EPT-FHT-1 -Construction Completion	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16190	EPT-FHT-1 -Transfer Document Date	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16200	EPT-FHT-1 -Contract Required Completion	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16210	EPT-FHT-1 -AE Evaluation Date	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16220	EPT-FHT-1 -Contractor Evaluation Date	CON16130	0.0d	0.0d	0%				06-Nov-08
CON16170	EPT-FHT-1 -Fiscal Completion	CON16130, CON16032	0.0d	0.0d	0%				05-May-09
143875.60000.61000.150.06	**MAR (10.78 miles)**		**284.0d**	**284.0d**			**18-Jun-08**		**05-Aug-0**
143875.60000.61000.150.06.001	**L-1 (2019-1) MAR-SBT-1 (4.63 miles) Neely's Crossing**		**212.0d**	**212.0d**			**27-Aug-08**		**06-Jul-09**
CON7510	MAR-SBT-1 -Contract Award	DES14188	0.0d	0.0d	0%				27-Aug-08
CON7580	MAR-SBT-1 -Design Task Order	CON7570	0.0d	0.0d	0%		28-Aug-08		28-Aug-08
CON7570	MAR-SBT-1 -Design T.O. NTP	CON7510	0.0d	0.0d	0%		28-Aug-08		
CON7520	MAR-SBT-1 -Contract for 4.63 miles PF	CON7570	132.0d	132.0d	0%		28-Aug-08		07-Jan-09
CON7530	MAR-SBT-1 -Supervision & Administration	CON7570	132.0d	132.0d	0%		28-Aug-08		07-Jan-09
CON7540	MAR-SBT-1 -Contingency	CON7570	132.0d	132.0d	0%		28-Aug-08		07-Jan-09
CON7550	MAR-SBT-1 -Other Direct Costs	CON7570	132.0d	132.0d	0%		28-Aug-08		07-Jan-09

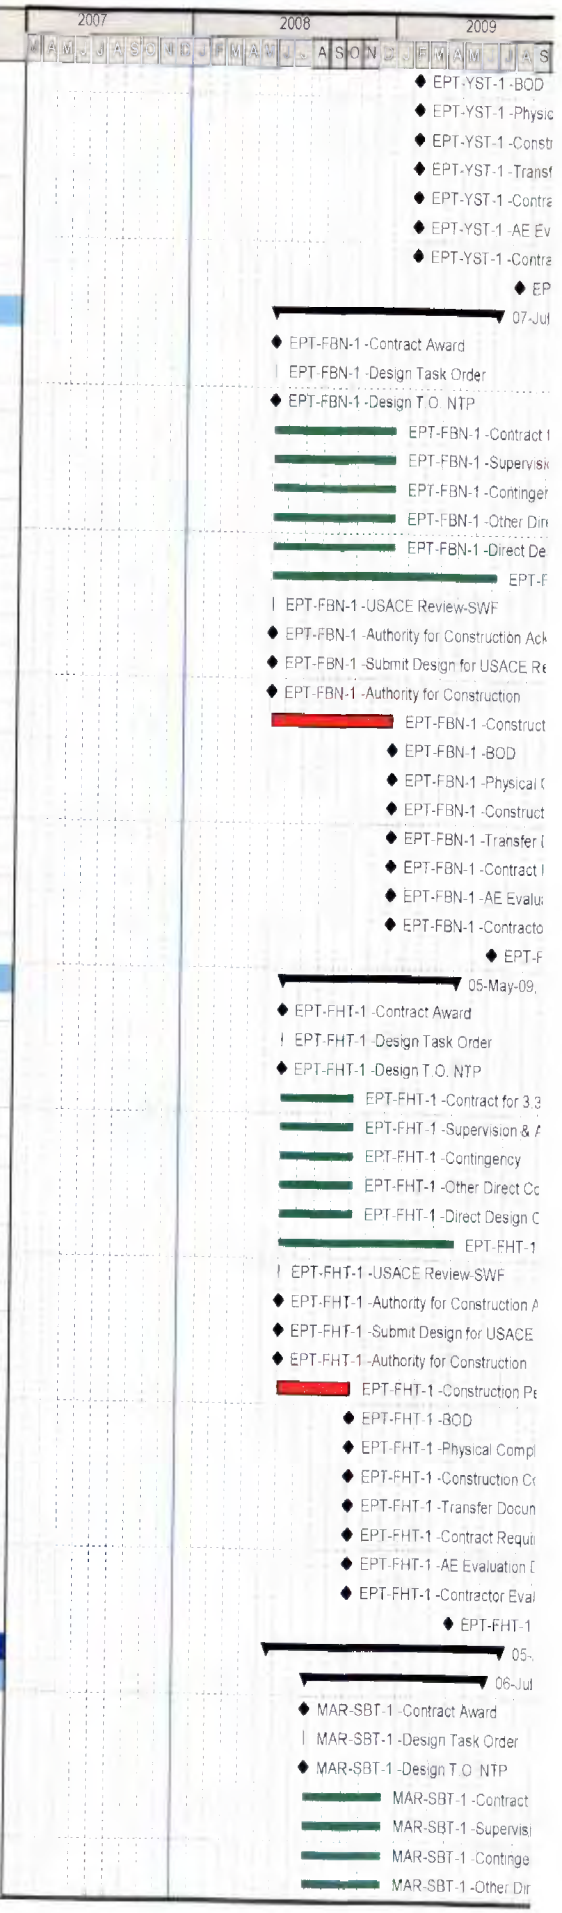

PF-225

PF225

04-Jan-08 11 (

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON7560	MAR-SBT-1 -Direct Design Costs	CON7570	132.0d	132.0d	0%		28-Aug-08		07-Jan-09
CON7522	MAR-SBT-1 -Contract for 4.63 miles PF - RMS	CON7510	312.0d	312.0d	0%		28-Aug-08		06-Jul-09
CON7590	MAR-SBT-1 -USACE Review-SWF	CON7630	0.0d	0.0d	0%		28-Aug-08		28-Aug-08
CON7610	MAR-SBT-1 -Authority for Construction Acknowledged	CON7600	0.0d	0.0d	0%		28-Aug-08		
CON7630	MAR-SBT-1 -Submit Design for USACE Review	CON7580	0.0d	0.0d	0%				28-Aug-08
CON7600	MAR-SBT-1 -Authority for Construction	CON7590, REO40399, ENV19256	0.0d	0.0d	0%		28-Aug-08		
CON7620	MAR-SBT-1 -Construction Period for 4.63 miles PF	CON7610, CON7520, CON7530, CON7540, CON7560, ...	132.0d	132.0d	0%		28-Aug-08		07-Jan-09
CON7640	MAR-SBT-1 -BOD	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7650	MAR-SBT-1 -Physical Completion	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7670	MAR-SBT-1 -Construction Completion	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7680	MAR-SBT-1 -Transfer Document Date	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7690	MAR-SBT-1 -Contract Required Completion	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7700	MAR-SBT-1 -AE Evaluation Date	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7710	MAR-SBT-1 -Contractor Evaluation Date	CON7620	0.0d	0.0d	0%				07-Jan-09
CON7660	MAR-SBT-1 -Fiscal Completion	CON7620, CON7522	0.0d	0.0d	0%				06-Jul-09
143875.60000.61000.150.06.002	**L-1A (2020-1) MAR-PRS-1 (3.28 miles) Presidio's POE to 3.2mi E of POE**		284.0d	284.0d			18-Jun-08		05-Aug-09
CON53105	MAR-PRS-1 -Contract Award	DES13442	0.0d	0.0d	0%				18-Jun-08
CON53140	MAR-PRS-1 -Design Task Order	CON53135	0.0d	0.0d	0%		19-Jun-08		19-Jun-08
CON53145	MAR-PRS-1 -USACE Review-SWF	CON53140	0.0d	0.0d	0%		19-Jun-08		19-Jun-08
CON53135	MAR-PRS-1 -Design T.O. NTP	CON53105	0.0d	0.0d	0%		19-Jun-08		
CON53110	MAR-PRS-1 -Contract for 3.28 miles PF	CON53135	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53115	MAR-PRS-1 -Supervision & Administration	CON53135	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53120	MAR-PRS-1 -Contingency	CON53135	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53125	MAR-PRS-1 -Other Direct Costs	CON53135	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53130	MAR-PRS-1 -Direct Design Costs	CON53135	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53112	MAR-PRS-1 -Contract for 3.28 miles PF - RMS	CON53105	413.0d	413.0d	0%		19-Jun-08		05-Aug-09
CON53165	MAR-PRS-1 -Submit Design for USACE Review	CON53140	0.0d	0.0d	0%				19-Jun-08
CON53155	MAR-PRS-1 -Authority for Construction Acknowledged	CON53150	0.0d	0.0d	0%		26-Jul-08		
CON53150	MAR-PRS-1 -Authority for Construction	CON53145, REO40500, ENV19256	0.0d	0.0d	0%		26-Jul-08		
CON53160	MAR-PRS-1 -Construction Period for 3.28 miles PF	CON53145, CON53155, CON53110, CON53115, CON53...	196.0d	196.0d	0%		26-Jul-08		06-Feb-09
CON53170	MAR-PRS-1 -BOD	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53175	MAR-PRS-1 -Physical Completion	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53185	MAR-PRS-1 -Construction Completion	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53190	MAR-PRS-1 -Transfer Document Date	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53195	MAR-PRS-1 -Contract Required Completion	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53200	MAR-PRS-1 -AE Evaluation Date	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53205	MAR-PRS-1 -Contractor Evaluation Date	CON53160	0.0d	0.0d	0%				06-Feb-09
CON53180	MAR-PRS-1 -Fiscal Completion	CON53160, CON53112	0.0d	0.0d	0%				05-Aug-09
143875.60000.61000.150.06.003	**L-1B (2020-2) MAR-PRS-2 (2.87 miles) Presidio's POE to 3.2mi W of POE**		284.0d	284.0d			18-Jun-08		05-Aug-09
CON53210	MAR-PRS-2 -Contract Award	DES13468	0.0d	0.0d	0%				18-Jun-08
CON53245	MAR-PRS-2 -Design Task Order	CON53240	0.0d	0.0d	0%		19-Jun-08		19-Jun-08
CON53250	MAR-PRS-2 -USACE Review-SWF	CON53245	0.0d	0.0d	0%		19-Jun-08		19-Jun-08
CON53240	MAR-PRS-2 -Design T.O. NTP	CON53210	0.0d	0.0d	0%		19-Jun-08		
CON53215	MAR-PRS-2 -Contract for 2.87 miles PF	CON53240	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53220	MAR-PRS-2 -Supervision & Administration	CON53240	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53225	MAR-PRS-2 -Contingency	CON53240	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53230	MAR-PRS-2 -Other Direct Costs	CON53240	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53235	MAR-PRS-2 -Direct Design Costs	CON53240	233.0d	233.0d	0%		19-Jun-08		06-Feb-09
CON53217	MAR-PRS-2 -Contract for 2.87 miles PF - RMS	CON53210	413.0d	413.0d	0%		19-Jun-08		05-Aug-09
CON53270	MAR-PRS-2 -Submit Design for USACE Review	CON53245	0.0d	0.0d	0%				19-Jun-08
CON53260	MAR-PRS-2 -Authority for Construction Acknowledged	CON53255	0.0d	0.0d	0%		26-Jul-08		
CON53255	MAR-PRS-2 -Authority for Construction	CON53250, REO40516, ENV19256	0.0d	0.0d	0%		26-Jul-08		
CON53265	MAR-PRS-2 -Construction Period for 2.87 miles PF	CON53250, CON53260, CON53215, CON53220, CON53...	196.0d	196.0d	0%		26-Jul-08		06-Feb-09
CON53275	MAR-PRS-2 -BOD	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53280	MAR-PRS-2 -Physical Completion	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53290	MAR-PRS-2 -Construction Completion	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53295	MAR-PRS-2 -Transfer Document Date	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53300	MAR-PRS-2 -Contract Required Completion	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53305	MAR-PRS-2 -AE Evaluation Date	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53310	MAR-PRS-2 -Contractor Evaluation Date	CON53265	0.0d	0.0d	0%				06-Feb-09
CON53285	MAR-PRS-2 -Fiscal Completion	CON53265, CON53217	0.0d	0.0d	0%				05-Aug-09
143875.60000.61000.150.07	**DRT (4.17 miles)**		255.0d	255.0d			06-Jun-08		13-Jun-09
143875.60000.61000.150.07.001	**M-1 (2021-1) DRT-DRS-1 (2.36 miles) DRS San Felipe & Rio Grande to Cienegas Creek & Rio Grande**		242.0d	242.0d			06-Jun-08		27-May-09

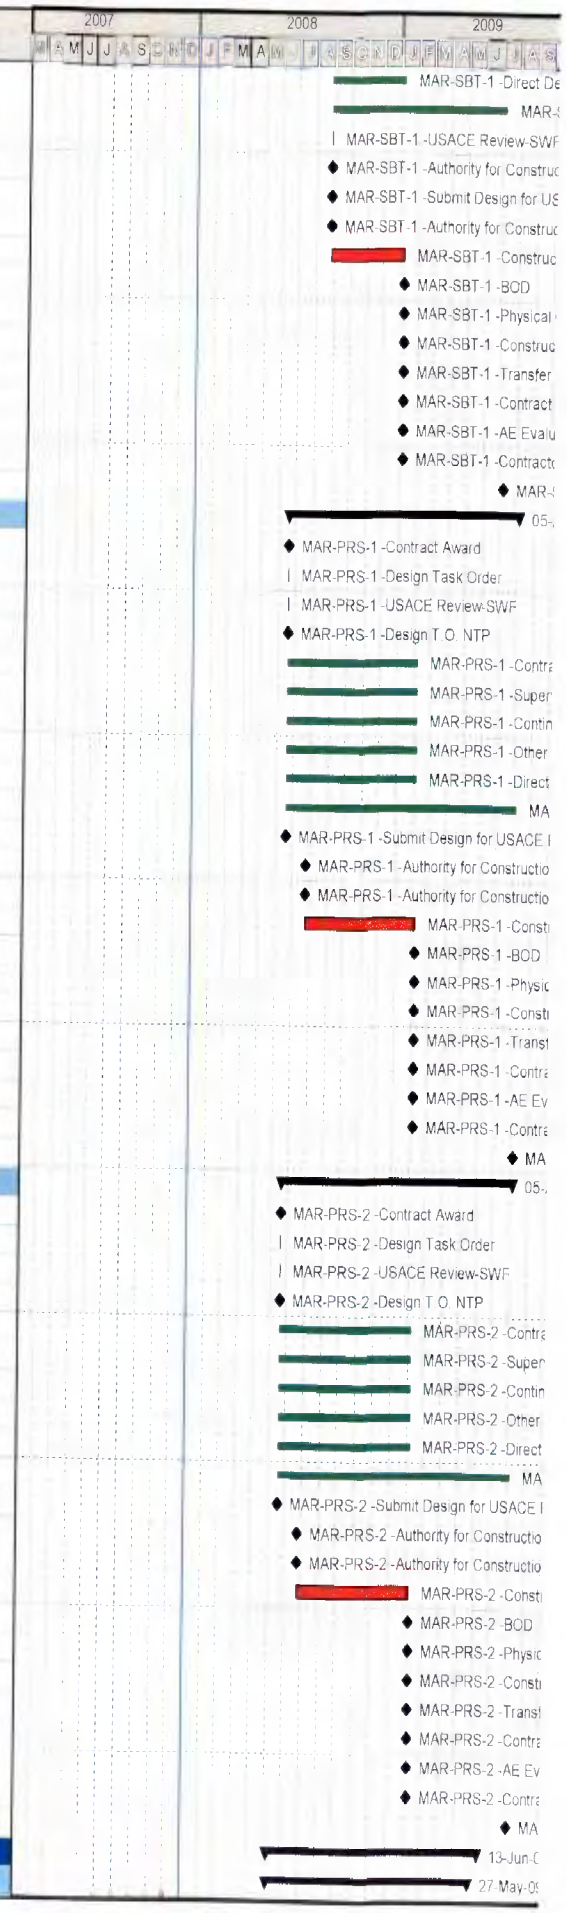

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON7720	DRT-DRS-1 -Contract Award	DES13494	0.0d	0.0d	0%				06-Jun-08
CON7790	DRT-DRS-1 -Design Task Order	CON7780	0.0d	0.0d	0%		07-Jun-08		07-Jun-08
CON7780	DRT-DRS-1 -Design T.O. NTP	CON7720	0.0d	0.0d	0%		07-Jun-08		
CON7730	DRT-DRS-1 -Contract for 2.36 miles PF	CON7780	174.0d	174.0d	0%		07-Jun-08		28-Nov-08
CON7740	DRT-DRS-1 -Supervision & Administration	CON7780	174.0d	174.0d	0%		07-Jun-08		28-Nov-08
CON7750	DRT-DRS-1 -Contingency	CON7780	174.0d	174.0d	0%		07-Jun-08		28-Nov-08
CON7760	DRT-DRS-1 -Other Direct Costs	CON7780	174.0d	174.0d	0%		07-Jun-08		28-Nov-08
CON7770	DRT-DRS-1 -Direct Design Costs	CON7780	174.0d	174.0d	0%		07-Jun-08		28-Nov-08
CON7732	DRT-DRS-1 -Contract for 2.36 miles PF - RMS	CON7720	354.0d	354.0d	0%		07-Jun-08		27-May-09
CON7800	DRT-DRS-1 -USACE Review-SWF	CON7840	0.0d	0.0d	0%		07-Jun-08		07-Jun-08
CON7820	DRT-DRS-1 -Authority for Construction Acknowledged	CON7810	0.0d	0.0d	0%		07-Jun-08		
CON7840	DRT-DRS-1 -Submit Design for USACE Review	CON7790	0.0d	0.0d	0%				07-Jun-08
CON7810	DRT-DRS-1 -Authority for Construction	CON7800, REO40532, ENV19342	0.0d	0.0d	0%		07-Jun-08		
CON7830	DRT-DRS-1 -Construction Period for 2.36miles PF	CON7800, CON7820, CON7730, CON7740, CON7750, ...	159.0d	159.0d	0%		22-Jun-08		28-Nov-08
CON7850	DRT-DRS-1 -BOD	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7860	DRT-DRS-1 -Physical Completion	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7880	DRT-DRS-1 -Construction Completion	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7890	DRT-DRS-1 -Transfer Document Date	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7900	DRT-DRS-1 -Contract Required Completion	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7910	DRT-DRS-1 -AE Evaluation Date	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7920	DRT-DRS-1 -Contractor Evaluation Date	CON7830	0.0d	0.0d	0%				28-Nov-08
CON7870	DRT-DRS-1 -Fiscal Completion	CON7830, CON7732	0.0d	0.0d	0%				27-May-09
143875.60000.61000.150.07.002	M-2A (2022-1) DRT-EGT-1 (0.75 miles) EGT 2.3mi upstream to 1mi North of POE		215.0d	215.0d			04-Aug-08		13-Jun-09
CON7930	DRT-EGT-1 -Contract Award	DES13520	0.0d	0.0d	0%				04-Aug-08
CON8000	DRT-EGT-1 -Design Task Order	CON7990	0.0d	0.0d	0%		05-Aug-08		05-Aug-08
CON7990	DRT-EGT-1 -Design T.O. NTP	CON7930	0.0d	0.0d	0%		05-Aug-08		
CON7940	DRT-EGT-1 -Contract for 0.75 miles PF	CON7990	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON7950	DRT-EGT-1 -Supervision & Administration	CON7990	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON7960	DRT-EGT-1 -Contingency	CON7990	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON7970	DRT-EGT-1 -Other Direct Costs	CON7990	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON7980	DRT-EGT-1 -Direct Design Costs	CON7990	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON7942	DRT-EGT-1 -Contract for 0.75 miles PF - RMS	CON7930	312.0d	312.0d	0%		05-Aug-08		13-Jun-09
CON8010	DRT-EGT-1 -USACE Review-SWF	CON8050	0.0d	0.0d	0%		05-Aug-08		05-Aug-08
CON8030	DRT-EGT-1 -Authority for Construction Acknowledged	CON8020	0.0d	0.0d	0%		05-Aug-08		
CON8050	DRT-EGT-1 -Submit Design for USACE Review	CON8000	0.0d	0.0d	0%				05-Aug-08
CON8020	DRT-EGT-1 -Authority for Construction	CON8010, REO40421, ENV19342	0.0d	0.0d	0%		05-Aug-08		
CON8040	DRT-EGT-1 -Construction Period for 0.75 miles PF	CON7940, CON8030, CON7950, CON7960, CON7970, ...	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8060	DRT-EGT-1 -BOD	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8070	DRT-EGT-1 -Physical Completion	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8090	DRT-EGT-1 -Construction Completion	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8100	DRT-EGT-1 -Transfer Document Date	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8110	DRT-EGT-1 -Contract Required Completion	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8120	DRT-EGT-1 -AE Evaluation Date	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8130	DRT-EGT-1 -Contractor Evaluation Date	CON8040	0.0d	0.0d	0%				15-Dec-08
CON8080	DRT-EGT-1 -Fiscal Completion	CON8040, CON7942	0.0d	0.0d	0%				13-Jun-09
143875.60000.61000.150.07.003	M-2B (2022-2) DRT-EGT-2 (1.06 miles) EGT POE to North of POE		215.0d	215.0d			04-Aug-08		13-Jun-09
CON8560	DRT-EGT-2 -Contract Award	DES14214	0.0d	0.0d	0%				04-Aug-08
CON8630	DRT-EGT-2 -Design Task Order	CON8620	0.0d	0.0d	0%		05-Aug-08		05-Aug-08
CON8620	DRT-EGT-2 -Design T.O. NTP	CON8560	0.0d	0.0d	0%		05-Aug-08		
CON8570	DRT-EGT-2 -Contract for 1.06 miles PF	CON8620	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8580	DRT-EGT-2 -Supervision & Administration	CON8620	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8590	DRT-EGT-2 -Contingency	CON8620	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8600	DRT-EGT-2 -Other Direct Costs	CON8620	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8610	DRT-EGT-2 -Direct Design Costs	CON8620	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8572	DRT-EGT-2 -Contract for 1.06 miles PF - RMS	CON8560	312.0d	312.0d	0%		05-Aug-08		13-Jun-09
CON8640	DRT-EGT-2 -USACE Review-SWF	CON8680	0.0d	0.0d	0%		05-Aug-08		05-Aug-08
CON8660	DRT-EGT-2 -Authority for Construction Acknowledged	CON8650	0.0d	0.0d	0%		05-Aug-08		
CON8680	DRT-EGT-2 -Submit Design for USACE Review	CON8630	0.0d	0.0d	0%				05-Aug-08
CON8650	DRT-EGT-2 -Authority for Construction	CON8640, REO40443, ENV19342	0.0d	0.0d	0%		05-Aug-08		
CON8670	DRT-EGT-2 -Construction Period for 1.06 miles PF	CON8660, CON8570, CON8580, CON8590, CON8600, ...	132.0d	132.0d	0%		05-Aug-08		15-Dec-08
CON8690	DRT-EGT-2 -BOD	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8700	DRT-EGT-2 -Physical Completion	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8720	DRT-EGT-2 -Construction Completion	CON8670	0.0d	0.0d	0%				15-Dec-08

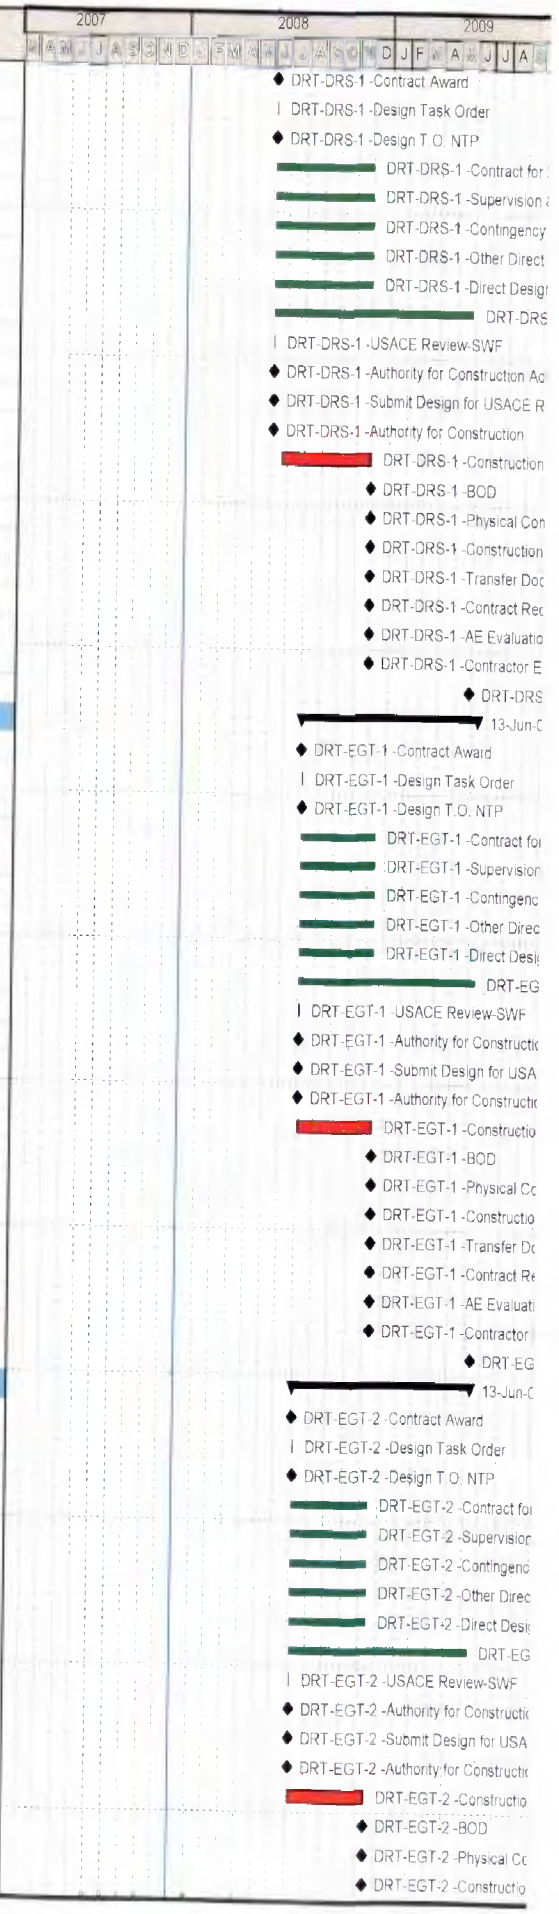

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON8730	DRT-EGT-2 -Transfer Document Date	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8740	DRT-EGT-2 -Contract Required Completion	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8750	DRT-EGT-2 -AE Evaluation Date	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8760	DRT-EGT-2 -Contractor Evaluation Date	CON8670	0.0d	0.0d	0%				15-Dec-08
CON8710	DRT-EGT-2 -Fiscal Completion	CON8670, CON8572	0.0d	0.0d	0%				13-Jun-09
143875.60000.61000.150.08 RGV (69.95 miles)			381.0d	381.0d			02-Jan-08		08-Jul-09
143875.60000.61000.150.08.001 O-1 (2023-1) RGV-RGC-1 (3.76 miles) Near Roma POE			377.0d	377.0d			02-Jan-08		01-Jul-09
CON13612	RGV-RGC-1 -Contract for 3.76 miles PF - RMS		546.0d	546.0d	0%		02-Jan-08		01-Jul-09
CON13600	RGV-RGC-1 -Contract Award	DES13546	0.0d	0.0d	0%				29-Aug-08
CON13670	RGV-RGC-1 -Design Task Order	CON13660	0.0d	0.0d	0%		30-Aug-08		30-Aug-08
CON13660	RGV-RGC-1 -Design T.O. NTP	CON13600	0.0d	0.0d	0%		30-Aug-08		
CON13610	RGV-RGC-1 -Contract for 3.76 miles PF	CON13600	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13620	RGV-RGC-1 -Supervision & Administration	CON13600	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13630	RGV-RGC-1 -Contingency	CON13600	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13640	RGV-RGC-1 -Other Direct Costs	CON13600	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13650	RGV-RGC-1 -Direct Design Costs	CON13720	0.0d	0.0d	0%		30-Aug-08		30-Aug-08
CON13680	RGV-RGC-1 -USACE Review-SWF	CON13690	0.0d	0.0d	0%		30-Aug-08		
CON13700	RGV-RGC-1 -Authority for Construction Acknowledged	CON13670	0.0d	0.0d	0%				30-Aug-08
CON13720	RGV-RGC-1 -Submit Design for USACE Review	CON13680, ENV16209, REO40465	0.0d	0.0d	0%		30-Aug-08		
CON13690	RGV-RGC-1 -Authority for Construction	CON13700, CON13610, CON13620, CON13630, CON13.	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13710	RGV-RGC-1 -Construction Period for 3.76 miles PF	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13730	RGV-RGC-1 -BOD	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13740	RGV-RGC-1 -Physical Completion	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13760	RGV-RGC-1 -Construction Completion	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13770	RGV-RGC-1 -Transfer Document Date	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13780	RGV-RGC-1 -Contract Required Completion	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13790	RGV-RGC-1 -AE Evaluation Date	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13800	RGV-RGC-1 -Contractor Evaluation Date	CON13710	0.0d	0.0d	0%				02-Jan-09
CON13750	RGV-RGC-1 -Fiscal Completion	CON13710, CON13612	0.0d	0.0d	0%				01-Jul-09
143875.60000.61000.150.08.002 O-2 (2023-2) RGV-RGC-2 (8.75 miles) Near RGC POE			204.0d	204.0d			03-Sep-08		29-Jun-09
CON13390	RGV-RGC-2 -Contract Award	DES13572	0.0d	0.0d	0%				03-Sep-08
CON13460	RGV-RGC-2 -Design Task Order	CON13450	0.0d	0.0d	0%		04-Sep-08		04-Sep-08
CON13450	RGV-RGC-2 -Design T.O. NTP	CON13390	0.0d	0.0d	0%		04-Sep-08		
CON13400	RGV-RGC-2 -Contract for 8.75 miles PF	CON13390	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13410	RGV-RGC-2 -Supervision & Administration	CON13390	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13420	RGV-RGC-2 -Contingency	CON13390	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13430	RGV-RGC-2 -Other Direct Costs	CON13390	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13440	RGV-RGC-2 -Direct Design Costs	CON13390	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13402	RGV-RGC-2 -Contract for 8.75 miles PF - RMS	CON13390	298.0d	298.0d	0%		04-Sep-08		29-Jun-09
CON13470	RGV-RGC-2 -USACE Review-SWF	CON13510	0.0d	0.0d	0%		04-Sep-08		04-Sep-08
CON13490	RGV-RGC-2 -Authority for Construction Acknowledged	CON13480	0.0d	0.0d	0%		04-Sep-08		
CON13510	RGV-RGC-2 -Submit Design for USACE Review	CON13460	0.0d	0.0d	0%				04-Sep-08
CON13480	RGV-RGC-2 -Authority for Construction	CON13470, REO40487, ENV16209	0.0d	0.0d	0%		04-Sep-08		
CON13500	RGV-RGC-2 -Construction Period for 8.75 miles PF	CON13490, CON13400, CON13410, CON13420, CON13.	118.0d	118.0d	0%		04-Sep-08		31-Dec-08
CON13520	RGV-RGC-2 -BOD	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13530	RGV-RGC-2 -Physical Completion	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13550	RGV-RGC-2 -Construction Completion	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13560	RGV-RGC-2 -Transfer Document Date	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13570	RGV-RGC-2 -Contract Required Completion	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13580	RGV-RGC-2 -AE Evaluation Date	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13590	RGV-RGC-2 -Contractor Evaluation Date	CON13500	0.0d	0.0d	0%				31-Dec-08
CON13540	RGV-RGC-2 -Fiscal Completion	CON13500, CON13402	0.0d	0.0d	0%				29-Jun-09
143875.60000.61000.150.08.003 O-3 (2024-1) RGV-MCS-1 (1.85 miles) Los Ebanos POE Area			209.0d	209.0d			28-Aug-08		01-Jul-09
CON13180	RGV-MCS-1 -Contract Award	DES13598	0.0d	0.0d	0%				28-Aug-08
CON13250	RGV-MCS-1 -Design Task Order	CON13240	0.0d	0.0d	0%		29-Aug-08		29-Aug-08
CON13240	RGV-MCS-1 -Design T.O. NTP	CON13180	0.0d	0.0d	0%		29-Aug-08		
CON13190	RGV-MCS-1 -Contract for 1.85 miles PF	CON13180	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13200	RGV-MCS-1 -Supervision & Administration	CON13180	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13210	RGV-MCS-1 -Contingency	CON13180	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13220	RGV-MCS-1 -Other Direct Costs	CON13180	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13230	RGV-MCS-1 -Direct Design Costs	CON13180	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13192	RGV-MCS-1 -Contract for 1.85 miles PF - RMS	CON13180	306.0d	306.0d	0%		29-Aug-08		01-Jul-09
CON13260	RGV-MCS-1 -USACE Review-SWF	CON13300	0.0d	0.0d	0%		29-Aug-08		29-Aug-08

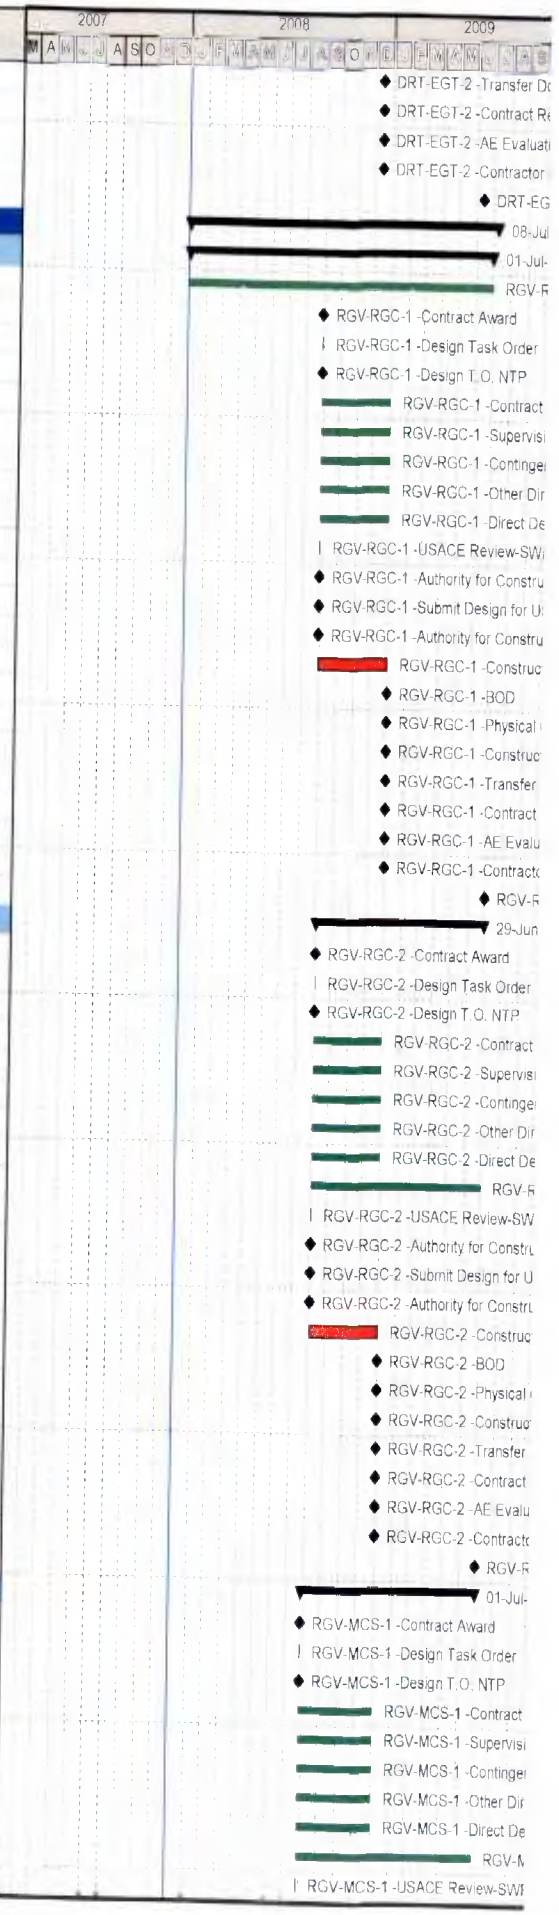

PF-225

PF225

04-Jan-08 11 (
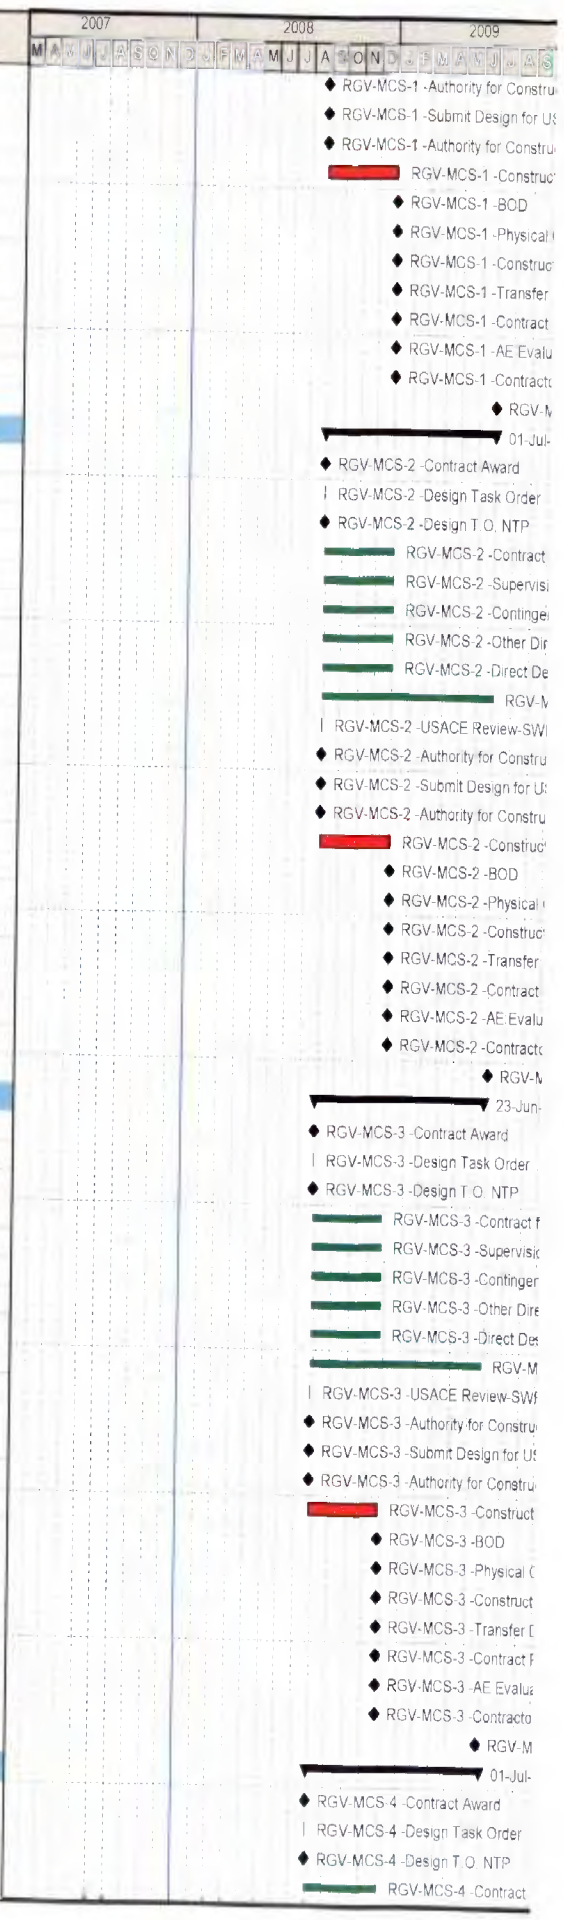
Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
CON13280	RGV-MCS-1 -Authority for Construction Acknowledged	CON13270	0.0d	0.0d	0%		29-Aug-08		29-Aug-08
CON13300	RGV-MCS-1 -Submit Design for USACE Review	CON13250	0.0d	0.0d	0%				
CON13270	RGV-MCS-1 -Authority for Construction	CON13260, REO40509, ENV16209	0.0d	0.0d	0%		29-Aug-08		
CON13290	RGV-MCS-1 -Construction Period for 1.85 miles PF	CON13280, CON13190, CON13200, CON13210, CON13...	126.0d	126.0d	0%		29-Aug-08		02-Jan-09
CON13310	RGV-MCS-1 -BOD	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13320	RGV-MCS-1 -Physical Completion	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13340	RGV-MCS-1 -Construction Completion	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13350	RGV-MCS-1 -Transfer Document Date	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13360	RGV-MCS-1 -Contract Required Completion	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13370	RGV-MCS-1 -AE Evaluation Date	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13380	RGV-MCS-1 -Contractor Evaluation Date	CON13290	0.0d	0.0d	0%				02-Jan-09
CON13330	RGV-MCS-1 -Fiscal Completion	CON13290, CON13192	0.0d	0.0d	0%				01-Jul-09
143875.60000.61000.150.08.004 O-4 (2024-2) RGV-MCS-2 (4.35 miles) From Penitas to Abram			208.0d	208.0d			29-Aug-08		01-Jul-09
CON12970	RGV-MCS-2 -Contract Award	DES13624	0.0d	0.0d	0%				29-Aug-08
CON13040	RGV-MCS-2 -Design Task Order	CON13030	0.0d	0.0d	0%		30-Aug-08		30-Aug-08
CON13030	RGV-MCS-2 -Design T.O. NTP	CON12970	0.0d	0.0d	0%		30-Aug-08		
CON12980	RGV-MCS-2 -Contract for 4.35 miles PF	CON12970	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON12990	RGV-MCS-2 -Supervision & Administration	CON12970	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13000	RGV-MCS-2 -Contingency	CON12970	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13010	RGV-MCS-2 -Other Direct Costs	CON12970	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13020	RGV-MCS-2 -Direct Design Costs	CON12970	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON12982	RGV-MCS-2 -Contract for 4.35 miles PF - RMS	CON12970	305.0d	305.0d	0%		30-Aug-08		01-Jul-09
CON13050	RGV-MCS-2 -USACE Review-SWF	CON13090	0.0d	0.0d	0%		30-Aug-08		30-Aug-08
CON13070	RGV-MCS-2 -Authority for Construction Acknowledged	CON13060	0.0d	0.0d	0%		30-Aug-08		
CON13090	RGV-MCS-2 -Submit Design for USACE Review	CON13040	0.0d	0.0d	0%				30-Aug-08
CON13060	RGV-MCS-2 -Authority for Construction	CON13050, REO40531, ENV16209	0.0d	0.0d	0%		30-Aug-08		
CON13080	RGV-MCS-2 -Construction Period for 4.35 miles PF	CON13070, CON12980, CON12990, CON13000, CON13...	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
CON13100	RGV-MCS-2 -BOD	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13110	RGV-MCS-2 -Physical Completion	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13130	RGV-MCS-2 -Construction Completion	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13140	RGV-MCS-2 -Transfer Document Date	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13150	RGV-MCS-2 -Contract Required Completion	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13160	RGV-MCS-2 -AE Evaluation Date	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13170	RGV-MCS-2 -Contractor Evaluation Date	CON13080	0.0d	0.0d	0%				02-Jan-09
CON13120	RGV-MCS-2 -Fiscal Completion	CON13080, CON12982	0.0d	0.0d	0%				01-Jul-09
143875.60000.61000.150.08.005 O-5 (2024-3) RGV-MCS-3 (1.73 miles) Future Anzalduas POE			203.0d	203.0d			28-Aug-08		23-Jun-09
CON12760	RGV-MCS-3 -Contract Award	DES13650	0.0d	0.0d	0%				28-Aug-08
CON12830	RGV-MCS-3 -Design Task Order	CON12820	0.0d	0.0d	0%		29-Aug-08		29-Aug-08
CON12820	RGV-MCS-3 -Design T.O. NTP	CON12760	0.0d	0.0d	0%		29-Aug-08		
CON12770	RGV-MCS-3 -Contract for 1.73 miles PF	CON12760	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12780	RGV-MCS-3 -Supervision & Administration	CON12760	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12790	RGV-MCS-3 -Contingency	CON12760	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12800	RGV-MCS-3 -Other Direct Costs	CON12760	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12810	RGV-MCS-3 -Direct Design Costs	CON12760	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12772	RGV-MCS-3 -Contract for 1.73 miles PF - RMS	CON12760	298.0d	298.0d	0%		29-Aug-08		23-Jun-09
CON12840	RGV-MCS-3 -USACE Review-SWF	CON12880	0.0d	0.0d	0%		29-Aug-08		29-Aug-08
CON12860	RGV-MCS-3 -Authority for Construction Acknowledged	CON12850	0.0d	0.0d	0%		29-Aug-08		
CON12880	RGV-MCS-3 -Submit Design for USACE Review	CON12830	0.0d	0.0d	0%				29-Aug-08
CON12850	RGV-MCS-3 -Authority for Construction	CON12840, REO40553, ENV16209	0.0d	0.0d	0%		29-Aug-08		
CON12870	RGV-MCS-3 -Construction Period for 1.73 miles PF	CON12860, CON12770, CON12780, CON12790, CON12...	118.0d	118.0d	0%		29-Aug-08		25-Dec-08
CON12890	RGV-MCS-3 -BOD	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12900	RGV-MCS-3 -Physical Completion	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12920	RGV-MCS-3 -Construction Completion	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12930	RGV-MCS-3 -Transfer Document Date	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12940	RGV-MCS-3 -Contract Required Completion	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12950	RGV-MCS-3 -AE Evaluation Date	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12960	RGV-MCS-3 -Contractor Evaluation Date	CON12870	0.0d	0.0d	0%				25-Dec-08
CON12910	RGV-MCS-3 -Fiscal Completion	CON12870, CON12772	0.0d	0.0d	0%				23-Jun-09
143875.60000.61000.150.08.006 O-6 (2024-4) RGV-MCS-4 (3.86 miles) Hidalgo POE			208.0d	208.0d			29-Aug-08		01-Jul-09
CON12550	RGV-MCS-4 -Contract Award	DES13676	0.0d	0.0d	0%				29-Aug-08
CON12620	RGV-MCS-4 -Design Task Order	CON12610	0.0d	0.0d	0%		30-Aug-08		30-Aug-08
CON12610	RGV-MCS-4 -Design T.O. NTP	CON12550	0.0d	0.0d	0%		30-Aug-08		
CON12560	RGV-MCS-4 -Contract for 3.86 miles PF	CON12550	125.0d	125.0d	0%		30-Aug-08		02-Jan-09
