PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
143875.90000.150.03.01 (2006-1) ELC-CAX-1			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.03.01.001 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40385	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40390	Conduct Investigations	REO40385	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40392	Property Valuations, Plat Map & Description	REO40390	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40394	Land Owner Negotiations	REO40392	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40396	Offer to Sell Executed	REO40394	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40398	Prepare Declaration of Taking (DT)	REO40396	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40402	CBP Signature on DT	REO40398	0.0d	0.0d	0%		31-Mar-08		
REO40404	File DT for Construction	REO40402	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40406	Order of Possession for Construction	REO40404	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.03.02 (2006-2) ELC-CAX-2			117.0d	83.0d		02-Nov-07	02-Nov-07 A		29-Apr-08
143875.90000.150.03.02.001 Voluntary ROE-SE			117.0d	83.0d		02-Nov-07	02-Nov-07 A		29-Apr-08
REO40863	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40400	Conduct Investigations	REO40863	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40408	Property Valuations, Plat Map & Description	REO40400	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40410	Land Owner Negotiations	REO40408	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40412	Offer to Sell Executed	REO40410	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40414	Prepare Declaration of Taking (DT)	REO40412	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		28-Mar-08
REO40416	CBP Signature on DT	REO40414	0.0d	0.0d	0%		02-Jan-08		
REO40418	File DT for Construction	REO40416	77.0d	77.0d	0%		09-Jan-08		28-Apr-08
REO40420	Order of Possession for Construction	REO40418	71.0d	71.0d	0%		18-Jan-08		29-Apr-08
143875.90000.150.04 YUM			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.04.01 (2007-1) YUM-SYU-1			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.04.01.01 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40865	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40422	Conduct Investigations	REO40865	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40424	Property Valuations, Plat Map & Description	REO40422	106.0d	61.0d	0%	02-Nov-07	02-Nov-07 A		28-Mar-08
REO40426	Land Owner Negotiations	REO40424	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40428	Offer to Sell Executed	REO40426	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40430	Prepare Declaration of Taking (DT)	REO40428	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40432	CBP Signature on DT	REO40430	0.0d	0.0d	0%		31-Mar-08		
REO40434	File DT for Construction	REO40432	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40436	Order of Possession for Construction	REO40434	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.04.02 (2007-2) YUM-YUS-1			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.04.02.01 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40867	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40438	Conduct Investigations	REO40867	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40440	Property Valuations, Plat Map & Description	REO40438	106.0d	61.0d	0%	02-Nov-07	02-Nov-07 A		28-Mar-08
REO40442	Land Owner Negotiations	REO40440	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40444	Offer to Sell Executed	REO40442	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40446	Prepare Declaration of Taking (DT)	REO40444	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40448	CBP Signature on DT	REO40446	0.0d	0.0d	0%		31-Mar-08		
REO40450	File DT for Construction	REO40448	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40452	Order of Possession for Construction	REO40450	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.05 TCA			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
143875.90000.150.05.01 (2010-2) TCA-NGL-2			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
143875.90000.150.05.01.01 No Voluntary ROE-SE			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
REO40311	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40313	Prepare Declaration of Taking (DT)		19.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	30-Nov-07	30-Nov-07 A
REO40315	CBP Signature on DT	REO40313	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40317	File DT for Temporary Taking	REO40313	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		31-Jan-08
REO40319	Order of Possession for Temporary Rights	REO40317	53.0d	53.0d	0%		02-Jan-08		18-Mar-08
REO40321	Conduct Investigations	REO40319	73.0d	73.0d	0%		02-Jan-08		15-Apr-08
REO40323	Property Valuations, Plat Map & Description	REO40321	95.0d	95.0d	0%		02-Jan-08		15-May-08
REO40325	Land Owner Negotiations	REO40323	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40327	Offer to Sell Executed	REO40325	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40329	Amend DT for Permanent Construction Access	REO40327	14.0d	14.0d	0%		04-Jun-08		23-Jun-08
REO40331	Order of Possession for Construction	REO40329	0.0d	0.0d	0%				23-Jun-08
143875.90000.150.05.02 (2010-3) TCA-NGL-3			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
143875.90000.150.05.02.01 No Voluntary ROE-SE			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
REO40333	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40335	Prepare Declaration of Taking (DT)		19.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	30-Nov-07	30-Nov-07 A

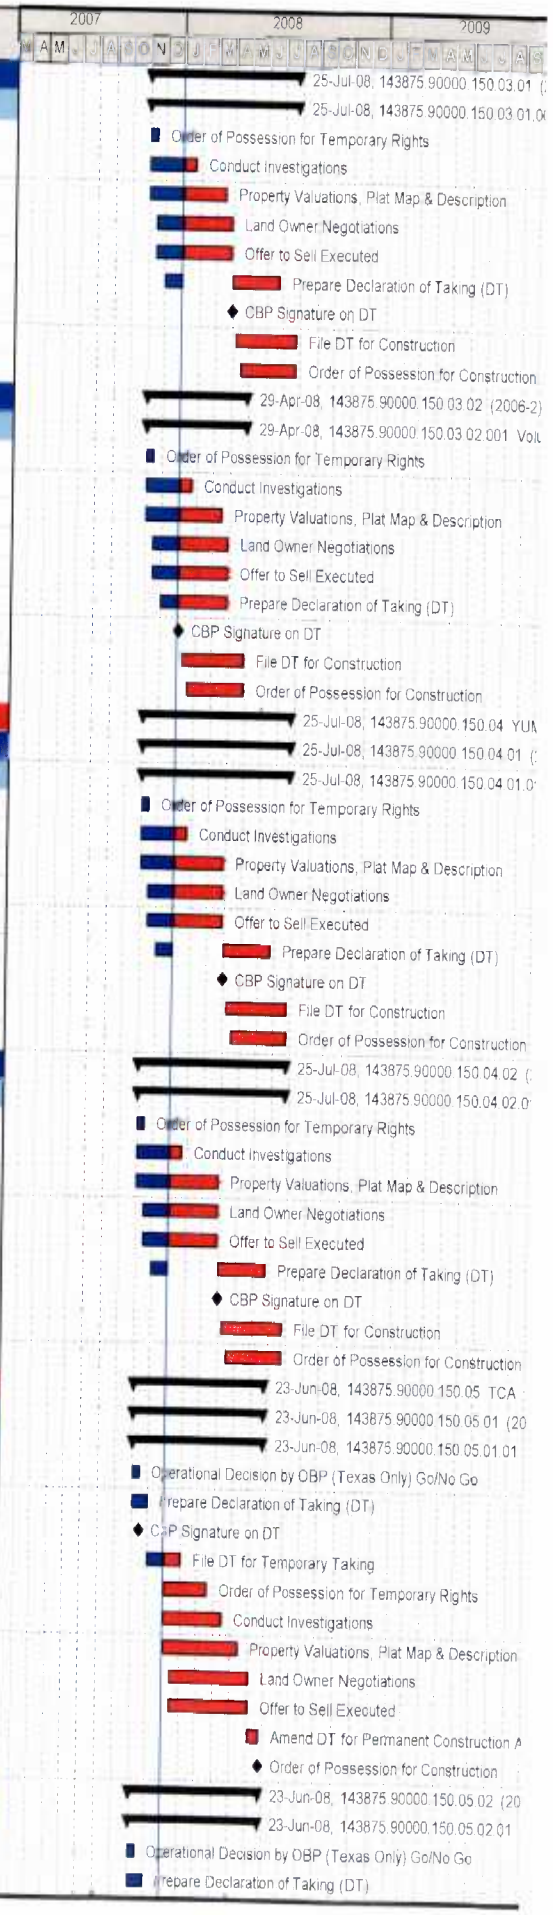

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40337	CBP Signature on DT	REO40335	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40339	File DT for Temporary Taking	REO40335	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		31-Jan-08
REO40341	Order of Possession for Temporary Rights	REO40339	53.0d	53.0d	0%		02-Jan-08		18-Mar-08
REO40343	Conduct Investigations	REO40341	73.0d	73.0d	0%		02-Jan-08		15-Apr-08
REO40345	Property Valuations, Plat Map & Description	REO40343	95.0d	95.0d	0%		02-Jan-08		15-May-08
REO40347	Land Owner Negotiations	REO40345	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40349	Offer to Sell Executed	REO40347	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40351	Amend DT for Permanent Construction Access	REO40349	14.0d	14.0d	0%		04-Jun-08		23-Jun-08
REO40353	Order of Possession for Construction	REO40351	0.0d	0.0d	0%				23-Jun-08
143875.90000.150.06 EPT			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.06.01 (2014-4) EPT-STN-4			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.06.01.001 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40905	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40566	Conduct Investigations	REO40905	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40568	Property Valuations, Plat Map & Description	REO40566	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40570	Land Owner Negotiations	REO40568	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40572	Offer to Sell Executed	REO40570	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40574	Prepare Declaration of Taking (DT)	REO40572	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40576	CBP Signature on DT	REO40574	0.0d	0.0d	0%		31-Mar-08		
REO40578	File DT for Construction	REO40576	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40580	Order of Possession for Construction	REO40578	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.06.02 (2016-2) EPT-YST-2			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.06.02.001 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40881	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40550	Conduct Investigations	REO40881	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40552	Property Valuations, Plat Map & Description	REO40550	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40554	Land Owner Negotiations	REO40552	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40556	Offer to Sell Executed	REO40554	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40558	Prepare Declaration of Taking (DT)	REO40556	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40560	CBP Signature on DT	REO40558	0.0d	0.0d	0%		31-Mar-08		
REO40562	File DT for Construction	REO40560	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40564	Order of Possession for Construction	REO40562	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.06.03 (2016-1) EPT-YST-1			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.06.03.001 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40869	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40454	Conduct Investigations	REO40869	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40456	Property Valuations, Plat Map & Description	REO40454	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40458	Land Owner Negotiations	REO40456	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40460	Offer to Sell Executed	REO40458	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40462	Prepare Declaration of Taking (DT)	REO40460	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40464	CBP Signature on DT	REO40462	0.0d	0.0d	0%		31-Mar-08		
REO40466	File DT for Construction	REO40464	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40468	Order of Possession for Construction	REO40466	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.06.04 (2017-1) EPT-FBN-1			117.0d	83.0d		02-Nov-07	02-Nov-07 A		29-Apr-08
143875.90000.150.06.04.001 Voluntary ROE-SE			117.0d	83.0d		02-Nov-07	02-Nov-07 A		29-Apr-08
REO40871	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40470	Conduct Investigations	REO40871	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40472	Property Valuations, Plat Map & Description	REO40470	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40474	Land Owner Negotiations	REO40472	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40476	Offer to Sell Executed	REO40474	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40478	Prepare Declaration of Taking (DT)		62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		28-Mar-08
REO40480	CBP Signature on DT	REO40478	0.0d	0.0d	0%		02-Jan-08		
REO40482	File DT for Construction	REO40480	77.0d	77.0d	0%		09-Jan-08		28-Apr-08
REO40484	Order of Possession for Construction	REO40482	71.0d	71.0d	0%		18-Jan-08		29-Apr-08
143875.90000.150.06.05 (2018-1) EPT-FHT-1			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
143875.90000.150.06.05.001 No Voluntary ROE-SE			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
REO40355	Operational Decision by OBP (Texas Only) Go/No Go		3.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40357	Prepare Declaration of Taking (DT)		19.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	30-Nov-07	30-Nov-07 A
REO40359	CBP Signature on DT	REO40357	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40361	File DT for Temporary Taking	REO40357	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		31-Jan-08
REO40363	Order of Possession for Temporary Rights	REO40361	53.0d	53.0d	0%		02-Jan-08		18-Mar-08
REO40365	Conduct Investigations	REO40363	73.0d	73.0d	0%		02-Jan-08		15-Apr-08
REO40367	Property Valuations, Plat Map & Description	REO40365	95.0d	95.0d	0%		02-Jan-08		15-May-08

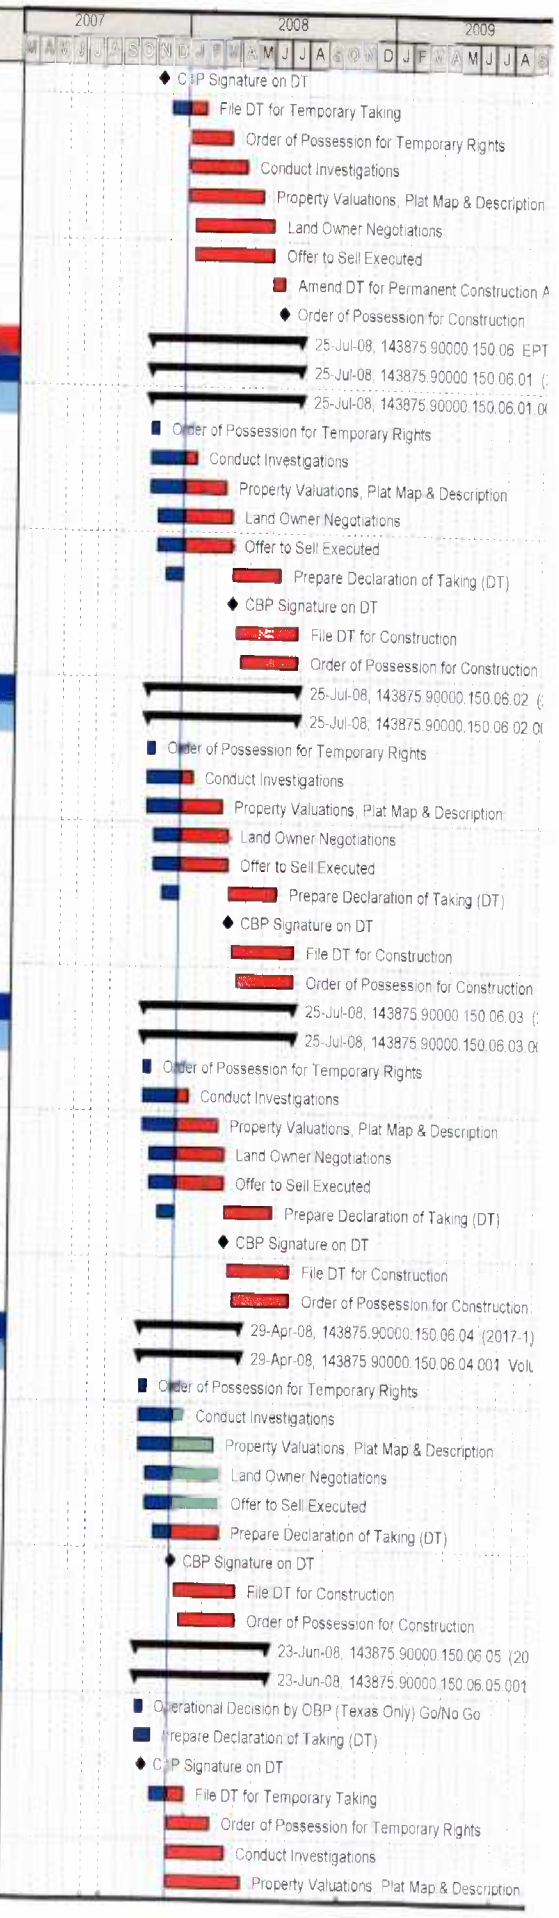

PF-225

PF225

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40369	Land Owner Negotiations	REO40367	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40371	Offer to Sell Executed	REO40369	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40373	Amend DT for Permanent Construction Access	REO40371	14.0d	14.0d	0%		04-Jun-08		23-Jun-08
REO40375	Order of Possession for Construction	REO40373	0.0d	0.0d	0%				23-Jun-08
143875.90000.150.07 MAR			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.07.01 (2019-1) MAR-SBT-1			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
143875.90000.150.07.01.01 No Voluntary ROE-SE			141.0d	121.0d		02-Nov-07	02-Nov-07 A		23-Jun-08
REO40377	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40379	Prepare Declaration of Taking (DT)		19.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	30-Nov-07	30-Nov-07 A
REO40381	CBP Signature on DT	REO40379	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40383	File DT for Temporary Taking	REO40379	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		31-Jan-08
REO40387	Order of Possession for Temporary Rights	REO40383	53.0d	53.0d	0%		02-Jan-08		18-Mar-08
REO40389	Conduct Investigations	REO40387	73.0d	73.0d	0%		02-Jan-08		15-Apr-08
REO40391	Property Valuations, Plat Map & Description	REO40389	95.0d	95.0d	0%		02-Jan-08		15-May-08
REO40393	Land Owner Negotiations	REO40391	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40395	Offer to Sell Executed	REO40393	99.0d	99.0d	0%		14-Jan-08		03-Jun-08
REO40397	Amend DT for Permanent Construction Access	REO40395	14.0d	14.0d	0%		04-Jun-08		23-Jun-08
REO40399	Order of Possession for Construction	REO40397	0.0d	0.0d	0%				23-Jun-08
143875.90000.150.07.02 (2020-1) MAR-PRS-1			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.07.02.01 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40873	Order of Possession for Temporary Rights		10.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40486	Conduct Investigations	REO40873	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40488	Property Valuations, Plat Map & Description	REO40486	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40490	Land Owner Negotiations	REO40488	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40492	Offer to Sell Executed	REO40490	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40494	Prepare Declaration of Taking (DT)	REO40492	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40496	CBP Signature on DT	REO40494	0.0d	0.0d	0%		31-Mar-08		
REO40498	File DT for Construction	REO40496	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40500	Order of Possession for Construction	REO40498	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.07.03 (2020-2) MAR-PRS-2			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
143875.90000.150.07.03.01 Voluntary ROE-SE			164.0d	144.0d		02-Nov-07	02-Nov-07 A		25-Jul-08
REO40875	Order of Possession for Temporary Rights		14.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40502	Conduct Investigations	REO40875	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40504	Property Valuations, Plat Map & Description	REO40502	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40506	Land Owner Negotiations	REO40504	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40508	Offer to Sell Executed	REO40506	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40510	Prepare Declaration of Taking (DT)	REO40508	62.0d	61.0d	100%	30-Nov-07	30-Nov-07 A		24-Jun-08
REO40512	CBP Signature on DT	REO40510	0.0d	0.0d	0%		31-Mar-08		
REO40514	File DT for Construction	REO40512	77.0d	77.0d	0%		07-Apr-08		24-Jul-08
REO40516	Order of Possession for Construction	REO40514	71.0d	71.0d	0%		16-Apr-08		25-Jul-08
143875.90000.150.08 DRT			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.08.01 (2021-1) DRT-DRS-1			117.0d	68.0d		02-Nov-07	02-Nov-07 A		08-Apr-08
143875.90000.150.08.01.01 Voluntary ROE-SE			117.0d	68.0d		02-Nov-07	02-Nov-07 A		08-Apr-08
REO40518	Conduct Investigations	REO40877	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40877	Order of Possession for Temporary Rights	REO40518	10.0d	41.0d	100%	02-Nov-07	02-Nov-07 A		29-Feb-08
REO40520	Property Valuations, Plat Map & Description	REO40520	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40522	Land Owner Negotiations	REO40522	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40524	Offer to Sell Executed	REO40524	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40526	Prepare Declaration of Taking (DT)	REO40526	62.0d	41.0d	100%	30-Nov-07	30-Nov-07 A		29-Feb-08
REO40528	CBP Signature on DT	REO40528	0.0d	0.0d	0%				29-Feb-08
REO40530	File DT for Construction	REO40530	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
REO40532	Order of Possession for Construction		20.0d	20.0d	0%		12-Mar-08		08-Apr-08
143875.90000.150.08.02 (2022-1) DRT-EGT-1			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.08.02.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40401	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40403	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40405	CBP Signature on DT	REO40403	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40407	File DT for Temporary Taking	REO40403	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40409	Order of Possession for Temporary Rights	REO40407	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40411	Conduct Investigations	REO40409	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40413	Property Valuations, Plat Map & Description	REO40411	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40415	Land Owner Negotiations	REO40413	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40417	Offer to Sell Executed	REO40415	99.0d	99.0d	0%		05-Feb-08		24-Jun-08

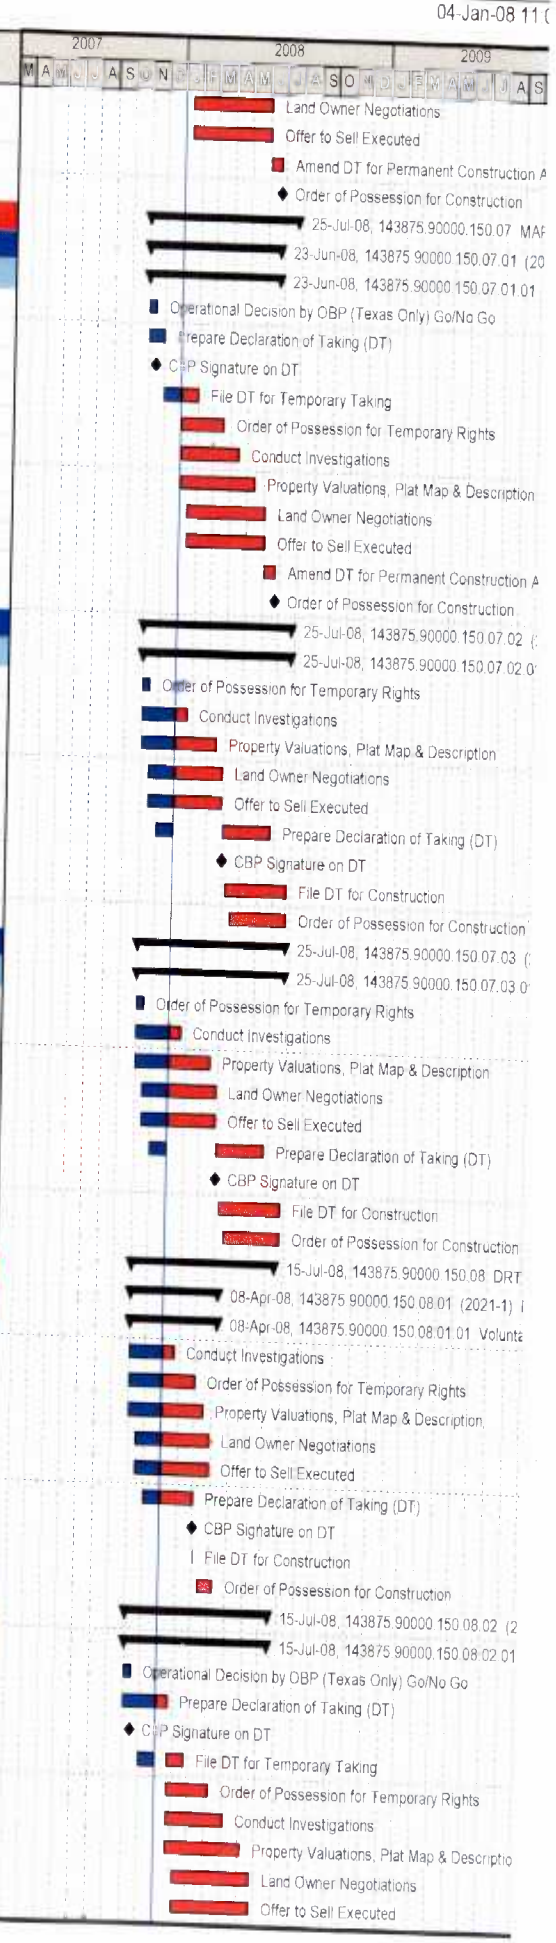

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40419	Amend DT for Permanent Construction Access	REO40417	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40421	Order of Possession for Construction	REO40419	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.08.03 (2022-2) DRT-EGT-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.08.03.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40423	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40425	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40427	CBP Signature on DT	REO40425	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40429	File DT for Temporary Taking	REO40425	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40431	Order of Possession for Temporary Rights	REO40429	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40433	Conduct Investigations	REO40431	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40435	Property Valuations, Plat Map & Description	REO40433	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40437	Land Owner Negotiations	REO40435	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40439	Offer to Sell Executed	REO40437	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40441	Amend DT for Permanent Construction Access	REO40439	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40443	Order of Possession for Construction	REO40441	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09 RGV			175.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.01 (2023-1) RGV-RGC-1			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.01.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40445	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40447	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40449	CBP Signature on DT	REO40447	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40451	File DT for Temporary Taking	REO40447	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40453	Order of Possession for Temporary Rights	REO40451	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40455	Conduct Investigations	REO40453	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40457	Property Valuations, Plat Map & Description	REO40455	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40459	Land Owner Negotiations	REO40457	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40461	Offer to Sell Executed	REO40459	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40463	Amend DT for Permanent Construction Access	REO40461	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40465	Order of Possession for Construction	REO40463	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.02 (2023-2) RGV-RGC-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.02.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40467	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40469	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40471	CBP Signature on DT	REO40469	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40473	File DT for Temporary Taking	REO40469	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40475	Order of Possession for Temporary Rights	REO40473	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40477	Conduct Investigations	REO40475	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40479	Property Valuations, Plat Map & Description	REO40477	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40481	Land Owner Negotiations	REO40479	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40483	Offer to Sell Executed	REO40481	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40485	Amend DT for Permanent Construction Access	REO40483	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40487	Order of Possession for Construction	REO40485	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.03 (2024-1) RGV-MCS-1			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.03.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40489	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40491	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40493	CBP Signature on DT	REO40491	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40495	File DT for Temporary Taking	REO40491	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40497	Order of Possession for Temporary Rights	REO40495	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40499	Conduct Investigations	REO40497	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40501	Property Valuations, Plat Map & Description	REO40499	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40503	Land Owner Negotiations	REO40501	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40505	Offer to Sell Executed	REO40503	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40507	Amend DT for Permanent Construction Access	REO40505	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40509	Order of Possession for Construction	REO40507	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.04 (2024-2) RGV-MCS-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.04.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40511	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40513	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40515	CBP Signature on DT	REO40513	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40517	File DT for Temporary Taking	REO40513	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40519	Order of Possession for Temporary Rights	REO40517	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40521	Conduct Investigations	REO40519	73.0d	73.0d	0%		24-Jan-08		06-May-08

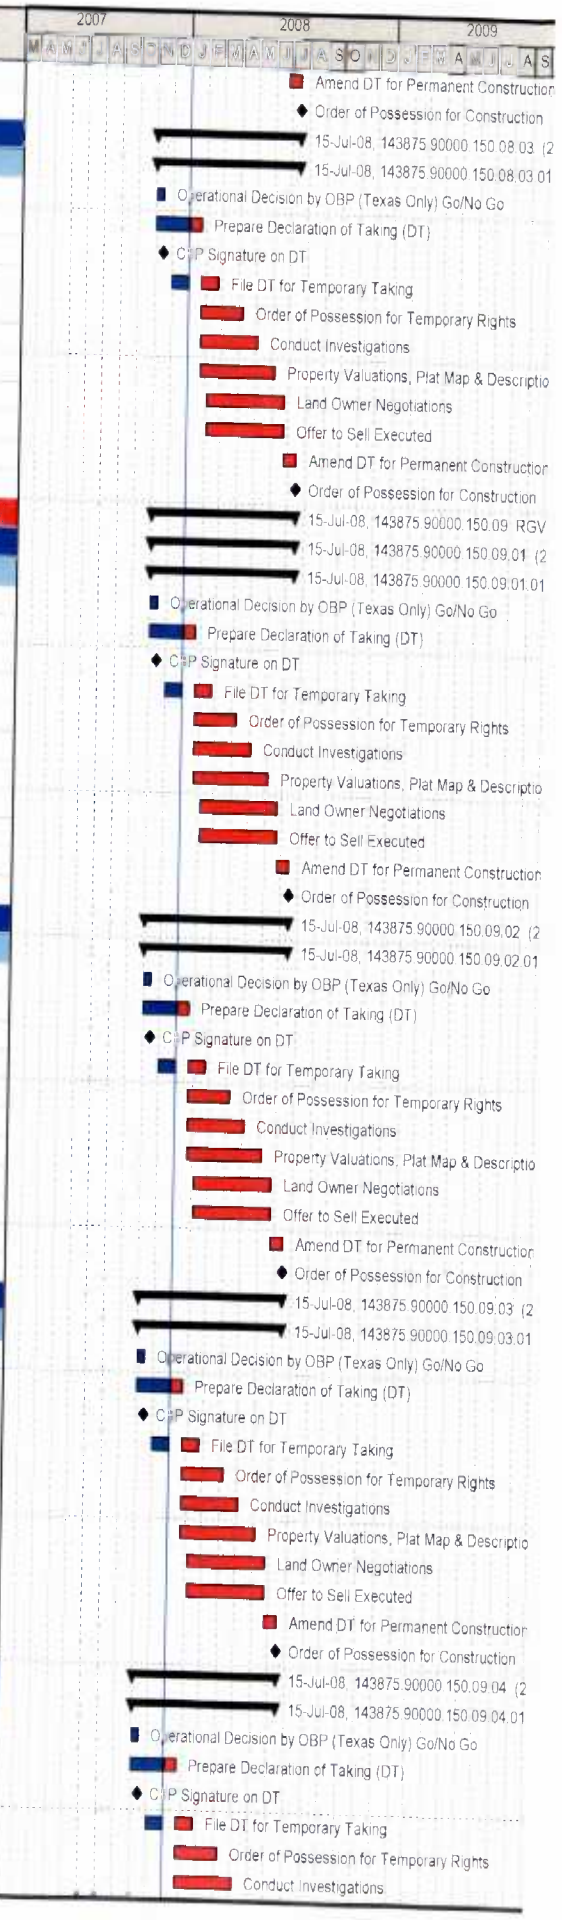

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40523	Property Valuations, Plat Map & Description	REO40521	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40525	Land Owner Negotiations	REO40523	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40527	Offer to Sell Executed	REO40525	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40529	Amend DT for Permanent Construction Access	REO40527	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40531	Order of Possession for Construction	REO40529	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.05 (2024-3) RGV-MCS-3			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.05.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40533	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40535	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40537	CBP Signature on DT	REO40535	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40539	File DT for Temporary Taking	REO40535	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40541	Order of Possession for Temporary Rights	REO40539	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40543	Conduct Investigations	REO40541	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40545	Property Valuations, Plat Map & Description	REO40543	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40547	Land Owner Negotiations	REO40545	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40549	Offer to Sell Executed	REO40547	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40551	Amend DT for Permanent Construction Access	REO40549	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40553	Order of Possession for Construction	REO40551	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.06 (2024-4) RGV-MCS-4			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.06.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40555	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40557	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40559	CBP Signature on DT	REO40557	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40561	File DT for Temporary Taking	REO40557	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40563	Order of Possession for Temporary Rights	REO40561	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40565	Conduct Investigations	REO40563	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40567	Property Valuations, Plat Map & Description	REO40565	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40569	Land Owner Negotiations	REO40567	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40571	Offer to Sell Executed	REO40569	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40573	Amend DT for Permanent Construction Access	REO40571	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40575	Order of Possession for Construction	REO40573	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.07 (2024-5) RGV-MER-1			106.0d	61.0d		02-Nov-07	02-Nov-07 A		28-Mar-08
143875.90000.150.09.07.01 Voluntary ROE-SE			106.0d	61.0d		02-Nov-07	02-Nov-07 A		28-Mar-08
REO40879	Order of Possession for Temporary Rights		12.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40534	Conduct Investigations	REO40879	50.0d	15.0d	0%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40536	Property Valuations, Plat Map & Description	REO40534	106.0d	52.0d	0%	02-Nov-07	02-Nov-07 A		17-Mar-08
REO40538	Land Owner Negotiations	REO40536	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40540	Offer to Sell Executed	REO40538	106.0d	61.0d	0%	14-Nov-07	14-Nov-07 A		28-Mar-08
REO40542	Prepare Declaration of Taking (DT)		62.0d	15.0d	100%	30-Nov-07	30-Nov-07 A		23-Jan-08
REO40544	CBP Signature on DT	REO40542	0.0d	0.0d	0%		07-Feb-08		
REO40546	File DT for Construction	REO40544	1.0d	1.0d	0%		14-Feb-08		14-Feb-08
REO40548	Order of Possession for Construction	REO40546	1.0d	1.0d	0%		25-Feb-08		25-Feb-08
143875.90000.150.09.08 (2024-6) RGV-MER-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.08.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40577	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40579	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40581	CBP Signature on DT	REO40579	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40583	File DT for Temporary Taking	REO40579	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40585	Order of Possession for Temporary Rights	REO40583	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40587	Conduct Investigations	REO40585	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40589	Property Valuations, Plat Map & Description	REO40587	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40591	Land Owner Negotiations	REO40589	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40593	Offer to Sell Executed	REO40591	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40595	Amend DT for Permanent Construction Access	REO40593	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40597	Order of Possession for Construction	REO40595	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.09 (2025-1) RGV-MER-3			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.09.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40599	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40601	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40603	CBP Signature on DT	REO40601	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40605	File DT for Temporary Taking	REO40601	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40607	Order of Possession for Temporary Rights	REO40605	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40609	Conduct Investigations	REO40607	73.0d	73.0d	0%		24-Jan-08		06-May-08

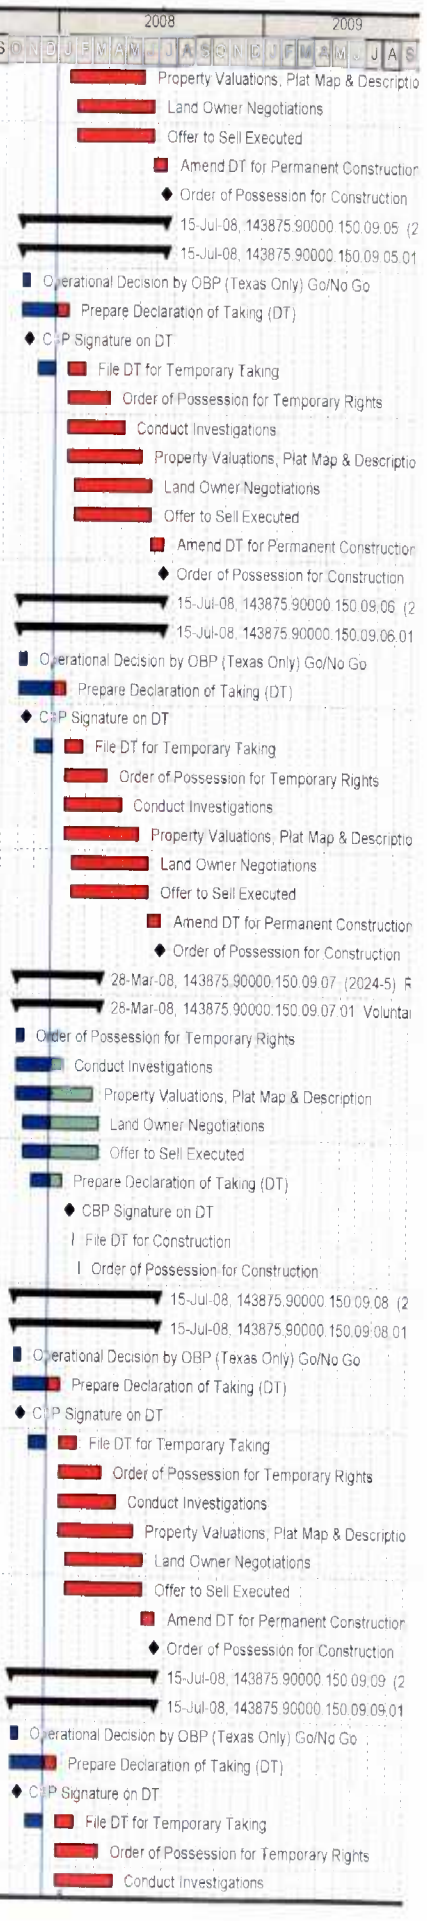

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40611	Property Valuations, Plat Map & Description	REO40609	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40613	Land Owner Negotiations	REO40611	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40615	Offer to Sell Executed	REO40613	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40617	Amend DT for Permanent Construction Access	REO40615	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40619	Order of Possession for Construction	REO40617	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.10 (2025-2) RGV-MER-4			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.10.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40621	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40623	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40625	CBP Signature on DT	REO40623	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40627	File DT for Temporary Taking	REO40623	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40629	Order of Possession for Temporary Rights	REO40627	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40631	Conduct Investigations	REO40629	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40633	Property Valuations, Plat Map & Description	REO40631	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40635	Land Owner Negotiations	REO40633	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40637	Offer to Sell Executed	REO40635	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40639	Amend DT for Permanent Construction Access	REO40637	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40641	Order of Possession for Construction	REO40639	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.11 (2025-3) RGV-HRL-1			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.11.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40883	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40885	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40887	CBP Signature on DT	REO40883	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40889	File DT for Temporary Taking	REO40883	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40891	Order of Possession for Temporary Rights	REO40887	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40893	Conduct Investigations	REO40889	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40895	Property Valuations, Plat Map & Description	REO40891	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40897	Land Owner Negotiations	REO40893	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40899	Offer to Sell Executed	REO40895	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40901	Amend DT for Permanent Construction Access	REO40897	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
	Order of Possession for Construction	REO40899	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.12 (2025-4) RGV-HRL-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.12.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40643	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40645	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40647	CBP Signature on DT	REO40645	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40649	File DT for Temporary Taking	REO40645	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40651	Order of Possession for Temporary Rights	REO40649	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40653	Conduct Investigations	REO40651	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40655	Property Valuations, Plat Map & Description	REO40653	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40657	Land Owner Negotiations	REO40655	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40659	Offer to Sell Executed	REO40657	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40661	Amend DT for Permanent Construction Access	REO40659	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40663	Order of Possession for Construction	REO40661	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.13 (2025-5) RGV-HRL-3			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.13.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40665	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40667	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40669	CBP Signature on DT	REO40667	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40671	File DT for Temporary Taking	REO40667	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40673	Order of Possession for Temporary Rights	REO40671	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40675	Conduct Investigations	REO40673	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40677	Property Valuations, Plat Map & Description	REO40675	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40679	Land Owner Negotiations	REO40677	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40681	Offer to Sell Executed	REO40679	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40683	Amend DT for Permanent Construction Access	REO40681	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40685	Order of Possession for Construction	REO40683	0.0d	0.0d	0%				15-Jul-08
143 75.90000.150.09.14 (2026-1) RGV-HRL-4			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.14.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40687	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40689	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40691	CBP Signature on DT	REO40689	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40693	File DT for Temporary Taking	REO40689	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08

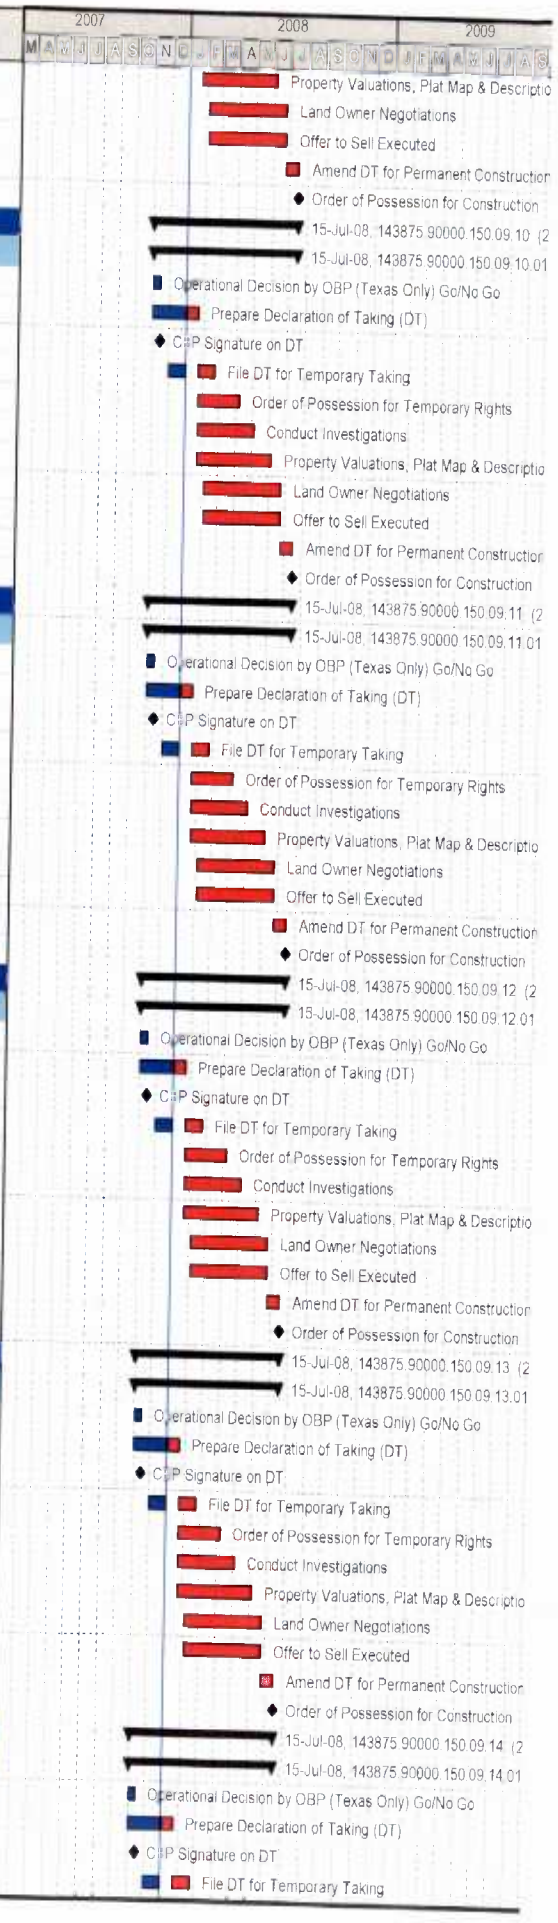

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40695	Order of Possession for Temporary Rights	REO40693	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40697	Conduct Investigations	REO40695	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40699	Property Valuations, Plat Map & Description	REO40697	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40701	Land Owner Negotiations	REO40699	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40703	Offer to Sell Executed	REO40701	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40705	Amend DT for Permanent Construction Access	REO40703	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40707	Order of Possession for Construction	REO40705	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.15 (2026-2) RGV-HRL-5			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.15.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40709	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40711	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40713	CBP Signature on DT	REO40711	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40715	File DT for Temporary Taking	REO40711	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40717	Order of Possession for Temporary Rights	REO40715	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40719	Conduct Investigations	REO40717	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40721	Property Valuations, Plat Map & Description	REO40719	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40723	Land Owner Negotiations	REO40721	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40725	Offer to Sell Executed	REO40723	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40727	Amend DT for Permanent Construction Access	REO40725	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40729	Order of Possession for Construction	REO40727	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.16 (2026-3) RGV-HRL-6			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.16.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40731	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40733	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40735	CBP Signature on DT	REO40733	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40737	File DT for Temporary Taking	REO40733	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40739	Order of Possession for Temporary Rights	REO40737	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40741	Conduct Investigations	REO40739	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40743	Property Valuations, Plat Map & Description	REO40741	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40745	Land Owner Negotiations	REO40743	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40747	Offer to Sell Executed	REO40745	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40749	Amend DT for Permanent Construction Access	REO40747	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40751	Order of Possession for Construction	REO40749	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.17 (2026-4) RGV-BRP-1			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.17.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40753	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40755	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40757	CBP Signature on DT	REO40755	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40759	File DT for Temporary Taking	REO40755	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40761	Order of Possession for Temporary Rights	REO40759	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40763	Conduct Investigations	REO40761	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40765	Property Valuations, Plat Map & Description	REO40763	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40767	Land Owner Negotiations	REO40765	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40769	Offer to Sell Executed	REO40767	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40771	Amend DT for Permanent Construction Access	REO40769	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40773	Order of Possession for Construction	REO40771	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.18 (2026-5) RGV-BRP-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.18.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40775	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40777	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40779	CBP Signature on DT	REO40777	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40781	File DT for Temporary Taking	REO40777	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40783	Order of Possession for Temporary Rights	REO40781	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40785	Conduct Investigations	REO40783	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40787	Property Valuations, Plat Map & Description	REO40785	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40789	Land Owner Negotiations	REO40787	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40791	Offer to Sell Executed	REO40789	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40793	Amend DT for Permanent Construction Access	REO40791	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40795	Order of Possession for Construction	REO40793	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.19 (2026-6) RGV-BRP-3			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.19.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40797	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40799	Prepare Declaration of Taking (DT)		19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08

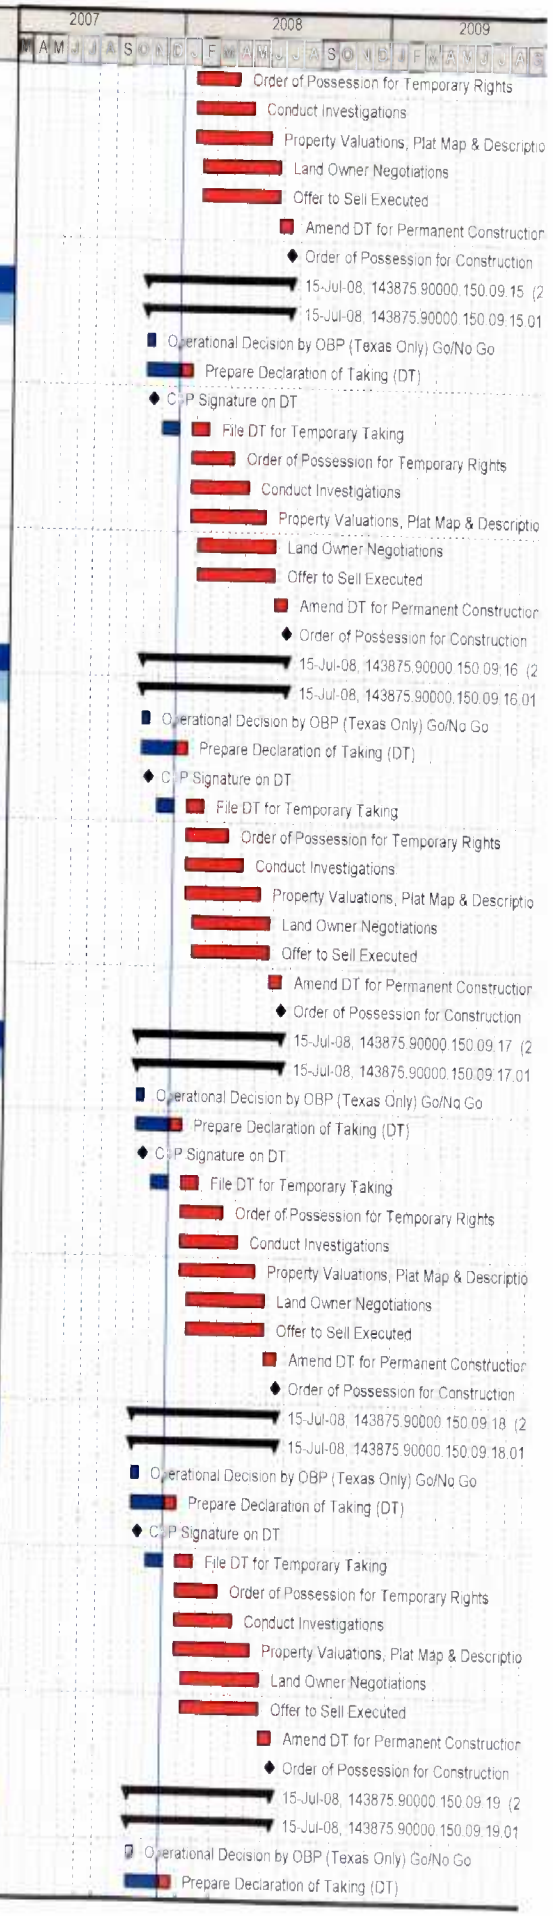

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
REO40801	CBP Signature on DT	REO40799	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40803	File DT for Temporary Taking	REO40799	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40805	Order of Possession for Temporary Rights	REO40803	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40807	Conduct Investigations	REO40805	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40809	Property Valuations, Plat Map & Description	REO40807	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40811	Land Owner Negotiations	REO40809	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40813	Offer to Sell Executed	REO40811	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40815	Amend DT for Permanent Construction Access	REO40813	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40817	Order of Possession for Construction	REO40815	0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.20 (2027-1) RGV-BRP-4			175.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.20.01 No Voluntary ROE-SE			175.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40819	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40821	Prepare Declaration of Taking (DT)	REO40821	19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40823	CBP Signature on DT	REO40821	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40825	File DT for Temporary Taking	REO40825	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40827	Order of Possession for Temporary Rights	REO40827	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40829	Conduct Investigations	REO40829	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40831	Property Valuations, Plat Map & Description	REO40831	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40833	Land Owner Negotiations	REO40833	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40835	Offer to Sell Executed	REO40835	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40837	Amend DT for Permanent Construction Access	REO40837	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40839	Order of Possession for Construction		0.0d	0.0d	0%				15-Jul-08
143875.90000.150.09.21 (2027-2) RGV-FTB-2			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
143875.90000.150.09.21.01 No Voluntary ROE-SE			156.0d	136.0d		02-Nov-07	02-Nov-07 A		15-Jul-08
REO40841	Operational Decision by OBP (Texas Only) Go/No Go		9.0d	0.0d	100%	02-Nov-07	02-Nov-07 A	15-Nov-07	15-Nov-07 A
REO40843	Prepare Declaration of Taking (DT)	REO40843	19.0d	15.0d	100%	02-Nov-07	02-Nov-07 A		23-Jan-08
REO40845	CBP Signature on DT	REO40843	0.0d	0.0d	100%	15-Nov-07	15-Nov-07 A		
REO40847	File DT for Temporary Taking	REO40847	22.0d	21.0d	0%	30-Nov-07	30-Nov-07 A		22-Feb-08
REO40849	Order of Possession for Temporary Rights	REO40849	53.0d	53.0d	0%		24-Jan-08		08-Apr-08
REO40851	Conduct Investigations	REO40851	73.0d	73.0d	0%		24-Jan-08		06-May-08
REO40853	Property Valuations, Plat Map & Description	REO40853	95.0d	95.0d	0%		24-Jan-08		06-Jun-08
REO40855	Land Owner Negotiations	REO40855	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40857	Offer to Sell Executed	REO40857	99.0d	99.0d	0%		05-Feb-08		24-Jun-08
REO40859	Amend DT for Permanent Construction Access	REO40859	14.0d	14.0d	0%		25-Jun-08		15-Jul-08
REO40861	Order of Possession for Construction		0.0d	0.0d	0%				15-Jul-08
143875.95000 Environmental Compliance (CBP 1745-7000-2)			381.0d	123.0d		06-Mar-07	06-Mar-07 A		25-Jun-08
143875.95000.001 Environmental Project Management			381.0d	123.0d		06-Mar-07	06-Mar-07 A		25-Jun-08
ENV2000	ENV IPT Technical Assistance		550.0d	144.0d	38%	06-Mar-07	06-Mar-07 A		24-May-08
ENV1000	Program Management and Oversight-SWF		100.0d	144.0d	25%	02-Apr-07	02-Apr-07 A		24-May-08
ENV2005	ITR & Coordination - SPL		183.0d	144.0d	24%	01-Jun-07	01-Jun-07 A		24-May-08
ENV2010	Program Management and Oversight - Baker		366.0d	144.0d	26%	01-Aug-07	01-Aug-07 A		24-May-08
ENV1010	Program Management and Oversight-SPL		160.0d	144.0d	27%	01-Aug-07	01-Aug-07 A		24-May-08
ENV1005	Program Management and Oversight-SWG		160.0d	144.0d	30%	01-Sep-07	01-Sep-07 A		24-May-08
ENV1015	Program Management and Oversight-SPA		100.0d	144.0d	31%	01-Sep-07	01-Sep-07 A		24-May-08
ENV1017	Program Management and Oversight-SWT		100.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	30-Nov-07	30-Nov-07 A
ENV2012	Travel for E2M - Phase 2		144.0d	144.0d	30%	01-Nov-07	01-Nov-07 A		24-May-08
ENV2014	E2M Contract		80.0d	144.0d	0%	01-Nov-07	01-Nov-07 A		24-May-08
ENV2016	Environmental Intern - SWG		120.0d	120.0d	0%		07-Jan-08*		25-Jun-08
143875.95000.002 Environmental Site Assessments			13.0d	13.0d			02-Jan-08		21-Jan-08
143875.95000.002.001 SDC			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18592	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18594	Draft Site Assessment	ENV18592	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18596	Document Review	ENV18594	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18598	Final Site Assessment	ENV18596	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18600	Accepted by CBP	ENV18598	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18602	Contract Award	ENV18600	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.002 ELC			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18604	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18606	Draft Site Assessment	ENV18604	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18608	Document Review	ENV18606	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18610	Final Site Assessment	ENV18608	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18612	Accepted by CBP	ENV18610	1.0d	1.0d	0%		16-Jan-08		16-Jan-08

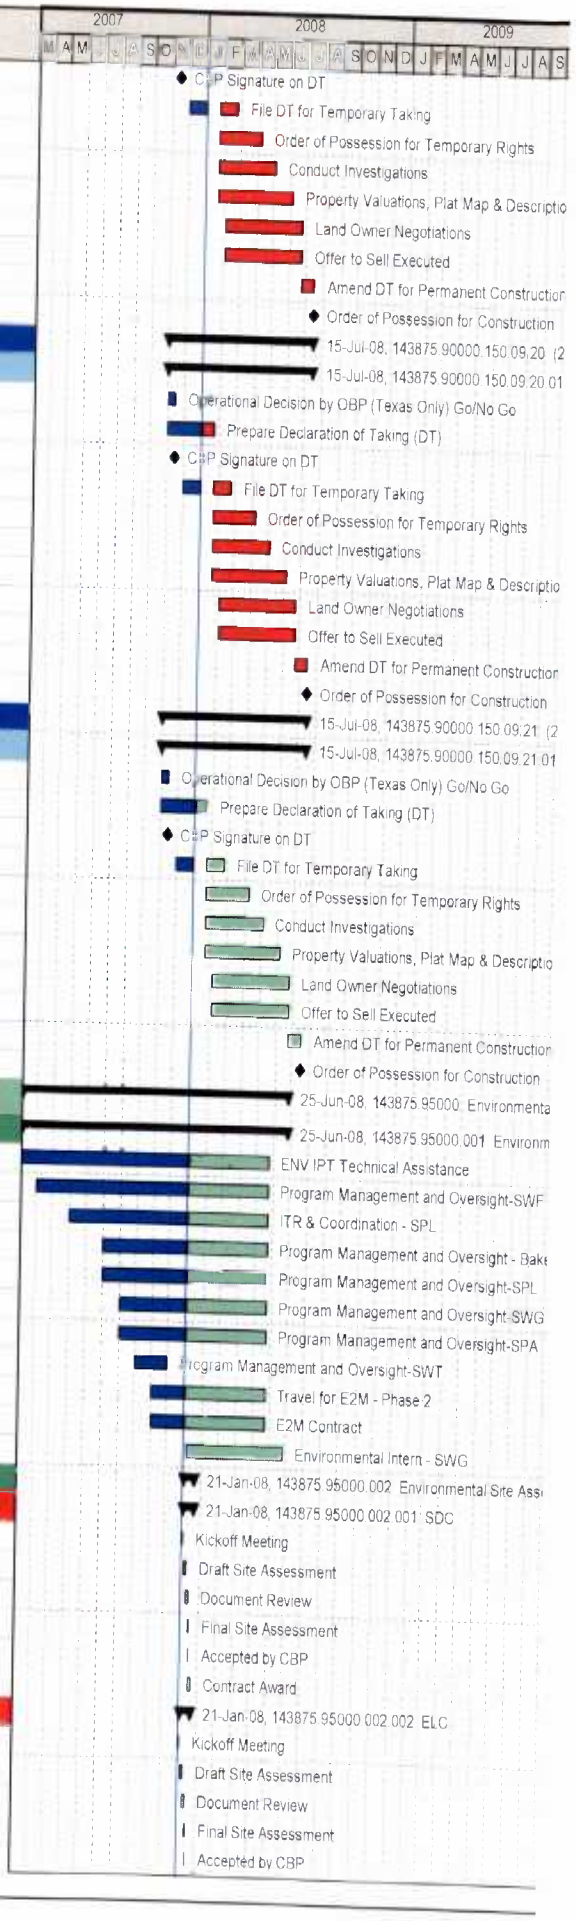

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV18614	Contract Award	ENV18612	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.003 YUM			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18628	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18630	Draft Site Assessment	ENV18628	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18632	Document Review	ENV18630	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18634	Final Site Assessment	ENV18632	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18636	Accepted by CBP	ENV18634	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18638	Contract Award	ENV18636	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.004 TCA			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18616	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18618	Draft Site Assessment	ENV18616	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18620	Document Review	ENV18618	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18622	Final Site Assessment	ENV18620	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18624	Accepted by CBP	ENV18622	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18626	Contract Award	ENV18624	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.005 EPT			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18640	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18642	Draft Site Assessment	ENV18640	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18644	Document Review	ENV18642	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18646	Final Site Assessment	ENV18644	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18648	Accepted by CBP	ENV18646	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18650	Contract Award	ENV18648	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.006 MAR			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18652	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18654	Draft Site Assessment	ENV18652	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18656	Document Review	ENV18654	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18658	Final Site Assessment	ENV18656	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18660	Accepted by CBP	ENV18658	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18662	Contract Award	ENV18660	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.007 DRT			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18664	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18666	Draft Site Assessment	ENV18664	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18668	Document Review	ENV18666	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18670	Final Site Assessment	ENV18668	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18672	Accepted by CBP	ENV18670	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18674	Contract Award	ENV18672	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.002.008 RGV			13.0d	13.0d			02-Jan-08		21-Jan-08
ENV18676	Kickoff Meeting		2.0d	2.0d	0%		02-Jan-08		03-Jan-08
ENV18678	Draft Site Assessment	ENV18676	5.0d	5.0d	0%		04-Jan-08		08-Jan-08
ENV18680	Document Review	ENV18678	5.0d	5.0d	0%		09-Jan-08		13-Jan-08
ENV18682	Final Site Assessment	ENV18680	2.0d	2.0d	0%		14-Jan-08		15-Jan-08
ENV18684	Accepted by CBP	ENV18682	1.0d	1.0d	0%		16-Jan-08		16-Jan-08
ENV18686	Contract Award	ENV18684	5.0d	5.0d	0%		17-Jan-08		21-Jan-08
143875.95000.003 Environmental Cultural Resource Investigations			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.01 SDC			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.01.001 A-2			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18690	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.02 YUM			62.0d	62.0d			03-Jan-08		01-Apr-08
143875.95000.003.02.1 C-1/C-2			62.0d	62.0d			03-Jan-08		01-Apr-08
ENV18692	Cultural Resource Investigation		62.0d	62.0d	0%		03-Jan-08*		01-Apr-08
143875.95000.003.03 TCA			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.03.001 Sasabe			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18694	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.03.002 E-2a			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18696	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.03.003 D-5b			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18698	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.03.004 D-6			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18700	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.03.005 E-3			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18702	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.04 EPT			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.04.001 J-2			62.0d	62.0d			02-Jan-08		31-Mar-08

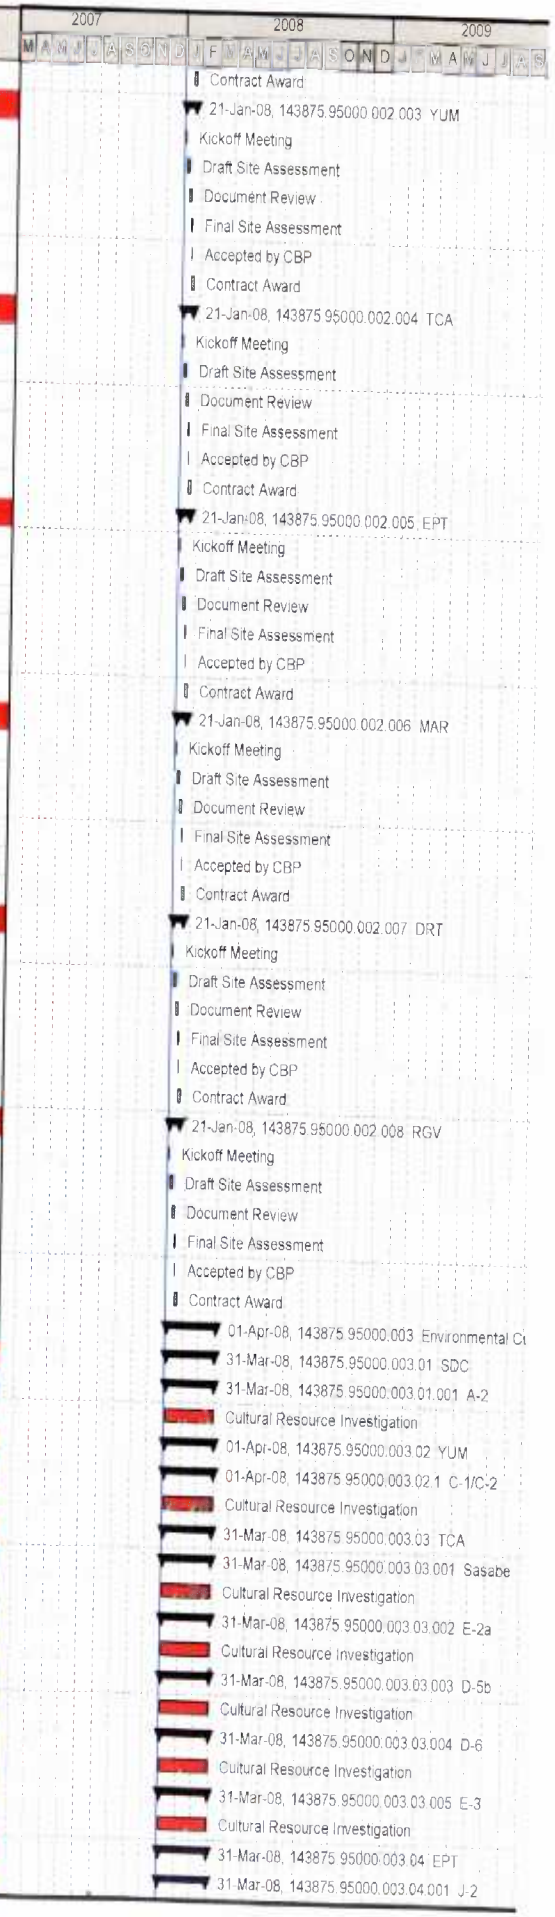

PF225
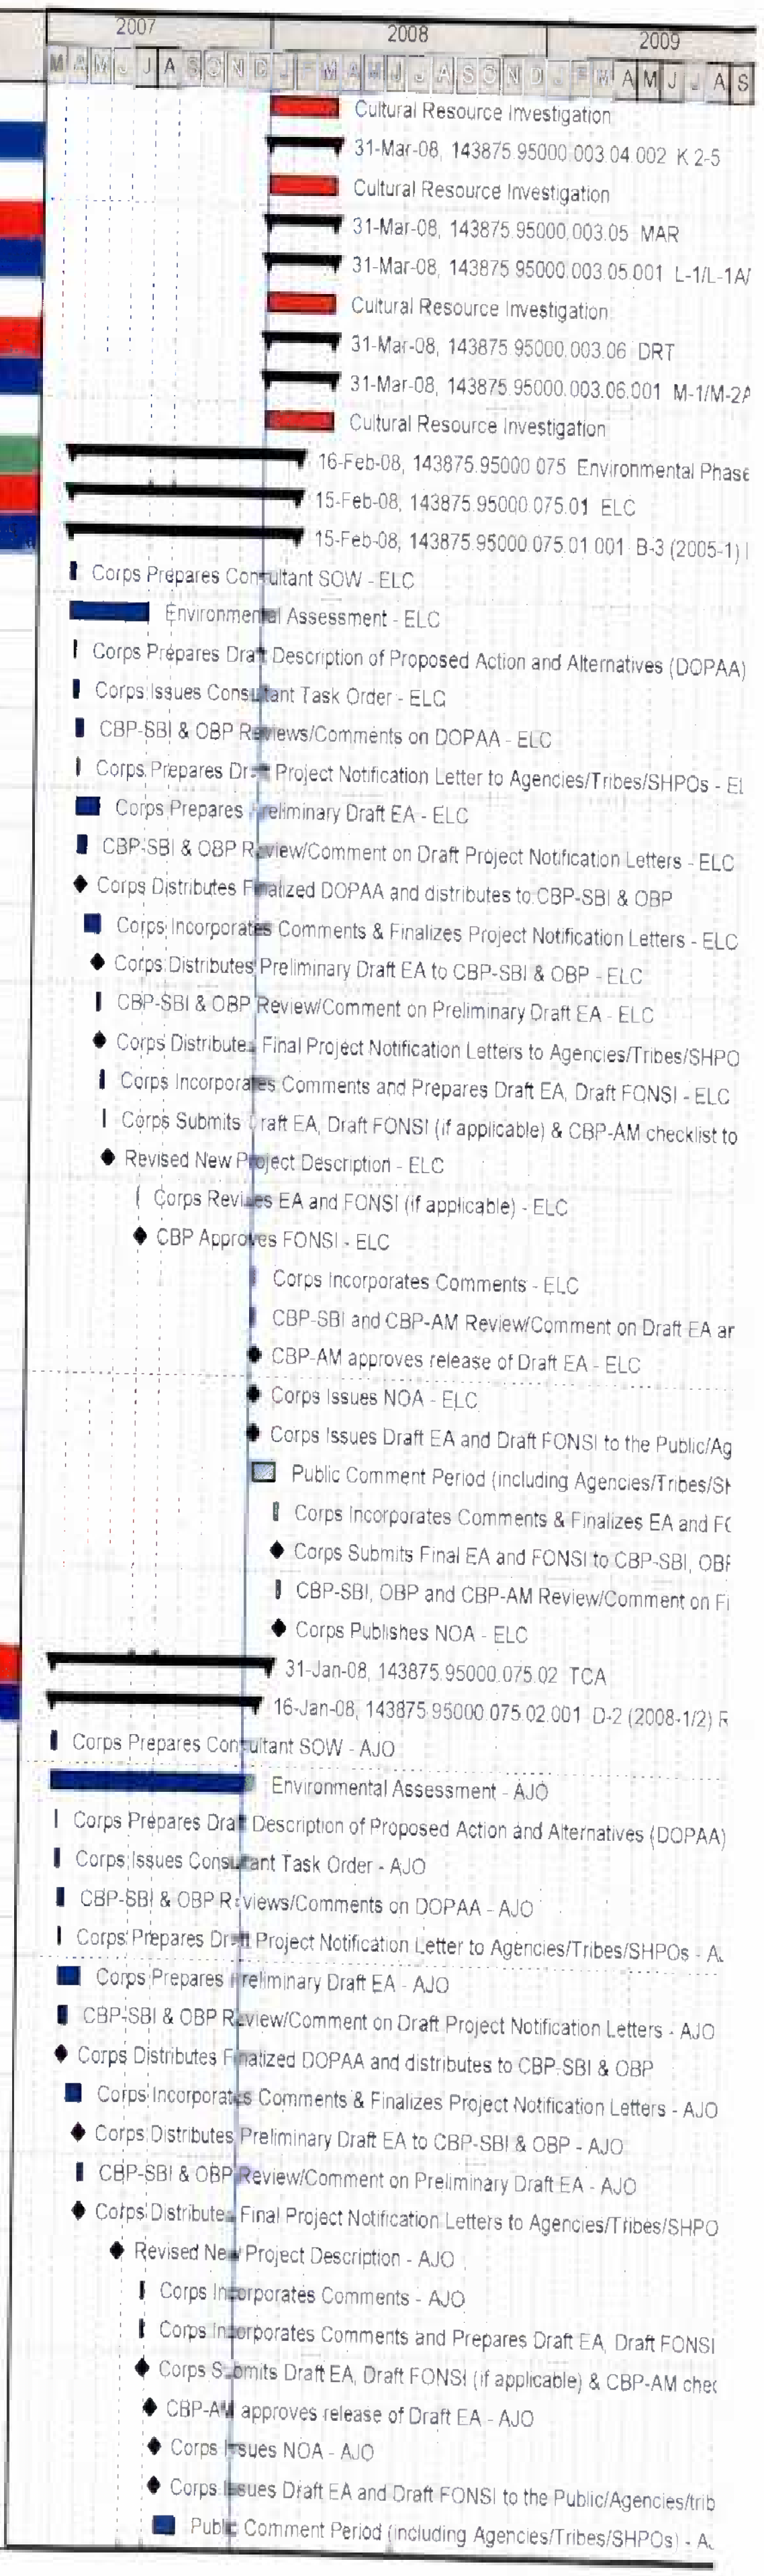
Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV18704	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.04.002 K 2-5			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18706	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.05 MAR			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.05.001 L-1/L-1A/L-1B			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18708	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.003.06 DRT			62.0d	62.0d			02-Jan-08		31-Mar-08
143875.95000.003.06.001 M-1/M-2A/M-2B			62.0d	62.0d			02-Jan-08		31-Mar-08
ENV18710	Cultural Resource Investigation		62.0d	62.0d	0%		02-Jan-08*		31-Mar-08
143875.95000.075 Environmental Phase I			209.0d	32.0d		18-Apr-07	18-Apr-07 A		15-Feb-08
143875.95000.075.01 ELC			209	32.0d		18-Apr-07	18-Apr-07 A		15-Feb-08
143875.95000.075.01.001 B-3 (2005-1)			209.0d	32.0d		18-Apr-07	18-Apr-07 A		15-Feb-08
ENV18450	Corps Prepares Consultant SOW - ELC		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV13320	Environmental Assessment - ELC		120.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	02-Aug-07	02-Aug-07 A
ENV18490	Corps Prepares Draft Description of Proposed Action and Alt...	ENV18475	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV18455	Corps Issues Consultant Task Order - ELC	ENV18450	5.0d	0.0d	100%	24-Apr-07	24-Apr-07 A	01-May-07	01-May-07 A
ENV18480	CBP-SBI & OBP Reviews/Comments on DOPAA - ELC	ENV18490	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV18460	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV18455	5.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV18500	Corps Prepares Preliminary Draft EA - ELC	ENV18495	35.0d	0.0d	100%	01-May-07	01-May-07 A	30-May-07	30-May-07 A
ENV18465	CBP-SBI & OBP Review/Comment on Draft Project Notificati...	ENV18460	5.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV18495	Corps Distributes Finalized DOPAA and distributes to CBP-S...	ENV18490	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV18470	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV18460	5.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV18505	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV18500	0.0d	0.0d	100%			01-Jun-07	01-Jun-07 A
ENV18510	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV18505	5.0d	0.0d	100%	01-Jun-07	01-Jun-07 A	06-Jun-07	06-Jun-07 A
ENV18475	Corps Distributes Final Project Notification Letters to Agencie...	ENV18470	0.0d	0.0d	100%			04-Jun-07	04-Jun-07 A
ENV18515	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV18510	5.0d	0.0d	100%	07-Jun-07	07-Jun-07 A	12-Jun-07	12-Jun-07 A
ENV18520	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV18515	2.0d	0.0d	100%	13-Jun-07	13-Jun-07 A	15-Jun-07	15-Jun-07 A
ENV18580	Revised New Project Description - ELC		0.0d	0.0d	100%			19-Jun-07	19-Jun-07 A
ENV18565	Corps Revises EA and FONSI (if applicable) - ELC	ENV18560	5.0d	0.0d	100%	30-Jul-07	30-Jul-07 A	30-Jul-07	30-Jul-07 A
ENV18570	CBP Approves FONSI - ELC	ENV18565	0.0d	0.0d	100%			02-Aug-07	02-Aug-07 A
ENV18485	Corps Incorporates Comments - ELC	ENV18490	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV18525	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV18520	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV18530	CBP-AM approves release of Draft EA - ELC	ENV18525	0.0d	0.0d	0%				06-Jan-08
ENV18535	Corps Issues NOA - ELC	ENV18530	0.0d	0.0d	0%				06-Jan-08
ENV18540	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV18535	0.0d	0.0d	0%				06-Jan-08
ENV18545	Public Comment Period (including Agencies/Tribes/SHPOs) - ...	ENV18540	30.0d	30.0d	0%		07-Jan-08		05-Feb-08
ENV18550	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV18545	5.0d	5.0d	0%		06-Feb-08		10-Feb-08
ENV18555	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV18550	0.0d	0.0d	0%				10-Feb-08
ENV18560	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV18555	5.0d	5.0d	0%		11-Feb-08		15-Feb-08
ENV18575	Corps Publishes NOA - ELC	ENV18570	0.0d	0.0d	0%				15-Feb-08
143875.95000.075.02 TCA			198.0d	21.0d		18-Apr-07	18-Apr-07 A		31-Jan-08
143875.95000.075.02.001 D-2 (2008-1/2) RFP#1 (5.20 Miles) SEA Ajo Station			[illegible]	11.0d		1[illegible]-Apr-07	1[illegible]-Apr-07 A		16-Jan-08
ENV16630	Corps Prepares Consultant SOW - AJO		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV10180	Environmental Assessment - AJO		120.0d	15.0d	95%	18-Apr-07	18-Apr-07 A		16-Jan-08
ENV16660	Corps Prepares Draft Description of Proposed Action and Alt...	ENV16655	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV16635	Corps Issues Consultant Task Order - AJO	ENV16630	5.0d	0.0d	100%	24-Apr-07	24-Apr-07 A	01-May-07	01-May-07 A
ENV16665	CBP-SBI & OBP Reviews/Comments on DOPAA - AJO	ENV16660	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV16640	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV16635	5.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV16680	Corps Prepares Preliminary Draft EA - AJO	ENV16675	35.0d	0.0d	100%	01-May-07	01-May-07 A	30-May-07	30-May-07 A
ENV16645	CBP-SBI & OBP Review/Comment on Draft Project Notificati...	ENV16640	5.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV16675	Corps Distributes Finalized DOPAA and distributes to CBP-S...	ENV16660	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV16650	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV16640	5.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV16685	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV16680	0.0d	0.0d	100%			01-Jun-07	01-Jun-07 A
ENV16690	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV16685	5.0d	0.0d	100%	01-Jun-07	01-Jun-07 A	08-Jun-07	08-Jun-07 A
ENV16655	Corps Distributes Final Project Notification Letters to Agencie...	ENV16650	0.0d	0.0d	100%			04-Jun-07	04-Jun-07 A
ENV18585	Revised New Project Description - AJO		0.0d	0.0d	100%			25-Jul-07	25-Jul-07 A
ENV16670	Corps Incorporates Comments - AJO	ENV16660	5.0d	0.0d	100%	26-Aug-07	26-Aug-07 A	30-Aug-07	30-Aug-07 A
ENV16695	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV16690	5.0d	0.0d	100%	26-Aug-07	26-Aug-07 A	30-Aug-07	30-Aug-07 A
ENV16700	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV16695	0.0d	0.0d	100%			30-Aug-07	30-Aug-07 A
ENV16710	CBP-AM approves release of Draft EA - AJO	ENV16705	0.0d	0.0d	100%			11-Sep-07	11-Sep-07 A
ENV16715	Corps Issues NOA - AJO	ENV16710	0.0d	0.0d	100%			17-Sep-07	17-Sep-07 A
ENV16720	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV16715	0.0d	0.0d	100%			17-Sep-07	17-Sep-07 A
ENV16725	Public Comment Period (including Agencies/Tribes/SHPOs) - ...	ENV16720	30.0d	0.0d	100%	17-Sep-07	17-Sep-07 A	16-Oct-07	16-Oct-07 A
