PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV16705	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV16700	5.0d	0.0d	100%	20-Nov-07	20-Nov-07 A	27-Nov-07	27-Nov-07 A
ENV16730	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV16725	5.0d	0.0d	100%	20-Nov-07	20-Nov-07 A	27-Nov-07	27-Nov-07 A
ENV16735	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV16730	0.0d	0.0d	100%			29-Nov-07	29-Nov-07 A
ENV16740	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV16735	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV16745	Corps Revises EA and FONSI (if applicable) - AJO	ENV16740	5.0d	5.0d	0%		07-Jan-08		11-Jan-08
ENV16750	CBP Approves FONSI - AJO	ENV16745	0.0d	0.0d	0%				11-Jan-08
ENV16755	Corps Publishes NOA - AJO	ENV16750	0.0d	0.0d	0%				11-Jan-08
143875.95000.075.02.002 E-2A/2B/3 (2011-1/2) RFP#2B/3 (22.86 Miles) SEA Naco Station			197.0d	21.0d		18-Apr-07*	18-Apr-07 A		31-Jan-08
ENV13990	NCO/DGL FONSI Signed 19-NOV-2003		0.0d	0.0d	100%			18-Apr-07	18-Apr-07 A
ENV14000	Biological Assessment Phase 1		30.0d	15.0d	100%	01-Aug-07	01-Aug-07 A		16-Jan-08
ENV13995	Limestone Supplemetal SEA		122.0d	30.0d	75%	01-Sep-07	01-Sep-07 A		31-Jan-08
ENV14007	Add'l Cultural/Arch Work		30.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	30-Nov-07	30-Nov-07 A
ENV14005	Biological Assessment Phase 2		30.0d	30.0d	0%		02-Jan-08*		31-Jan-08
143875.95000.075.02.003 F-1 (2012-1) RFP#4 (2.42 Miles) SEA Douglas Station			0.0d	0.0d		18-Apr-07	18-Apr-07 A	18-Apr-07	18-Apr-07 A
ENV13630	NCO/DGL FONSI Signed 19-NOV-2003		0.0d	0.0d	100%			18-Apr-07	18-Apr-07 A
143875.95000.075.02.004 D-5A (2010-1) RFP#1B (2.00 Miles) SEA Nogales Station			169.0d	0.0d		18-Apr-07	18-Apr-07 A	19-Nov-07	19-Nov-07 A
ENV16760	Corps Prepares Consultant SOW - NGL		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV13820	Environmental Assessment - NGL		120.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	19-Nov-07	19-Nov-07 A
ENV16790	Corps Prepares Draft Description of Proposed Action and Alt...	ENV16785	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV16765	Corps Issues Consultant Task Order - NGL	ENV16760	5.0d	0.0d	100%	24-Apr-07	24-Apr-07 A	01-May-07	01-May-07 A
ENV16800	Corps Incorporates Comments - NGL	ENV16790	5.0d	0.0d	100%	26-Apr-07	26-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV16795	CBP-SBI & OBP Reviews/Comments on DOPAA - NGL	ENV16790	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV16770	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV16765	5.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV16810	Corps Prepares Preliminary Draft EA - NGL	ENV16805	35.0d	0.0d	100%	01-May-07	01-May-07 A	22-May-07	22-May-07 A
ENV16775	CBP-SBI & OBP Review/Comment on Draft Project Notificati...	ENV16770	5.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV16805	Corps Distributes Finalized DOPAA and distributes to CBP-S...	ENV16790	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV16780	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV16770	5.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV16815	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV16810	0.0d	0.0d	100%			23-May-07	23-May-07 A
ENV16820	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV16815	5.0d	0.0d	100%	23-May-07	23-May-07 A	29-May-07	29-May-07 A
ENV16825	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV16820	5.0d	0.0d	100%	30-May-07	30-May-07 A	05-Jun-07	05-Jun-07 A
ENV16785	Corps Distributes Final Project Notification Letters to Agencie...	ENV16780	0.0d	0.0d	100%			04-Jun-07	04-Jun-07 A
ENV18590	Revised New Project Description - NGL		0.0d	0.0d	100%			20-Jul-07	20-Jul-07 A
ENV16830	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV16825	0.0d	0.0d	100%			17-Aug-07	17-Aug-07 A
ENV16835	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV16830	22.0d	0.0d	100%	20-Aug-07	20-Aug-07 A	10-Sep-07	10-Sep-07 A
ENV16840	CBP-AM approves release of Draft EA - NGL	ENV16835	0.0d	0.0d	100%			11-Sep-07	11-Sep-07 A
ENV16845	Corps Issues NOA - NGL	ENV16840	0.0d	0.0d	100%			17-Sep-07	17-Sep-07 A
ENV16850	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV16845	0.0d	0.0d	100%			17-Sep-07	17-Sep-07 A
ENV16855	Public Comment Period (including Agencies/Tribes/SHPOs) - ...	ENV16850	30.0d	0.0d	100%	17-Sep-07	17-Sep-07 A	16-Oct-07	16-Oct-07 A
ENV16860	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV16855	5.0d	0.0d	100%	17-Oct-07	17-Oct-07 A	24-Oct-07	24-Oct-07 A
ENV16865	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV16860	0.0d	0.0d	100%			24-Oct-07	24-Oct-07 A
ENV16870	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV16865	5.0d	0.0d	100%	25-Oct-07	25-Oct-07 A	31-Oct-07	31-Oct-07 A
ENV16880	CBP Approves FONSI - NGL	ENV16870	13.0d	0.0d	100%	01-Nov-07	01-Nov-07 A	14-Nov-07	14-Nov-07 A
ENV16885	Corps Publishes NOA - NGL	ENV16880	5.0d	0.0d	100%	15-Nov-07	15-Nov-07 A	19-Nov-07	19-Nov-07 A
143875.95000.075.03 EPT			209.0d	32.0d		18-Apr-07	18-Apr-07 A		16-Feb-08
143875.95000.075.03.001 H-2B/I-1A (2013-1/2) RFP#N/A/5 (2.50 Miles) SEA Deming Station			209.0d	32.0d		18-Apr-07	18-Apr-07 A		16-Feb-08
ENV16890	Corps Prepares Consultant SOW - DNM		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV14180	Environmental Assessment - DNM		120.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	24-Jul-07	24-Jul-07 A
ENV16920	Corps Prepares Draft Description of Proposed Action and Alt...	ENV16915	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV16895	Corps Issues Consultant Task Order - DNM	ENV16890	5.0d	0.0d	100%	24-Apr-07	24-Apr-07 A	01-May-07	01-May-07 A
ENV16925	CBP-SBI & OBP Reviews/Comments on DOPAA - DNM	ENV16920	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV16900	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV16895	5.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV16940	Corps Prepares Preliminary Draft EA - DNM	ENV16935	35.0d	0.0d	100%	01-May-07	01-May-07 A	15-May-07	15-May-07 A
ENV16905	CBP-SBI & OBP Review/Comment on Draft Project Notificat...	ENV16900	5.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV16935	Corps Distributes Finalized DOPAA and distributes to CBP-S...	ENV16920	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV16910	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV16900	5.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV16945	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV16940	0.0d	0.0d	100%			16-May-07	16-May-07 A
ENV16950	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV16945	5.0d	0.0d	100%	16-May-07	16-May-07 A	23-May-07	23-May-07 A
ENV16955	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV16950	5.0d	0.0d	100%	24-May-07	24-May-07 A	29-May-07	29-May-07 A
ENV16915	Corps Distributes Final Project Notification Letters to Agencie...	ENV16910	0.0d	0.0d	100%			04-Jun-07	04-Jun-07 A
ENV17005	Corps Revises EA and FONSI (if applicable) - DNM	ENV17000	0.0d	0.0d	100%			18-Jul-07	18-Jul-07 A
ENV17010	CBP Approves FONSI - DNM	ENV17005	5.0d	0.0d	100%	19-Jul-07	19-Jul-07 A	24-Jul-07	24-Jul-07 A
ENV16930	Corps Incorporates Comments - DNM	ENV16920	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV16960	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV16955	0.0d	0.0d	0%				02-Jan-08

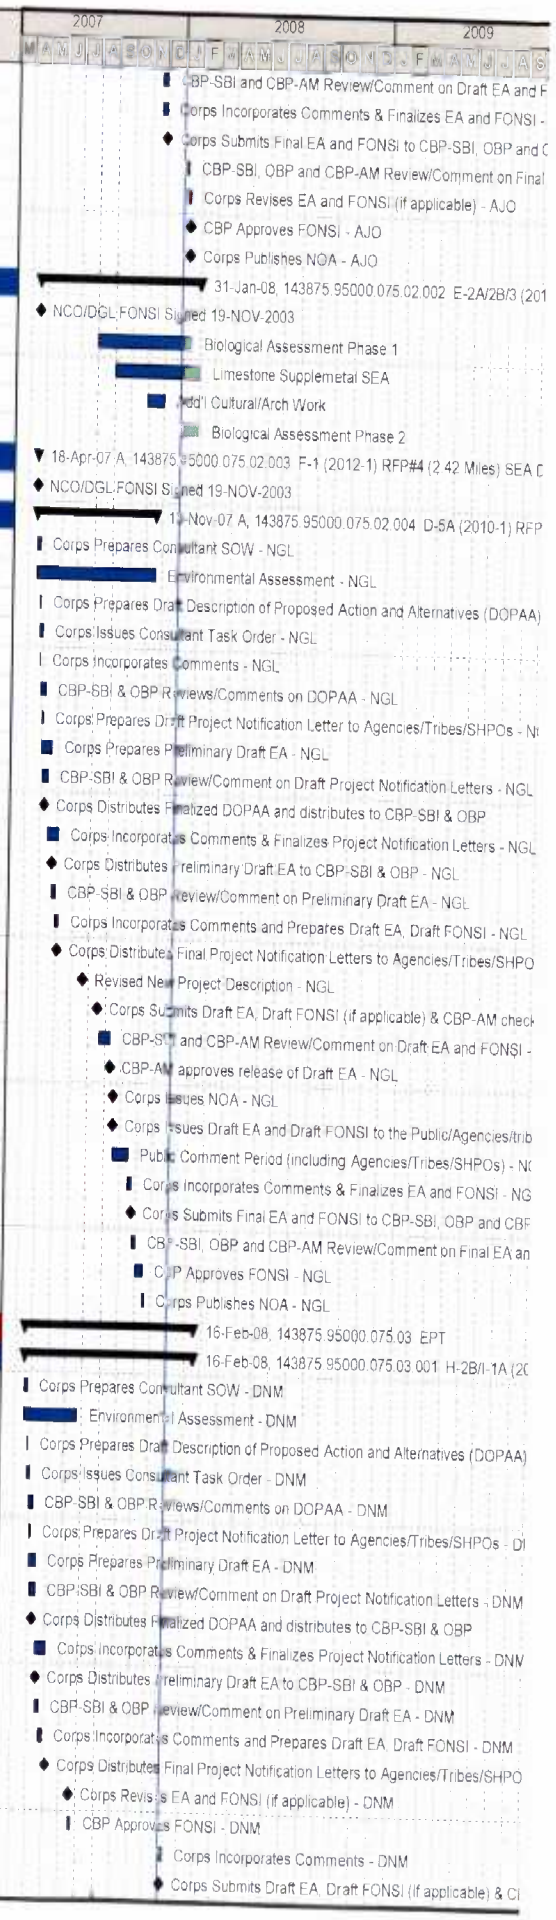

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV16965	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV16960	5.0d	5.0d	0%		02-Jan-08		07-Jan-08
ENV16970	CBP-AM approves release of Draft EA - DNM	ENV16965	0.0d	0.0d	0%				07-Jan-08
ENV16975	Corps Issues NOA - DNM	ENV16970	0.0d	0.0d	0%				07-Jan-08
ENV16980	Corps Issues Draft EA and Draft FONSI to the Public/Agenci	ENV16975	0.0d	0.0d	0%				07-Jan-08
ENV16985	Public Comment Period (including Agencies/Tribes/SHPOs) -	ENV16980	30.0d	30.0d	0%		07-Jan-08		06-Feb-08
ENV16990	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV16985	5.0d	5.0d	0%		06-Feb-08		11-Feb-08
ENV16995	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV16990	0.0d	0.0d	0%				11-Feb-08
ENV17000	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV16995	5.0d	5.0d	0%		11-Feb-08		16-Feb-08
ENV17015	Corps Publishes NOA - DNM	ENV17010	0.0d	0.0d	0%				16-Feb-08
143875.95000.075.03.002 J-1/2/3 (2014-1/2/3) RFP#6 (3.29 Miles) SEA Santa Theresa Station			170.0d	0.0d		18-Apr-07	18-Apr-07 A	20-Nov-07	20-Nov-07 A
ENV17020	Corps Prepares Consultant SOW - STN		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV14540	Environmental Assessment - STN		120.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	20-Nov-07	20-Nov-07 A
ENV17050	Corps Prepares Draft Description of Proposed Action and Alt...	ENV17045	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV17025	Corps Issues Consultant Task Order - STN	ENV17020	5.0d	0.0d	100%	24-Apr-07	24-Apr-07 A	01-May-07	01-May-07 A
ENV17055	CBP-SBI & OBP Reviews/Comments on DOPAA - STN	ENV17050	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV17030	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV17025	0.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV17070	Corps Prepares Preliminary Draft EA - STN	ENV17065	35.0d	0.0d	100%	01-May-07	01-May-07 A	22-May-07	22-May-07 A
ENV17060	Corps Incorporates Comments - STN	ENV17050	5.0d	0.0d	100%	03-May-07	03-May-07 A	07-May-07	07-May-07 A
ENV17035	CBP-SBI & OBP Review/Comment on Draft Project Notificati...	ENV17030	0.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV17065	Corps Distributes Finalized DOPAA and distributes to CBP-S...	ENV17050	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV17040	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV17030	0.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV17075	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV17070	0.0d	0.0d	100%			23-May-07	23-May-07 A
ENV17080	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV17075	5.0d	0.0d	100%	23-May-07	23-May-07 A	30-Jun-07	30-Jun-07 A
ENV17085	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV17080	5.0d	0.0d	100%	01-Jun-07	01-Jun-07 A	06-Jun-07	06-Jun-07 A
ENV17086	Revised New Project Description 6/29		0.0d	0.0d	100%			29-Jun-07	29-Jun-07 A
ENV17045	Corps Distributes Final Project Notification Letters to Agencie...	ENV17040	0.0d	0.0d	100%			04-Jul-07	04-Jul-07 A
ENV17090	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV17085	0.0d	0.0d	100%			24-Aug-07	24-Aug-07 A
ENV17095	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV17090	5.0d	0.0d	100%	24-Aug-07	24-Aug-07 A	27-Aug-07	27-Aug-07 A
ENV17100	CBP-AM approves release of Draft EA - STN	ENV17095	0.0d	0.0d	100%			28-Aug-07	28-Aug-07 A
ENV17105	Corps Issues NOA - STN	ENV17100	0.0d	0.0d	100%			04-Sep-07	04-Sep-07 A
ENV17110	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV17105	0.0d	0.0d	100%			04-Sep-07	04-Sep-07 A
ENV17115	Public Comment Period (including Agencies/Tribes/SHPOs) -	ENV17110	30.0d	0.0d	100%	04-Sep-07	04-Sep-07 A	03-Oct-07	03-Oct-07 A
ENV17120	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV17115	5.0d	0.0d	100%	04-Oct-07	04-Oct-07 A	11-Oct-07	11-Oct-07 A
ENV17125	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV17120	0.0d	0.0d	100%			11-Oct-07	11-Oct-07 A
ENV17130	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV17125	5.0d	0.0d	100%	12-Oct-07	12-Oct-07 A	19-Oct-07	19-Oct-07 A
ENV17140	CBP Approves FONSI - STN	ENV17130	13.0d	0.0d	100%	01-Nov-07	01-Nov-07 A	14-Nov-07	14-Nov-07 A
ENV17145	Corps Publishes NOA - STN	ENV17140	6.0d	0.0d	100%	13-Nov-07	13-Nov-07 A	20-Nov-07	20-Nov-07 A
143875.95000.075.03.003 K-1 (2015-1/2/3) RFP#7 (3.09 Miles) SEA El Paso Station			188.0d	13.0d		18-Apr-07	18-Apr-07 A		21-Jan-08
ENV17150	Corps Prepares Consultant SOW - EPT		10.0d	0.0d	100%	18-Apr-07	18-Apr-07 A	23-Apr-07	23-Apr-07 A
ENV14360	Environmental Assessment - EPT		120.0d	20.0d	95%	18-Apr-07	18-Apr-07 A		21-Jan-08
ENV17180	Corps Prepares Draft Description of Proposed Action and Alt...	ENV17175	10.0d	0.0d	100%	23-Apr-07	23-Apr-07 A	27-Apr-07	27-Apr-07 A
ENV17185	CBP-SBI & OBP Reviews/Comments on DOPAA - EPT	ENV17180	5.0d	0.0d	100%	28-Apr-07	28-Apr-07 A	07-May-07	07-May-07 A
ENV17160	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV17155	5.0d	0.0d	100%	30-Apr-07	30-Apr-07 A	03-May-07	03-May-07 A
ENV17155	Corps Issues Consultant Task Order - EPT	ENV17150	5.0d	0.0d	100%	01-May-07	01-May-07 A	01-May-07	01-May-07 A
ENV17200	Corps Prepares Preliminary Draft EA - EPT	ENV17195	35.0d	0.0d	100%	01-May-07	01-May-07 A	24-May-07	24-May-07 A
ENV17165	CBP-SBI & OBP Review/Comment on Draft Project Notificati...	ENV17160	5.0d	0.0d	100%	04-May-07	04-May-07 A	15-May-07	15-May-07 A
ENV17195	Corps Distributes Finalized DOPAA and distributes to CBP-S	ENV17180	0.0d	0.0d	100%			08-May-07	08-May-07 A
ENV17170	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV17160	5.0d	0.0d	100%	15-May-07	15-May-07 A	03-Jun-07	03-Jun-07 A
ENV17205	Corps Distributes Preliminary Draft EA to CBP-SBI & OBP - ...	ENV17200	0.0d	0.0d	100%			25-May-07	25-May-07 A
ENV17210	CBP-SBI & OBP Review/Comment on Preliminary Draft EA - ...	ENV17205	5.0d	0.0d	100%	25-May-07	25-May-07 A	29-May-07	29-May-07 A
ENV17215	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV17210	5.0d	0.0d	100%	30-May-07	30-May-07 A	12-Jun-07	12-Jun-07 A
ENV17175	Corps Distributes Final Project Notification Letters to Agencie...	ENV17170	0.0d	0.0d	100%			04-Jun-07	04-Jun-07 A
ENV17216	Revised New Project Description 7/25		0.0d	0.0d	100%			25-Jul-07	25-Jul-07 A
ENV17230	CBP-AM approves release of Draft EA - EPT	ENV17225	0.0d	0.0d	100%			21-Aug-07	21-Aug-07 A
ENV17235	Corps Issues NOA - EPT	ENV17230	0.0d	0.0d	100%			27-Aug-07	27-Aug-07 A
ENV17240	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV17235	0.0d	0.0d	100%			27-Aug-07	27-Aug-07 A
ENV17245	Public Comment Period (including Agencies/Tribes/SHPOs) -	ENV17240	30.0d	0.0d	100%	27-Aug-07	27-Aug-07 A	26-Sep-07	26-Sep-07 A
ENV17250	Corps Incorporates Comments & Finalizes EA and FONSI - ...	ENV17245	5.0d	0.0d	100%	09-Nov-07	09-Nov-07 A	16-Nov-07	16-Nov-07 A
ENV17220	Corps Submits Draft EA, Draft FONSI (if applicable) & CBP-...	ENV17215	0.0d	0.0d	100%			26-Nov-07	26-Nov-07 A
ENV17255	Corps Submits Final EA and FONSI to CBP-SBI, OBP and C...	ENV17250	0.0d	0.0d	100%			27-Nov-07	27-Nov-07 A
ENV17190	Corps Incorporates Comments - EPT	ENV17180	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV17225	CBP-SBI and CBP-AM Review/Comment on Draft EA and F...	ENV17220	5.0d	5.0d	0%		02-Jan-08		06-Jan-08
ENV17260	CBP-SBI, OBP and CBP-AM Review/Comment on Final EA ...	ENV17255	5.0d	5.0d	0%		07-Jan-08		11-Jan-08

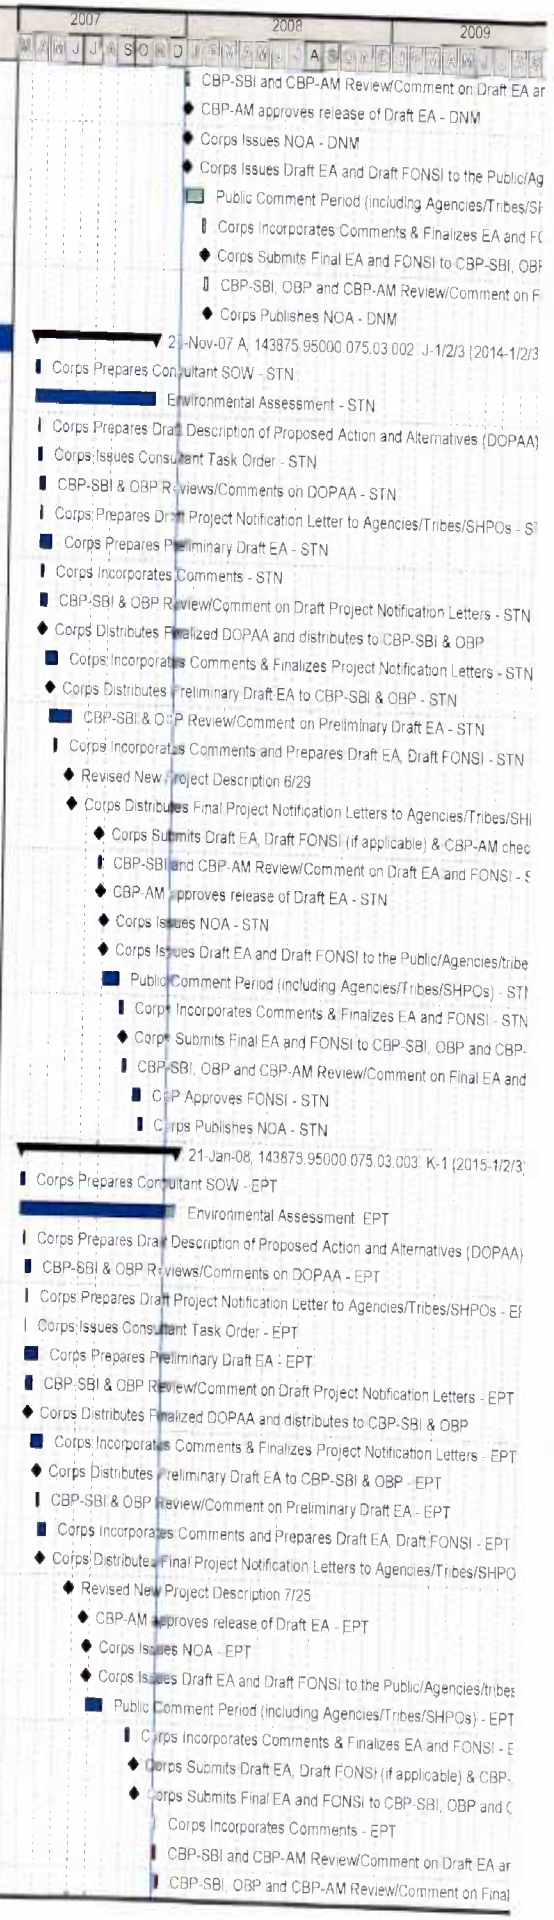

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV17265	Corps Revises EA and FONSI (if applicable) - EPT	ENV17260	5.0d	5.0d	0%		12-Jan-08		16-Jan-08
ENV17270	CBP Approves FONSI - EPT	ENV17265	0.0d	0.0d	0%				16-Jan-08
ENV17275	Corps Publishes NOA - EPT	ENV17270	0.0d	0.0d	0%				16-Jan-08
143875.95000.150 Environmental Phase 2			212.0d	92.0d		09-Aug-07	09-Aug-07 A		12-May-08
143875.95000.150.01 SDC			150.0d	92.0d		09-Aug-07	09-Aug-07 A		[illegible]
143875.95000.150.01.001 EA for Proposed TI Fencing - SDC			[illegible]	70.0d		28-Sep-07	28-Sep-07 A		10-Apr-08
ENV19344	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19346	CBP-SBI & OBP Initiate Draft DOPAA	ENV19344	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19348	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV19346	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV15000	Environmental Assessment Resource Estimate - SDC		141.0d	100.0d	0%	28-Sep-07	28-Sep-07 A		10-Apr-08
ENV19390	Corps Prepares Preliminary Draft EA	ENV19358	36.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	30-Nov-07	30-Nov-07 A
ENV19358	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV19360	Conduct Field Surveys (Biological and Cultural)	ENV19358	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV19350	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV19348	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19352	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV19348	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19354	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV19348	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19356	CBP-SBI Distributes Final Project Notification Letters to Agenc...	ENV19354	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV19368	Prepare Cultural Resource Survey Report	ENV19360	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV19370	CBP Review of Survey Report	ENV19368	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV19372	Cultural Resource Final Survey Report	ENV19370	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV19374	SHPO Review of Survey Report	ENV19372	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV19362	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV19392	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV19390	0.0d	0.0d	100%			30-Nov-07	30-Nov-07 A
ENV19394	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV19392	5.0d	5.0d	0%	30-Nov-07	30-Nov-07 A		08-Jan-08
ENV19396	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV19394	2.0d	2.0d	0%		09-Jan-08		10-Jan-08
ENV19398	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV19396	0.0d	0.0d	0%				10-Jan-08
ENV19400	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV19398	1.0d	1.0d	0%		11-Jan-08		11-Jan-08
ENV19402	Corps Finalizes Draft EA, Draft FONSI	ENV19400	1.0d	1.0d	0%		14-Jan-08		14-Jan-08
ENV19404	CBP-AM approves release of Draft EA	ENV19402	2.0d	2.0d	0%		15-Jan-08		16-Jan-08
ENV19376	SHPO Concurrence with Effect Determination	ENV19374	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV19408	Corps issues Draft EA and Draft FONSI to the Public/Agenci...	ENV19404	2.0d	2.0d	0%		17-Jan-08		18-Jan-08
ENV19406	Corps Issues NOA	ENV19404	3.0d	3.0d	0%		17-Jan-08		22-Jan-08
ENV19410	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV19408	31.0d	31.0d	0%		19-Jan-08		18-Feb-08
ENV19412	Corps Prepares Public Information Meeting Materials	ENV19410	4.0d	4.0d	0%		22-Jan-08		25-Jan-08
ENV19378	Corps Prepares Draft MOA (if required)	ENV19376	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV19380	CBP-AM, SBI Review of Draft MOA (if required)	ENV19378	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV19414	CBP-SBI Review and Approval of Meeting Materials	ENV19412	4.0d	4.0d	0%		28-Jan-08		31-Jan-08
ENV19382	Corps Revises MOA (if required)	ENV19380	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV19384	CBP Approval and Signature of MOA	ENV19382	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV19386	ACHP/SHPO review and approval of MOA or PA (if required)	ENV19384	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV19416	Public Information Meeting	ENV19414	5.0d	5.0d	0%		05-Feb-08		11-Feb-08
ENV19364	Final BO Issued by USFWS	ENV19362	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV19418	Corps Prepares Draft Final EA and Draft FONSI	ENV19410	12.0d	12.0d	0%		07-Feb-08		25-Feb-08
ENV19420	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV19418	0.0d	0.0d	0%				25-Feb-08
ENV19422	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV19420	3.0d	3.0d	0%		26-Feb-08		28-Feb-08
ENV19424	Corps Revises Draft Final EA and Draft FONSI	ENV19422	4.0d	4.0d	0%		29-Feb-08		05-Mar-08
ENV19388	MOA Executed (if applicable)	ENV19386	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV19426	CBP Approves FONSI	ENV19424	1.0d	1.0d	0%		06-Mar-08		06-Mar-08
ENV19428	Corps Publishes NOA	ENV19426	0.0d	0.0d	0%				14-Mar-08
ENV19366	USFWS Concurrence Letter on Recommendation	ENV19364	0.0d	0.0d	0%				27-Mar-08
143875.95000.150.01.002 EIS for Proposed TI Fencing - SDC A-1			190.0d	92.0d		09-Aug-07	09-Aug-07 A		12-May-08
ENV18712	Start EIS		0.0d	0.0d	100%	09-Aug-07	09-Aug-07 A		
ENV18714	CBP-SBI & OBP Initiate Draft DOPAA	ENV18712	14.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	28-Aug-07	28-Aug-07 A
ENV18716	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV18714	0.0d	0.0d	100%			28-Aug-07	28-Aug-07 A
ENV18718	Publication of the NOI		0.0d	0.0d	100%			24-Sep-07	24-Sep-07 A
ENV18720	Pre DEIS Public Comment Period	ENV18718	15.0d	0.0d	100%	24-Sep-07	24-Sep-07 A	15-Oct-07	15-Oct-07 A
ENV18722	Cooperating Agency Letters	ENV18718	5.0d	0.0d	100%	25-Sep-07	25-Sep-07 A	01-Oct-07	01-Oct-07 A
ENV18738	Final BA completed by USFWS		26.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	08-Nov-07	08-Nov-07 A
ENV18762	Corps Prepares Preliminary DEIS		55.0d	6.0d	100%	01-Oct-07	01-Oct-07 A		09-Jan-08
ENV18724	CBP-SBI Review and Approval of Cooperating Agency Letters	ENV18722	5.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	08-Oct-07	08-Oct-07 A
ENV18734	Receive Initial Available ROE		0.0d	0.0d	100%			10-Oct-07	10-Oct-07 A
ENV18736	Conduct Field Surveys (Biological and Cultural)		9.0d	0.0d	100%	11-Oct-07	11-Oct-07 A	23-Oct-07	23-Oct-07 A
ENV18726	Corps Prepares Draft Project Coordination Letter to Agencie...	ENV18720	3.0d	0.0d	100%	16-Oct-07	16-Oct-07 A	18-Oct-07	18-Oct-07 A

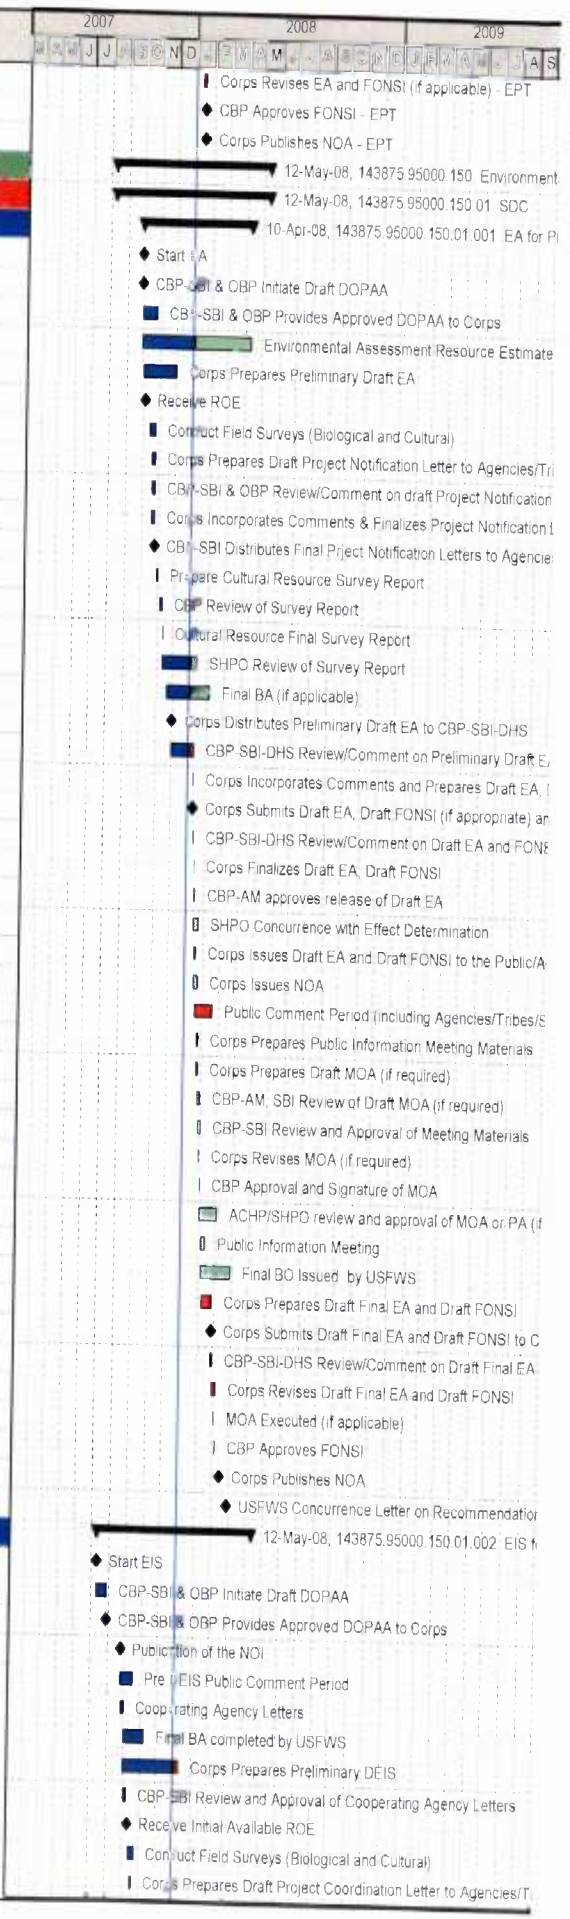

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV18728	CBP-SBI & OBP Review/Comment on Draft6 Project Coordin...	ENV18726	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18742	Corps Prepares Cultural Resource Survey Report	ENV18736	5.0d	0.0d	100%	24-Oct-07	24-Oct-07 A	30-Oct-07	30-Oct-07 A
ENV18730	Corps Incorporates Comments & Finalizes Project Coordinati...	ENV18728	3.0d	0.0d	100%	26-Oct-07	26-Oct-07 A	30-Oct-07	30-Oct-07 A
ENV18732	Corps Distrubutes Final Project Coordination Letters to Agen...	ENV18730	0.0d	0.0d	100%			30-Oct-07	30-Oct-07 A
ENV18744	CPB Review of Survey Report	ENV18742	5.0d	0.0d	100%	31-Oct-07	31-Oct-07 A	06-Nov-07	06-Nov-07 A
ENV18746	Corps Prepares Cultural Resource Final Survey Report	ENV18744	2.0d	0.0d	100%	07-Nov-07	07-Nov-07 A	08-Nov-07	08-Nov-07 A
ENV18748	SHPO Review of Survey Report	ENV18746	19.0d	5.0d	0%	08-Nov-07	08-Nov-07 A		08-Jan-08
ENV18784	Corps Prepares Draft NOAs, Public Notice (Newspaper), Tra...		1.0d	1.0d	0%		07-Jan-08*		07-Jan-08
ENV18786	CBP-SBI-DHS Review of NOA, Public Notice (Newspaper), T...	ENV18784	2.0d	2.0d	0%		07-Jan-08		08-Jan-08
ENV18750	SHPO Concurrence with Effect Determination	ENV18748	5.0d	5.0d	0%		09-Jan-08		15-Jan-08
ENV18764	Corps Distributes Preliminary DEIS, NOA and transmittal lett...	ENV18762	0.0d	0.0d	0%				09-Jan-08
ENV18766	CBP-SBI & OBP Review/Comment on Prelinimary DEIS, NO...	ENV18764	3.0d	3.0d	0%		10-Jan-08		14-Jan-08
ENV18768	Corps Incorporates Comments and Prepares DEIS, NOA an...	ENV18766	4.0d	4.0d	0%		10-Jan-08		15-Jan-08
ENV18752	Corps Prepares Draft MOA (if required)	ENV18750	3.0d	3.0d	0%		16-Jan-08		18-Jan-08
ENV18770	Corps Submits DEIS, NOA and Transmittal Letters for CBP s...	ENV18768	4.0d	4.0d	0%		16-Jan-08		22-Jan-08
ENV18788	Corps Finalizes NOA, Public Notice (Newspaper), Transmittals	ENV18786	2.0d	2.0d	0%		18-Jan-08		21-Jan-08
ENV18754	CBP-AM, SBI Review of Draft MOA (if required)	ENV18752	3.0d	3.0d	0%		22-Jan-08		24-Jan-08
ENV18772	CBP Obtains Go-No Go from EPA on DEIS and notifies ORR...	ENV18770	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV18776	ORR sends signed NOA for DEIS to FR (assumes "go" from...	ENV18772	0.0d	0.0d	0%				24-Jan-08
ENV18756	Corps Revises MOA (if required)	ENV18754	1.0d	1.0d	0%		25-Jan-08		25-Jan-08
ENV18774	Corps Distributes DEIS to Agencies, Tribes and Public	ENV18772	2.0d	2.0d	0%		25-Jan-08		28-Jan-08
ENV18758	ACHP/SHPO Review of MOA (if required)	ENV18756	19.0d	19.0d	0%		28-Jan-08		22-Feb-08
ENV18778	NOA Published in FR	ENV18776	0.0d	0.0d	0%		29-Jan-08		
ENV18780	45 day Public Comment Period	ENV18778	47.0d	47.0d	0%		29-Jan-08		15-Mar-08
ENV18782	Public Hearing(s)	ENV18780	5.0d	5.0d	0%		12-Feb-08		19-Feb-08
ENV18740	Final BO issued by USFWS	ENV18738	1.0d	1.0d	0%		25-Feb-08*		25-Feb-08
ENV18760	CBP Approval and Signature of MOA (if required)	ENV18758	3.0d	3.0d	0%		25-Feb-08		27-Feb-08
ENV18792	Corps Incorporates Public Comments into Draft FEIS	ENV18780	19.0d	19.0d	0%		27-Feb-08		24-Mar-08
ENV18794	CBP-SBI-DHS Review of Draft FEIS	ENV18792	3.0d	3.0d	0%		24-Mar-08		26-Mar-08
ENV18796	Corps Revises Draft FEIS	ENV18794	5.0d	5.0d	0%		27-Mar-08		02-Apr-08
ENV18800	CBP-SBI-DHS Signature Process for NOA for FEIS and Tran...	ENV18798	4.0d	4.0d	0%		02-Apr-08		07-Apr-08
ENV18798	CBP-SBI-DHS Check-Copy Final of FEIS, NOA, Public Notic...	ENV18796	0.0d	0.0d	0%				02-Apr-08
ENV18802	FEIS Signed	ENV18800	0.0d	0.0d	0%				07-Apr-08
ENV18804	ORR sends signed NOA for FEIS to FR (assumes "go" from...	ENV18802	1.0d	1.0d	0%		08-Apr-08		08-Apr-08
ENV18812	Corps submits Preliminary Draft ROD and NOA	ENV18806	0.0d	0.0d	0%		09-Apr-08		
ENV18806	Corps Distributes FEIS to Agencies, Tribes and Public	ENV18804	2.0d	2.0d	0%		09-Apr-08		10-Apr-08
ENV18814	CBP-SBI-DHS Review of Preliminary Draft Rod and NOA	ENV18812	3.0d	3.0d	0%		09-Apr-08		11-Apr-08
ENV18808	NOA published in FR	ENV18806	1.0d	1.0d	0%		11-Apr-08		11-Apr-08
ENV18816	Corps Revises Preliminary Draft Rod and NOA	ENV18814	3.0d	3.0d	0%		12-Apr-08		14-Apr-08
ENV18810	30 day Public Comment Period on FEIS	ENV18808	31.0d	31.0d	0%		12-Apr-08		12-May-08
ENV18818	CBP-SBI-DHS Reviews Draft ROD and NOA	ENV18816	4.0d	4.0d	0%		15-Apr-08		18-Apr-08
ENV18820	Corps Finalizes Draft ROD and NOA	ENV18818	3.0d	3.0d	0%		19-Apr-08		21-Apr-08
ENV18822	DHS Executive Secretary Review of Final ROD and NOA	ENV18820	4.0d	4.0d	0%		22-Apr-08		25-Apr-08
ENV18826	Publication in FR of ROD and NOA	ENV18824, ENV18760	0.0d	0.0d	0%				22-Apr-08*
ENV18824	Corps Finalizes ROD for Signature and NOA	ENV18822, ENV18740	10.0d	10.0d	0%		28-Apr-08		09-May-08
143875.95000.150.02 ELC			159.0d	60.0d		28-Sep-07	28-Sep-07 A		27-Mar-08
143875.95000.150.02.001 EA for Proposed TI Facility			159.0d	60.0d		28-Sep-07	28-Sep-07 A		27-Mar-08
ENV15497	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV15499	CBP-SBI & OBP Initiate Draft DOPAA	ENV15497	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV15501	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV15499	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV15543	Corps Prepares Preliminary Draft EA	ENV15511	36.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	21-Nov-07	21-Nov-07 A
ENV15511	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV15513	Conduct Field Surveys (Biological and Cultural)	ENV15511	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV15503	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV15501	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV15505	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV15501	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV15507	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV15501	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV15509	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV15507	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV15521	Prepare Cultural Resource Survey Report	ENV15513	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV15523	CBP Review of Survey Report	ENV15521	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV15525	Cultural Resource Final Survey Report	ENV15523	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV15527	SHPO Review of Survey Report	ENV15525	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV15545	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV15543	0.0d	0.0d	100%			21-Nov-07	21-Nov-07 A
ENV15515	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08

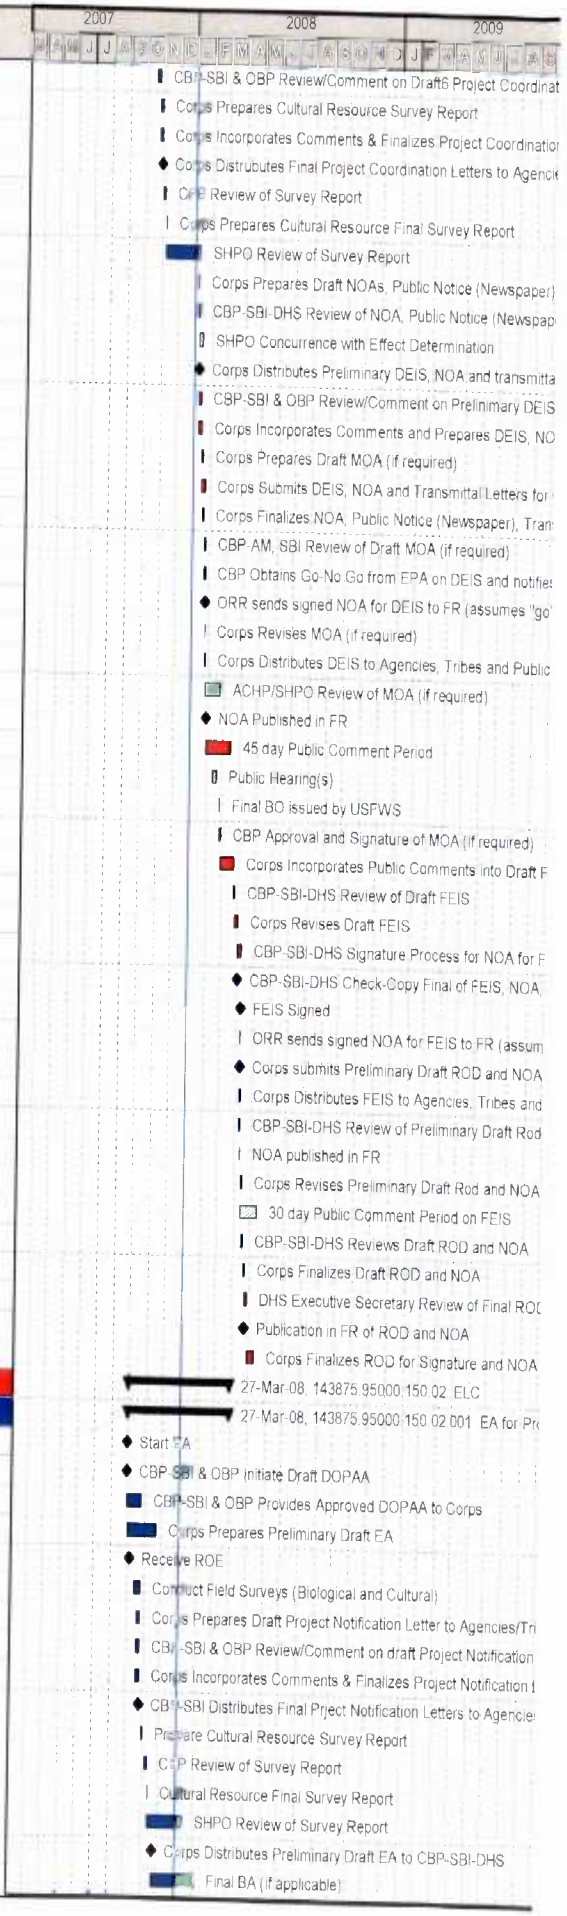

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV15547	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV15545	5.0d	0.0d	100%	23-Nov-07	23-Nov-07 A	28-Nov-07	28-Nov-07 A
ENV15549	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV15547	7.0d	5.0d	0%	29-Nov-07	29-Nov-07 A		08-Jan-08
ENV15495	Environmental Assessment Resource Estimate - ELC		169.0d	77.0d	0%	01-Dec-07	01-Dec-07 A		18-Mar-08
ENV15551	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV15549	2.0d	2.0d	0%		09-Jan-08		10-Jan-08
ENV15553	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV15551	1.0d	1.0d	0%		11-Jan-08		11-Jan-08
ENV15555	Corps Finalizes Draft EA, Draft FONSI	ENV15553	1.0d	1.0d	0%		14-Jan-08		14-Jan-08
ENV15557	CBP-AM approves release of Draft EA	ENV15555	2.0d	2.0d	0%		15-Jan-08		16-Jan-08
ENV15529	SHPO Concurrence with Effect Determination	ENV15527	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV15561	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV15557	2.0d	2.0d	0%		17-Jan-08		18-Jan-08
ENV15559	Corps Issues NOA	ENV15557	3.0d	3.0d	0%		17-Jan-08		22-Jan-08
ENV15563	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV15561	31.0d	31.0d	0%		19-Jan-08		18-Feb-08
ENV15565	Corps Prepares Public Information Meeting Materials	ENV15563	4.0d	4.0d	0%		22-Jan-08		25-Jan-08
ENV15531	Corps Prepares Draft MOA (if required)	ENV15529	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV15533	CBP-AM, SBI Review of Draft MOA (if required)	ENV15531	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV15567	CBP-SBI Review and Approval of Meeting Materials	ENV15565	4.0d	4.0d	0%		28-Jan-08		31-Jan-08
ENV15535	Corps Revises MOA (if required)	ENV15533	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV15537	CBP Approval and Signature of MOA	ENV15535	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV15539	ACHP/SHPO review and approval of MOA or PA (if required)	ENV15537	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV15569	Public Information Meeting	ENV15567	5.0d	5.0d	0%		05-Feb-08		11-Feb-08
ENV15517	Final BO Issued by USFWS	ENV15515	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV15571	Corps Prepares Draft Final EA and Draft FONSI	ENV15563	12.0d	12.0d	0%		07-Feb-08		25-Feb-08
ENV15573	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV15571	0.0d	0.0d	0%				25-Feb-08
ENV15575	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV15573	3.0d	3.0d	0%				28-Feb-08
ENV15577	Corps Revises Draft Final EA and Draft FONSI	ENV15575	4.0d	4.0d	0%		26-Feb-08		05-Mar-08
ENV15541	MOA Executed (if applicable)	ENV15539	1.0d	1.0d	0%		29-Feb-08		03-Mar-08
ENV15579	CBP Approves FONSI	ENV15577	1.0d	1.0d	0%		03-Mar-08		06-Mar-08
ENV15581	Corps Publishes NOA	ENV15579	0.0d	0.0d	0%		06-Mar-08		14-Mar-08
ENV15519	USFWS Concurrence Letter on Recommendation	ENV15517	0.0d	0.0d	0%				27-Mar-08
143875.95000.150.03 YUM			[illegible]	[illegible]		28-Sep-07	28-Sep-07 A		15-Apr-08
143875.95000.150.03.001 EA for [illegible] Fencing - YUM			[illegible]	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV18828	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV18830	CBP-SBI & OBP Initiate Draft DOPAA	ENV18828	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV15595	Environmental Assessment Resource Estimate - YUM		169.0d	105.0d	0%	28-Sep-07	28-Sep-07 A		15-Apr-08
ENV18832	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV18830	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV18874	Corps Prepares Preliminary Draft EA	ENV18842	66.0d	20.0d	100%	01-Oct-07	01-Oct-07 A		30-Jan-08
ENV18842	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV18844	Conduct Field Surveys (Biological and Cultural)	ENV18842	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV18834	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV18832	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18836	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV18832	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18838	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV18832	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18840	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV18838	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV18852	Prepare Cultural Resource Survey Report	ENV18844	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV18854	CBP Review of Survey Report	ENV18852	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV18856	Cultural Resource Final Survey Report	ENV18854	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV18858	SHPO Review of Survey Report	ENV18856	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV18846	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV18860	SHPO Concurrence with Effect Determination	ENV18858	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV18862	Corps Prepares Draft MOA (if required)	ENV18860	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV18864	CBP-AM, SBI Review of Draft MOA (if required)	ENV18862	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV18866	Corps Revises MOA (if required)	ENV18864	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV18876	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV18874	0.0d	0.0d	0%				30-Jan-08
ENV18868	CBP Approval and Signature of MOA	ENV18866	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV18878	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV18876	4.0d	4.0d	0%		31-Jan-08		05-Feb-08
ENV18870	ACHP/SHPO review and approval of MOA or PA (if required)	ENV18868	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV18848	Final BO Issued by USFWS	ENV18846	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV18880	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV18878	5.0d	5.0d	0%		06-Feb-08		12-Feb-08
ENV18882	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV18880	0.0d	0.0d	0%				12-Feb-08
ENV18884	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV18882	0.0d	0.0d	0%				12-Feb-08
ENV18886	Corps Finalizes Draft EA, Draft FONSI	ENV18884	0.0d	0.0d	0%				12-Feb-08
ENV18888	CBP-AM approves release of Draft EA	ENV18886	0.0d	0.0d	0%				12-Feb-08
ENV18892	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV18888	2.0d	2.0d	0%		13-Feb-08		14-Feb-08
ENV18890	Corps Issues NOA	ENV18888	3.0d	3.0d	0%		13-Feb-08		15-Feb-08
ENV18896	Corps Prepares Public Information Meeting Materials	ENV18894	4.0d	4.0d	0%		15-Feb-08		21-Feb-08

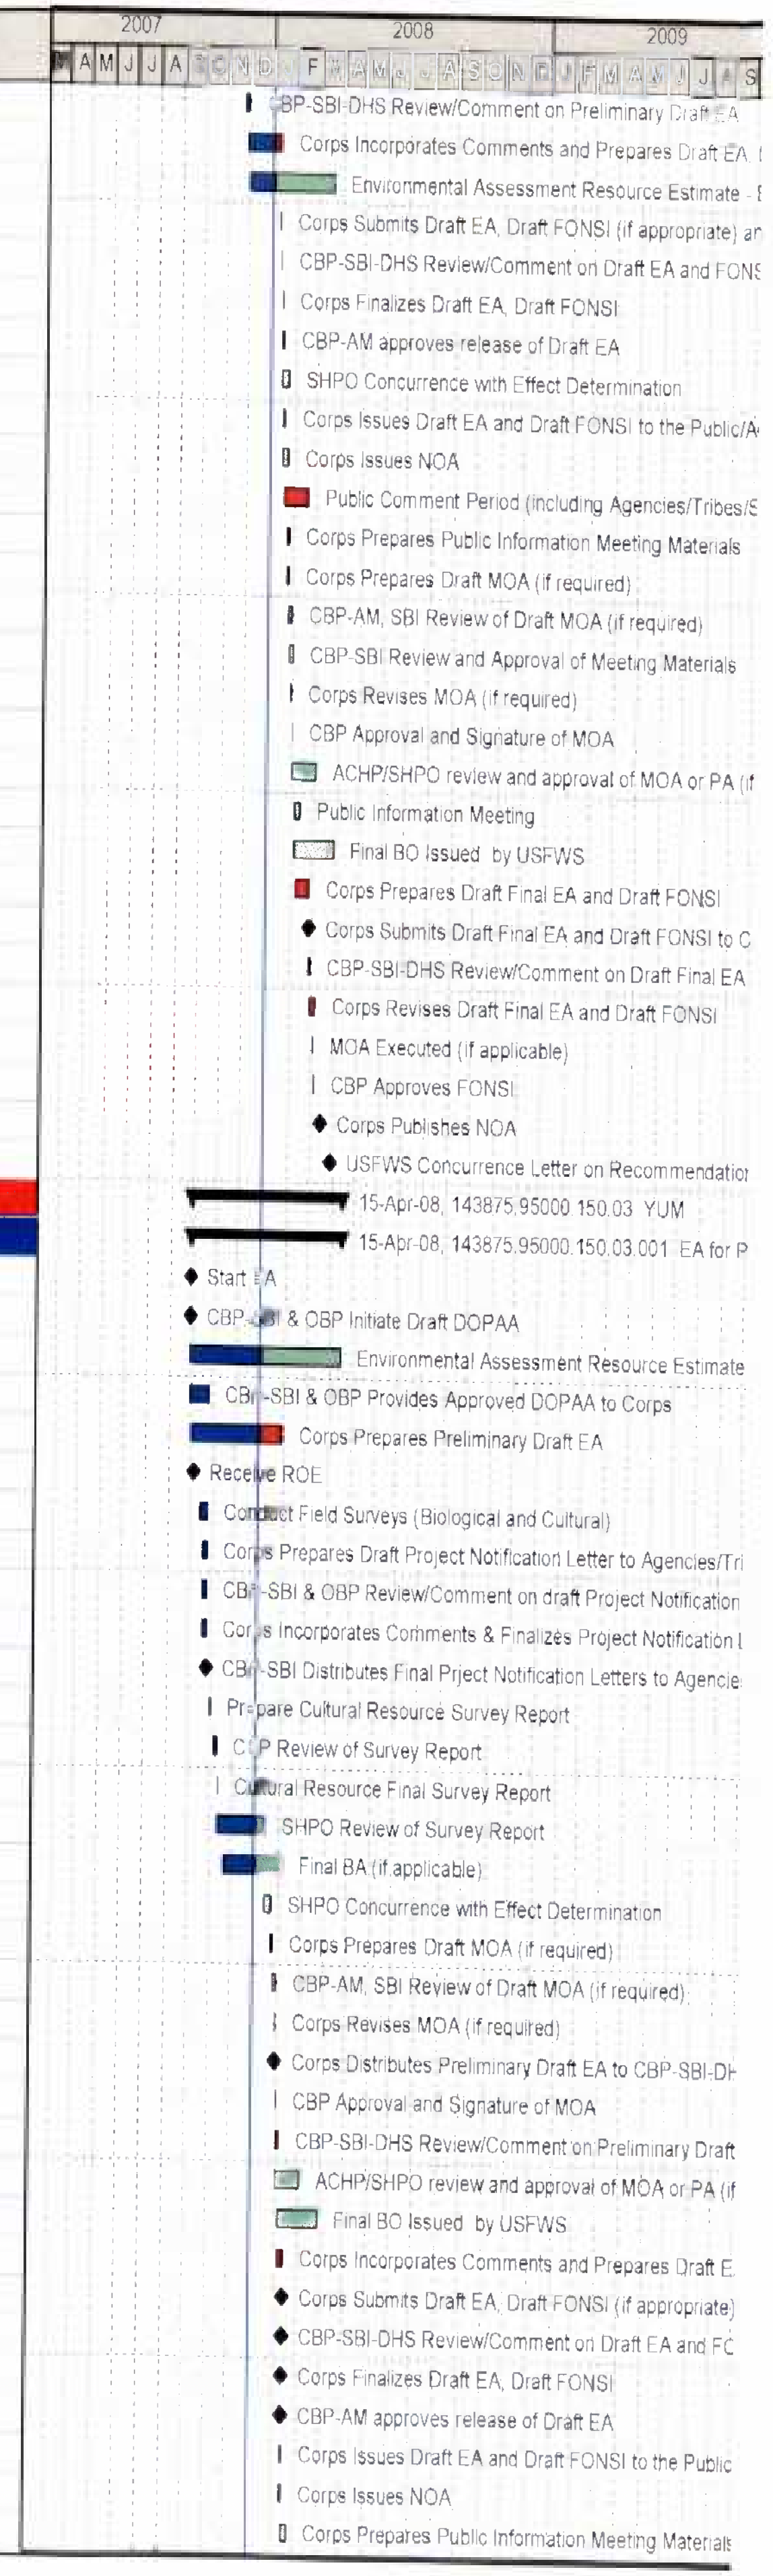

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV18894	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV18892	31.0d	31.0d	0%		15-Feb-08		16-Mar-08
ENV18898	CBP-SBI Review and Approval of Meeting Materials	ENV18896	5.0d	5.0d	0%		22-Feb-08		28-Feb-08
ENV18872	MOA Executed (if applicable)	ENV18870	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV18900	Public Information Meeting	ENV18898	5.0d	5.0d	0%		04-Mar-08		10-Mar-08
ENV18902	Corps Prepares Draft Final EA and Draft FONSI	ENV18894	12.0d	12.0d	0%		06-Mar-08		21-Mar-08
ENV18904	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV18902	0.0d	0.0d	0%				21-Mar-08
ENV18906	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft ...	ENV18904	4.0d	4.0d	0%		24-Mar-08		27-Mar-08
ENV18850	USFWS Concurrence Letter on Recommendation	ENV18848	0.0d	0.0d	0%				27-Mar-08
ENV18908	Corps Revises Draft Final EA and Draft FONSI	ENV18906	3.0d	3.0d	0%		28-Mar-08		01-Apr-08
ENV18910	CBP Approves FONSI	ENV18908	1.0d	1.0d	0%		02-Apr-08		02-Apr-08
ENV18912	Corps Publishes NOA	ENV18910	0.0d	0.0d	0%				10-Apr-08
143875.95000.150.04 TCA			33.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
143875.95000.150.04.001 EA for Proposed TI Fencing - TCA			133.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
ENV18914	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV18916	CBP-SBI & OBP Initiate Draft DOPAA	ENV18914	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV18918	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV18916	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV15695	Environmental Assessment Resource Estimate - TCA		169.0d	105.0d	0%	28-Sep-07	28-Sep-07 A		15-Apr-08
ENV18960	Corps Prepares Preliminary Draft EA	ENV18928	66.0d	20.0d	100%	01-Oct-07	01-Oct-07 A		30-Jan-08
ENV18928	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV18930	Conduct Field Surveys (Biological and Cultural)	ENV18928	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV18920	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV18918	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18922	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV18918	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18924	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV18918	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV18926	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV18924	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV18938	Prepare Cultural Resource Survey Report	ENV18930	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV18940	CBP Review of Survey Report	ENV18938	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV18942	Cultural Resource Final Survey Report	ENV18940	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV18944	SHPO Review of Survey Report	ENV18942	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV18932	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV18946	SHPO Concurrence with Effect Determination	ENV18944	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV18948	Corps Prepares Draft MOA (if required)	ENV18946	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV18950	CBP-AM, SBI Review of Draft MOA (if required)	ENV18948	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV18952	Corps Revises MOA (if required)	ENV18950	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV18962	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV18960	0.0d	0.0d	0%				30-Jan-08
ENV18954	CBP Approval and Signature of MOA	ENV18952	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV18964	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV18962	4.0d	4.0d	0%		31-Jan-08		05-Feb-08
ENV18956	ACHP/SHPO review and approval of MOA or PA (if required)	ENV18954	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV18934	Final BO Issued by USFWS	ENV18932	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV18966	Corps Incorporates Comments and Prepares Draft EA, Draft ...	ENV18964	5.0d	5.0d	0%		06-Feb-08		12-Feb-08
ENV18968	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV18966	0.0d	0.0d	0%				12-Feb-08
ENV18970	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV18968	0.0d	0.0d	0%				12-Feb-08
ENV18972	Corps Finalizes Draft EA, Draft FONSI	ENV18970	0.0d	0.0d	0%				12-Feb-08
ENV18974	CBP-AM approves release of Draft EA	ENV18972	0.0d	0.0d	0%				12-Feb-08
ENV18978	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV18974	2.0d	2.0d	0%		13-Feb-08		14-Feb-08
ENV18976	Corps Issues NOA	ENV18974	3.0d	3.0d	0%		13-Feb-08		15-Feb-08
ENV18982	Corps Prepares Public Information Meeting Materials	ENV18980	4.0d	4.0d	0%		15-Feb-08		21-Feb-08
ENV18980	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV18978	31.0d	31.0d	0%		15-Feb-08		16-Mar-08
ENV18984	CBP-SBI Review and Approval of Meeting Materials	ENV18982	5.0d	5.0d	0%		22-Feb-08		28-Feb-08
ENV18958	MOA Executed (if applicable)	ENV18956	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV18986	Public Information Meeting	ENV18984	5.0d	5.0d	0%		04-Mar-08		10-Mar-08
ENV18988	Corps Prepares Draft Final EA and Draft FONSI	ENV18980	12.0d	12.0d	0%		06-Mar-08		21-Mar-08
ENV18990	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV18988	0.0d	0.0d	0%				21-Mar-08
ENV18992	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft ...	ENV18990	3.0d	3.0d	0%		24-Mar-08		26-Mar-08
ENV18994	Corps Revises Draft Final EA and Draft FONSI	ENV18992	4.0d	4.0d	0%		27-Mar-08		01-Apr-08
ENV18936	USFWS Concurrence Letter on Recommendation	ENV18934	0.0d	0.0d	0%				27-Mar-08
ENV18996	CBP Approves FONSI	ENV18994	1.0d	1.0d	0%		02-Apr-08		02-Apr-08
ENV18998	Corps Publishes NOA	ENV18996	0.0d	0.0d	0%				10-Apr-08
143875.95000.150.05 EPT			159.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
143875.95000.150.05.001 EA for Proposed TI Fencing - EPT - NM			159.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19000	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19002	CBP-SBI & OBP Initiate Draft DOPAA	ENV19000	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV15795	Environmental Assessment Resource Estimate - EPT - NM		169.0d	105.0d	0%	28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19004	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV19002	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A

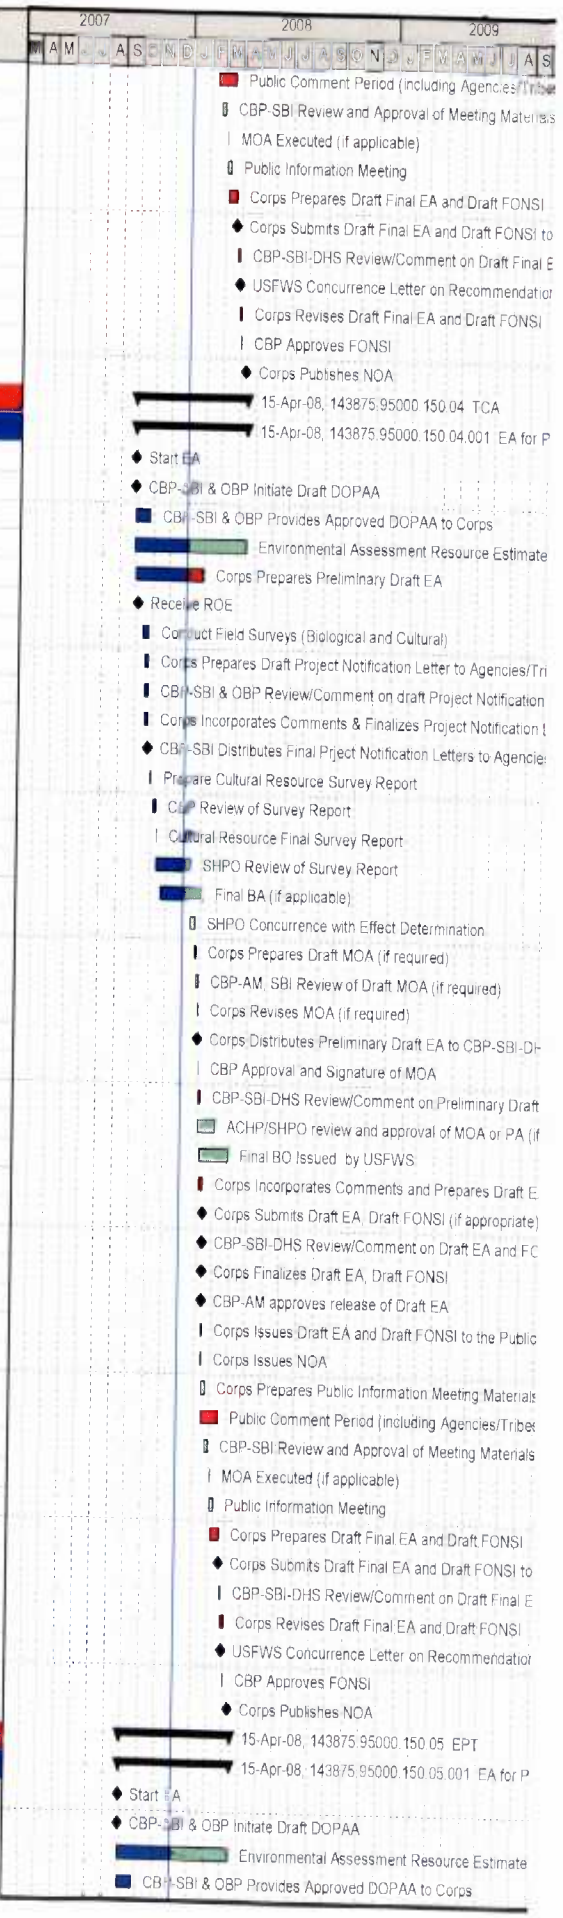

PF-225

PF225

04-Jan-08 11:(

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV19046	Corps Prepares Preliminary Draft EA	ENV19014	66.0d	20.0d	100%	01-Oct-07	01-Oct-07 A		30-Jan-08
ENV19014	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV19016	Conduct Field Surveys (Biological and Cultural)	ENV19014	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV19006	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV19004	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19008	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV19004	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19010	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV19004	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19012	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV19010	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV19024	Prepare Cultural Resource Survey Report	ENV19016	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV19026	CBP Review of Survey Report	ENV19024	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV19028	Cultural Resource Final Survey Report	ENV19026	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV19030	SHPO Review of Survey Report	ENV19028	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV19018	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV19032	SHPO Concurrence with Effect Determination	ENV19030	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV19034	Corps Prepares Draft MOA (if required)	ENV19032	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV19036	CBP-AM, SBI Review of Draft MOA (if required)	ENV19034	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV19038	Corps Revises MOA (if required)	ENV19036	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV19048	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV19046	0.0d	0.0d	0%				30-Jan-08
ENV19040	CBP Approval and Signature of MOA	ENV19038	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV19050	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV19048	4.0d	4.0d	0%		31-Jan-08		05-Feb-08
ENV19042	ACHP/SHPO review and approval of MOA or PA (if required)	ENV19040	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV19020	Final BO Issued by USFWS	ENV19018	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV19052	Corps Incorporates Comments and Prepares Draft EA, Draft	ENV19050	5.0d	5.0d	0%		06-Feb-08		12-Feb-08
ENV19054	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV19052	0.0d	0.0d	0%				12-Feb-08
ENV19056	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV19054	0.0d	0.0d	0%				12-Feb-08
ENV19058	Corps Finalizes Draft EA, Draft FONSI	ENV19056	0.0d	0.0d	0%				12-Feb-08
ENV19060	CBP-AM approves release of Draft EA	ENV19058	0.0d	0.0d	0%				12-Feb-08
ENV19064	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV19060	2.0d	2.0d	0%		13-Feb-08		14-Feb-08
ENV19062	Corps Issues NOA	ENV19060	3.0d	3.0d	0%		13-Feb-08		15-Feb-08
ENV19068	Corps Prepares Public Information Meeting Materials	ENV19066	4.0d	4.0d	0%		15-Feb-08		21-Feb-08
ENV19066	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV19064	31.0d	31.0d	0%		15-Feb-08		16-Mar-08
ENV19070	CBP-SBI Review and Approval of Meeting Materials	ENV19068	5.0d	5.0d	0%		22-Feb-08		28-Feb-08
ENV19044	MOA Executed (if applicable)	ENV19042	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV19072	Public Information Meeting	ENV19070	5.0d	5.0d	0%		04-Mar-08		10-Mar-08
ENV19074	Corps Prepares Draft Final EA and Draft FONSI	ENV19066	12.0d	12.0d	0%		06-Mar-08		21-Mar-08
ENV19076	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV19074	0.0d	0.0d	0%				21-Mar-08
ENV19078	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV19076	4.0d	4.0d	0%		24-Mar-08		27-Mar-08
ENV19022	USFWS Concurrence Letter on Recommendation	ENV19020	0.0d	0.0d	0%				27-Mar-08
ENV19080	Corps Revises Draft Final EA and Draft FONSI	ENV19078	3.0d	3.0d	0%		28-Mar-08		01-Apr-08
ENV19082	CBP Approves FONSI	ENV19080	1.0d	1.0d	0%		02-Apr-08		02-Apr-08
ENV19084	Corps Publishes NOA	ENV19082	0.0d	0.0d	0%				10-Apr-08
143875.95000.150.05.002 EA for Proposed TI Fencing - EPT - TX			159.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19086	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19088	CBP-SBI & OBP Initiate Draft DOPAA	ENV19086	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV15895	Environmental Assessment Resource Estimate - EPT - TX	ENV19086	169.0d	105.0d	0%	28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19090	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV19088	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV19132	Corps Prepares Preliminary Draft EA	ENV19100	66.0d	20.0d	100%	01-Oct-07	01-Oct-07 A		30-Jan-08
ENV19100	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV19102	Conduct Field Surveys (Biological and Cultural)	ENV19100	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV19092	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV19090	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19094	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV19090	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19096	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV19090	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19098	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV19096	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV19110	Prepare Cultural Resource Survey Report	ENV19102	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV19112	CBP Review of Survey Report	ENV19110	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV19114	Cultural Resource Final Survey Report	ENV19112	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV19116	SHPO Review of Survey Report	ENV19114	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV19104	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV19118	SHPO Concurrence with Effect Determination	ENV19116	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV19120	Corps Prepares Draft MOA (if required)	ENV19118	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV19122	CBP-AM, SBI Review of Draft MOA (if required)	ENV19120	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV19124	Corps Revises MOA (if required)	ENV19122	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV19134	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV19132	0.0d	0.0d	0%				30-Jan-08
ENV19126	CBP Approval and Signature of MOA	ENV19124	2.0d	2.0d	0%		31-Jan-08		01-Feb-08

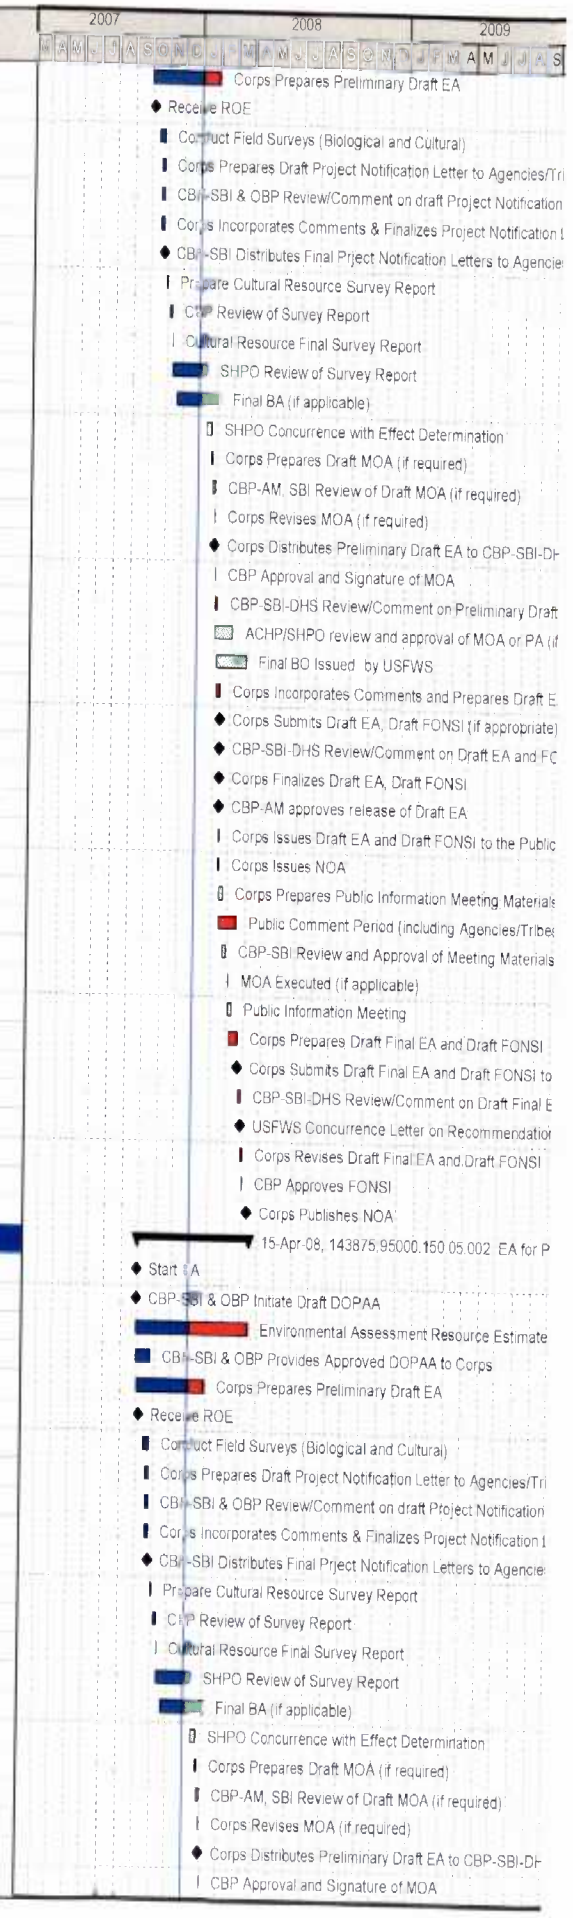

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV19136	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV19134	4.0d	4.0d	0%		31-Jan-08		05-Feb-08
ENV19128	ACHP/SHPO review and approval of MOA or PA (if required)	ENV19126	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV19106	Final BO Issued by USFWS	ENV19104	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV19138	Corps Incorporates Comments and Prepares Draft EA, Draft...	ENV19136	5.0d	5.0d	0%		06-Feb-08		12-Feb-08
ENV19140	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV19138	0.0d	0.0d	0%				12-Feb-08
ENV19142	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV19140	0.0d	0.0d	0%				12-Feb-08
ENV19144	Corps Finalizes Draft EA, Draft FONSI	ENV19142	0.0d	0.0d	0%				12-Feb-08
ENV19146	CBP-AM approves release of Draft EA	ENV19144	0.0d	0.0d	0%				12-Feb-08
ENV19150	Corps Issues Draft EA and Draft FONSI to the Public/Agenci	ENV19146	2.0d	2.0d	0%		13-Feb-08		14-Feb-08
ENV19148	Corps Issues NOA	ENV19146	3.0d	3.0d	0%		13-Feb-08		15-Feb-08
ENV19154	Corps Prepares Public Information Meeting Materials	ENV19152	4.0d	4.0d	0%		15-Feb-08		21-Feb-08
ENV19152	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV19150	31.0d	31.0d	0%		15-Feb-08		16-Mar-08
ENV19156	CBP-SBI Review and Approval of Meeting Materials	ENV19154	5.0d	5.0d	0%		22-Feb-08		28-Feb-08
ENV19130	MOA Executed (if applicable)	ENV19128	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV19158	Public Information Meeting	ENV19156	5.0d	5.0d	0%		04-Mar-08		10-Mar-08
ENV19160	Corps Prepares Draft Final EA and Draft FONSI	ENV19152	12.0d	12.0d	0%		06-Mar-08		21-Mar-08
ENV19162	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV19160	0.0d	0.0d	0%				21-Mar-08
ENV19164	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV19162	4.0d	4.0d	0%		24-Mar-08		27-Mar-08
ENV19108	USFWS Concurrence Letter on Recommendation	ENV19106	0.0d	0.0d	0%				27-Mar-08
ENV19166	Corps Revises Draft Final EA and Draft FONSI	ENV19164	3.0d	3.0d	0%		28-Mar-08		01-Apr-08
ENV19168	CBP Approves FONSI	ENV19166	1.0d	1.0d	0%		02-Apr-08		02-Apr-08
ENV19170	Corps Publishes NOA	ENV19168, ENV15895	0.0d	0.0d	0%				15-Apr-08
143875.95000.150.06 MAR			159.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
143875.95000.150.06.001 EA for Proposed TI Fencing - MAR			159.0d	73.0d		28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19172	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19174	CBP-SBI & OBP Initiate Draft DOPAA	ENV19172	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV16495	Environmental Assessment Resource Estimate - MAR		169.0d	105.0d	0%	28-Sep-07	28-Sep-07 A		15-Apr-08
ENV19176	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV19174	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV19218	Corps Prepares Preliminary Draft EA	ENV19186	36.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	30-Nov-07	30-Nov-07 A
ENV19186	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV19188	Conduct Field Surveys (Biological and Cultural)	ENV19186	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV19178	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV19176	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19180	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV19176	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19182	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV19176	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19184	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV19182	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV19196	Prepare Cultural Resource Survey Report	ENV19188	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV19198	CBP Review of Survey Report	ENV19196	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV19200	Cultural Resource Final Survey Report	ENV19198	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV19202	SHPO Review of Survey Report	ENV19200	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV19190	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV19220	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV19218	0.0d	0.0d	100%			30-Nov-07	30-Nov-07 A
ENV19222	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV19220	5.0d	5.0d	0%	30-Nov-07	30-Nov-07 A		08-Jan-08
ENV19224	Corps Incorporates Comments and Prepares Draft EA, Draft...	ENV19222	2.0d	2.0d	0%		09-Jan-08		10-Jan-08
ENV19226	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV19224	0.0d	0.0d	0%				10-Jan-08
ENV19228	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV19226	1.0d	1.0d	0%		11-Jan-08		11-Jan-08
ENV19230	Corps Finalizes Draft EA, Draft FONSI	ENV19228	1.0d	1.0d	0%		14-Jan-08		14-Jan-08
ENV19232	CBP-AM approves release of Draft EA	ENV19230	2.0d	2.0d	0%		15-Jan-08		16-Jan-08
ENV19204	SHPO Concurrence with Effect Determination	ENV19202	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV19236	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV19232	2.0d	2.0d	0%		17-Jan-08		18-Jan-08
ENV19234	Corps Issues NOA	ENV19232	3.0d	3.0d	0%		17-Jan-08		22-Jan-08
ENV19238	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV19236	31.0d	31.0d	0%		19-Jan-08		18-Feb-08
ENV19240	Corps Prepares Public Information Meeting Materials	ENV19238	4.0d	4.0d	0%		22-Jan-08		25-Jan-08
ENV19206	Corps Prepares Draft MOA (if required)	ENV19204	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV19208	CBP-AM, SBI Review of Draft MOA (if required)	ENV19206	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV19242	CBP-SBI Review and Approval of Meeting Materials	ENV19240	4.0d	4.0d	0%		28-Jan-08		31-Jan-08
ENV19210	Corps Revises MOA (if required)	ENV19208	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV19212	CBP Approval and Signature of MOA	ENV19210	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV19214	ACHP/SHPO review and approval of MOA or PA (if required)	ENV19212	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV19244	Public Information Meeting	ENV19242	5.0d	5.0d	0%		05-Feb-08		11-Feb-08
ENV19192	Final BO Issued by USFWS	ENV19190	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV19246	Corps Prepares Draft Final EA and Draft FONSI	ENV19238	12.0d	12.0d	0%		07-Feb-08		25-Feb-08
ENV19248	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV19246	0.0d	0.0d	0%				25-Feb-08
ENV19250	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV19248	3.0d	3.0d	0%		26-Feb-08		28-Feb-08

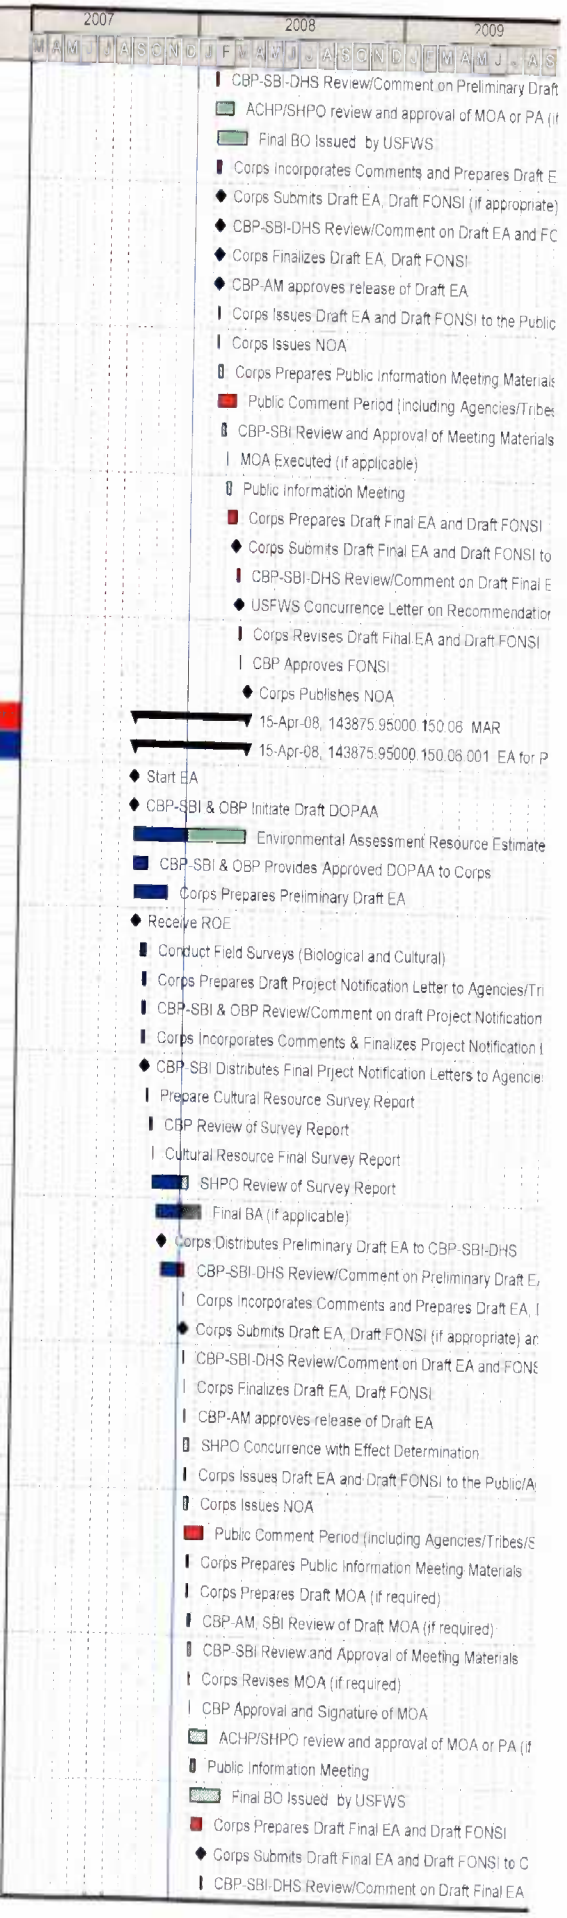

PF-225

PF225

04-Jan-08 11:0

Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV19252	Corps Revises Draft Final EA and Draft FONSI	ENV19250	4.0d	4.0d	0%		29-Feb-08		05-Mar-08
ENV19216	MOA Executed (if applicable)	ENV19214	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV19254	CBP Approves FONSI	ENV19252	1.0d	1.0d	0%		06-Mar-08		06-Mar-08
ENV19256	Corps Publishes NOA	ENV19254	0.0d	0.0d	0%				14-Mar-08
ENV19194	USFWS Concurrence Letter on Recommendation	ENV19192	0.0d	0.0d	0%				27-Mar-08
143875.95000.150.07 DRT			159.0d	61.0d		28-Sep-07	28-Sep-07 A		28-Mar-08
143875.95000.150.07.001 EA for Proposed TI Fencing - DRT			159.0d	61.0d		28-Sep-07	28-Sep-07 A		28-Mar-08
ENV19258	Start EA		0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV19260	CBP-SBI & OBP Initiate Draft DOPAA	ENV19258	0.0d	0.0d	100%	28-Sep-07	28-Sep-07 A		
ENV16295	Environmental Assessment Resource Estimate - DRT		169.0d	87.0d	0%	28-Sep-07	28-Sep-07 A		28-Mar-08
ENV19262	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV19260	19.0d	0.0d	100%	28-Sep-07	28-Sep-07 A	25-Oct-07	25-Oct-07 A
ENV19304	Corps Prepares Preliminary Draft EA	ENV19272	36.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	30-Nov-07	30-Nov-07 A
ENV19272	Receive ROE		0.0d	0.0d	100%	05-Oct-07	05-Oct-07 A		
ENV19274	Conduct Field Surveys (Biological and Cultural)	ENV19272	1.0d	0.0d	100%	15-Oct-07	15-Oct-07 A	26-Oct-07	26-Oct-07 A
ENV19264	Corps Prepares Draft Project Notification Letter to Agencies/...	ENV19262	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19266	CBP-SBI & OBP Review/Comment on draft Project Notificati...	ENV19262	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19268	Corps Incorporates Comments & Finalizes Project Notificatio...	ENV19262	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV19270	CBP-SBI Distributes Final Prject Notification Letters to Agenc...	ENV19268	0.0d	0.0d	100%			25-Oct-07	25-Oct-07 A
ENV19282	Prepare Cultural Resource Survey Report	ENV19274	5.0d	0.0d	100%	29-Oct-07	29-Oct-07 A	02-Nov-07	02-Nov-07 A
ENV19284	CBP Review of Survey Report	ENV19282	5.0d	0.0d	100%	05-Nov-07	05-Nov-07 A	09-Nov-07	09-Nov-07 A
ENV19286	Cultural Resource Final Survey Report	ENV19284	2.0d	0.0d	100%	12-Nov-07	12-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV19288	SHPO Review of Survey Report	ENV19286	30.0d	13.0d	0%	13-Nov-07	13-Nov-07 A		14-Jan-08
ENV19276	Final BA (if applicable)		30.0d	23.0d	0%	21-Nov-07	21-Nov-07 A		04-Feb-08
ENV19306	Corps Distributes Preliminary Draft EA to CBP-SBI-DHS	ENV19304	0.0d	0.0d	100%			30-Nov-07	30-Nov-07 A
ENV19308	CBP-SBI-DHS Review/Comment on Preliminary Draft EA	ENV19306	5.0d	5.0d	0%	30-Nov-07	30-Nov-07 A		08-Jan-08
ENV19310	Corps Incorporates Comments and Prepares Draft EA, Draft	ENV19308	2.0d	2.0d	0%		09-Jan-08		10-Jan-08
ENV19312	Corps Submits Draft EA, Draft FONSI (if appropriate) and CB...	ENV19310	0.0d	0.0d	0%				10-Jan-08
ENV19314	CBP-SBI-DHS Review/Comment on Draft EA and FONSI	ENV19312	1.0d	1.0d	0%		11-Jan-08		11-Jan-08
ENV19316	Corps Finalizes Draft EA, Draft FONSI	ENV19314	1.0d	1.0d	0%		14-Jan-08		14-Jan-08
ENV19318	CBP-AM approves release of Draft EA	ENV19316	2.0d	2.0d	0%		15-Jan-08		16-Jan-08
ENV19290	SHPO Concurrence with Effect Determination	ENV19288	5.0d	5.0d	0%		15-Jan-08		22-Jan-08
ENV19322	Corps Issues Draft EA and Draft FONSI to the Public/Agenci...	ENV19318	2.0d	2.0d	0%		17-Jan-08		18-Jan-08
ENV19320	Corps Issues NOA	ENV19318	3.0d	3.0d	0%		17-Jan-08		22-Jan-08
ENV19324	Public Comment Period (including Agencies/Tribes/SHPO's)	ENV19322	31.0d	31.0d	0%		19-Jan-08		18-Feb-08
ENV19326	Corps Prepares Public Information Meeting Materials	ENV19324	4.0d	4.0d	0%		22-Jan-08		25-Jan-08
ENV19292	Corps Prepares Draft MOA (if required)	ENV19290	2.0d	2.0d	0%		23-Jan-08		24-Jan-08
ENV19294	CBP-AM, SBI Review of Draft MOA (if required)	ENV19292	3.0d	3.0d	0%		25-Jan-08		29-Jan-08
ENV19328	CBP-SBI Review and Approval of Meeting Materials	ENV19326	4.0d	4.0d	0%		28-Jan-08		31-Jan-08
ENV19296	Corps Revises MOA (if required)	ENV19294	1.0d	1.0d	0%		30-Jan-08		30-Jan-08
ENV19298	CBP Approval and Signature of MOA	ENV19296	2.0d	2.0d	0%		31-Jan-08		01-Feb-08
ENV19300	ACHP/SHPO review and approval of MOA or PA (if required)	ENV19298	30.0d	30.0d	0%		02-Feb-08		02-Mar-08
ENV19330	Public Information Meeting	ENV19328	5.0d	5.0d	0%		05-Feb-08		11-Feb-08
ENV19278	Final BO Issued by USFWS	ENV19276	37.0d	37.0d	0%		05-Feb-08		27-Mar-08
ENV19332	Corps Prepares Draft Final EA and Draft FONSI	ENV19324	12.0d	12.0d	0%		07-Feb-08		25-Feb-08
ENV19334	Corps Submits Draft Final EA and Draft FONSI to CBP-SBI-...	ENV19332	0.0d	0.0d	0%				25-Feb-08
ENV19336	CBP-SBI-DHS Review/Comment on Draft Final EA and Draft...	ENV19334	3.0d	3.0d	0%		26-Feb-08		28-Feb-08
ENV19338	Corps Revises Draft Final EA and Draft FONSI	ENV19336	4.0d	4.0d	0%		29-Feb-08		05-Mar-08
ENV19302	MOA Executed (if applicable)	ENV19300	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV19340	CBP Approves FONSI	ENV19338	1.0d	1.0d	0%		06-Mar-08		06-Mar-08
ENV19342	Corps Publishes NOA	ENV19340	0.0d	0.0d	0%				14-Mar-08
ENV19280	USFWS Concurrence Letter on Recommendation	ENV19278	0.0d	0.0d	0%				27-Mar-08
143875.95000.150.08 RGV			212.0d	6[illegible]		09-Aug-07	09-Aug-07 A		08-Apr-08
143875.95000.150.08.001 EIS for Proposed Fencing - RGV			212.0d	68.0d		09-Aug-07	09-Aug-07 A		08-Apr-08
ENV16097	Start EIS		0.0d	0.0d	100%	09-Aug-07	09-Aug-07 A		
ENV16095	Environmental Assessment Resource Estimate - RGV		195.0d	98.0d	0%	09-Aug-07	09-Aug-07 A		08-Apr-08
ENV16099	CBP-SBI & OBP Initiate Draft DOPAA	ENV16097	14.0d	0.0d	100%	09-Aug-07	09-Aug-07 A	28-Aug-07	28-Aug-07 A
ENV16103	Publication of the NOI		19.0d	0.0d	100%	28-Aug-07	28-Aug-07 A	24-Sep-07	24-Sep-07 A
ENV16101	CBP-SBI & OBP Provides Approved DOPAA to Corps	ENV16099	0.0d	0.0d	100%			28-Aug-07	28-Aug-07 A
ENV16105	Pre DEIS Public Comment Period	ENV16103	15.0d	0.0d	100%	24-Sep-07	24-Sep-07 A	15-Oct-07	15-Oct-07 A
ENV16107	Cooperating Agency Letters	ENV16103	5.0d	0.0d	100%	25-Sep-07	25-Sep-07 A	01-Oct-07	01-Oct-07 A
ENV16145	Corps Prepares Preliminary DEIS		19.0d	0.0d	100%	26-Sep-07	26-Sep-07 A	16-Oct-07	16-Oct-07 A
ENV16121	Final BA completed by USFWS		28.0d	0.0d	100%	01-Oct-07	01-Oct-07 A	08-Nov-07	08-Nov-07 A
ENV16109	CBP-SBI Review and Approval of Cooperating Agency Letters	ENV16107	5.0d	0.0d	100%	02-Oct-07	02-Oct-07 A	08-Oct-07	08-Oct-07 A

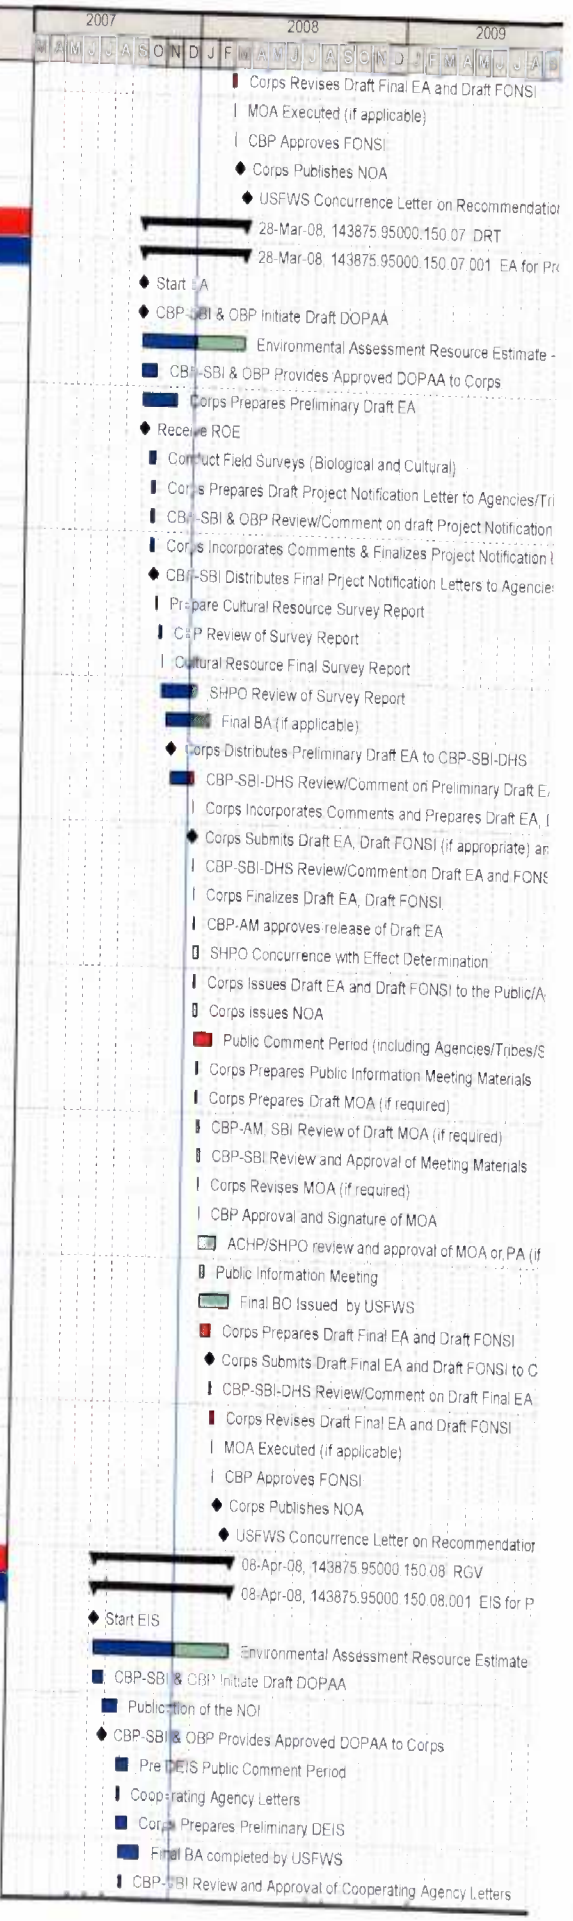

PF-225

PF225

04-Jan-08 11:0
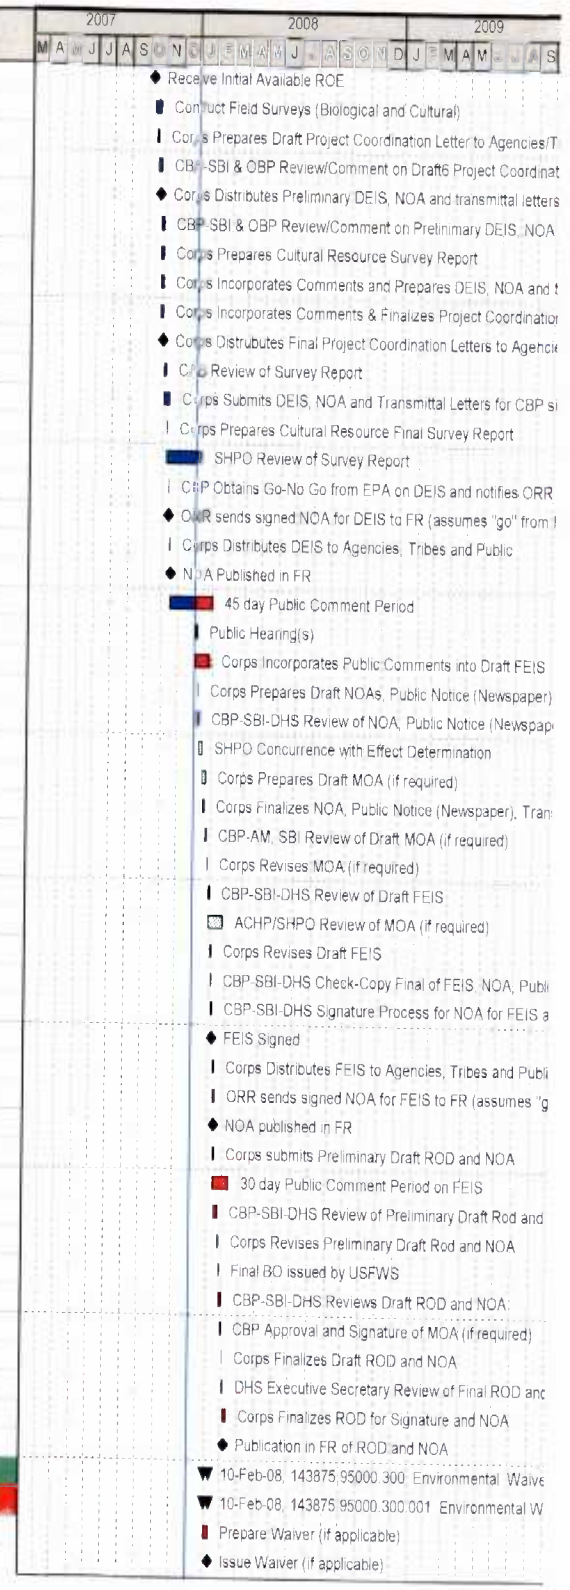
Activity ID	Activity Name	Predecessors	Original Duration	Remaining Duration	Physical % Complete	Actual Start	Start	Actual Finish	Finish
ENV16118	Receive Initial Available ROE		0.0d	0.0d	100%			10-Oct-07	10-Oct-07 A
ENV16119	Conduct Field Surveys (Biological and Cultural)		9.0d	0.0d	100%	11-Oct-07	11-Oct-07 A	23-Oct-07	23-Oct-07 A
ENV16111	Corps Prepares Draft Project Coordination Letter to Agencie...	ENV16105	3.0d	0.0d	100%	16-Oct-07	16-Oct-07 A	18-Oct-07	18-Oct-07 A
ENV16113	CBP-SBI & OBP Review/Comment on Draft6 Project Coordin...	ENV16111	5.0d	0.0d	100%	19-Oct-07	19-Oct-07 A	25-Oct-07	25-Oct-07 A
ENV16147	Corps Distributes Preliminary DEIS, NOA and transmittal lett...	ENV16145	0.0d	0.0d	100%			23-Oct-07	23-Oct-07 A
ENV16149	CBP-SBI & OBP Review/Comment on Prelinimary DEIS, NO...	ENV16147	4.0d	0.0d	100%	24-Oct-07	24-Oct-07 A	29-Oct-07	29-Oct-07 A
ENV16125	Corps Prepares Cultural Resource Survey Report	ENV16119	5.0d	0.0d	100%	24-Oct-07	24-Oct-07 A	30-Oct-07	30-Oct-07 A
ENV16151	Corps Incorporates Comments and Prepares DEIS, NOA an...	ENV16149	5.0d	0.0d	100%	24-Oct-07	24-Oct-07 A	30-Oct-07	30-Oct-07 A
ENV16115	Corps Incorporates Comments & Finalizes Project Coordinati...	ENV16113	3.0d	0.0d	100%	26-Oct-07	26-Oct-07 A	30-Oct-07	30-Oct-07 A
ENV16117	Corps Distrubutes Final Project Coordination Letters to Agen...	ENV16115	0.0d	0.0d	100%			30-Oct-07	30-Oct-07 A
ENV16127	CPB Review of Survey Report	ENV16125	5.0d	0.0d	100%	31-Oct-07	31-Oct-07 A	06-Nov-07	06-Nov-07 A
ENV16153	Corps Submits DEIS, NOA and Transmittal Letters for CBP s...	ENV16151	8.0d	0.0d	100%	31-Oct-07	31-Oct-07 A	13-Nov-07	13-Nov-07 A
ENV16129	Corps Prepares Cultural Resource Final Survey Report	ENV16127	2.0d	0.0d	100%	07-Nov-07	07-Nov-07 A	08-Nov-07	08-Nov-07 A
ENV16131	SHPO Review of Survey Report	ENV16129	30.0d	8.0d	0%	08-Nov-07	08-Nov-07 A		09-Jan-08
ENV16155	CBP Obtains Go-No Go from EPA on DEIS and notifies ORR...	ENV16153	1.0d	0.0d	100%	13-Nov-07	13-Nov-07 A	13-Nov-07	13-Nov-07 A
ENV16159	ORR sends signed NOA for DEIS to FR (assumes "go" from ...	ENV16153	0.0d	0.0d	100%			13-Nov-07	13-Nov-07 A
ENV16157	Corps Distributes DEIS to Agencies, Tribes and Public	ENV16155	2.0d	0.0d	100%	14-Nov-07	14-Nov-07 A	15-Nov-07	15-Nov-07 A
ENV16161	NOA Published in FR	ENV16159	0.0d	0.0d	100%			16-Nov-07	16-Nov-07 A
ENV16163	45 day Public Comment Period	ENV16161	45.0d	31.0d	0%	16-Nov-07	16-Nov-07 A		01-Feb-08
ENV16165	Public Hearing(s)	ENV16163	3.0d	3.0d	0%		02-Jan-08		04-Jan-08
ENV16175	Corps Incorporates Public Comments into Draft FEIS	ENV16163	18.0d	18.0d	0%		02-Jan-08		28-Jan-08
ENV16167	Corps Prepares Draft NOAs, Public Notice (Newspaper), Tra...		1.0d	1.0d	0%		07-Jan-08*		07-Jan-08
ENV16169	CBP-SBI-DHS Review of NOA, Public Notice (Newspaper), T...	ENV16167	2.0d	2.0d	0%		07-Jan-08		08-Jan-08
ENV16133	SHPO Concurrence with Effect Determination	ENV16131	5.0d	5.0d	0%		10-Jan-08		16-Jan-08
ENV16135	Corps Prepares Draft MOA (if required)	ENV16133	3.0d	3.0d	0%		17-Jan-08		22-Jan-08
ENV16173	Corps Finalizes NOA, Public Notice (Newspaper), Transmittals	ENV16169	2.0d	2.0d	0%		18-Jan-08		21-Jan-08
ENV16137	CBP-AM, SBI Review of Draft MOA (if required)	ENV16135	3.0d	3.0d	0%		23-Jan-08		25-Jan-08
ENV16139	Corps Revises MOA (if required)	ENV16137	1.0d	1.0d	0%		28-Jan-08		28-Jan-08
ENV16177	CBP-SBI-DHS Review of Draft FEIS	ENV16175	4.0d	4.0d	0%		29-Jan-08		01-Feb-08
ENV16141	ACHP/SHPO Review of MOA (if required)	ENV16139	29.0d	29.0d	0%		29-Jan-08		26-Feb-08
ENV16179	Corps Revises Draft FEIS	ENV16177	2.0d	2.0d	0%		04-Feb-08		05-Feb-08
ENV16181	CBP-SBI-DHS Check-Copy Final of FEIS, NOA, Public Notic...	ENV16179	1.0d	1.0d	0%		06-Feb-08		06-Feb-08
ENV16183	CBP-SBI-DHS Signature Process for NOA for FEIS and Tran...	ENV16181	3.0d	3.0d	0%		06-Feb-08		08-Feb-08
ENV16185	FEIS Signed	ENV16183	0.0d	0.0d	0%				08-Feb-08
ENV16189	Corps Distributes FEIS to Agencies, Tribes and Public	ENV16187	2.0d	2.0d	0%		11-Feb-08		12-Feb-08
ENV16187	ORR sends signed NOA for FEIS to FR (assumes "go" from ...	ENV16185	3.0d	3.0d	0%		11-Feb-08		13-Feb-08
ENV16191	NOA published in FR	ENV16189	0.0d	0.0d	0%		13-Feb-08*		
ENV16195	Corps submits Preliminary Draft ROD and NOA	ENV16193	2.0d	2.0d	0%		13-Feb-08		14-Feb-08
ENV16193	30 day Public Comment Period on FEIS	ENV16191	21.0d	21.0d	0%		13-Feb-08		13-Mar-08
ENV16197	CBP-SBI-DHS Review of Preliminary Draft Rod and NOA	ENV16195	6.0d	6.0d	0%		15-Feb-08		20-Feb-08
ENV16199	Corps Revises Preliminary Draft Rod and NOA	ENV16197	2.0d	2.0d	0%		21-Feb-08		22-Feb-08
ENV16123	Final BO issued by USFWS	ENV16121	1.0d	1.0d	0%		25-Feb-08		25-Feb-08*
ENV16201	CBP-SBI-DHS Reviews Draft ROD and NOA	ENV16199	5.0d	5.0d	0%		25-Feb-08		29-Feb-08
ENV16143	CBP Approval and Signature of MOA (if required)	ENV16141	3.0d	3.0d	0%		27-Feb-08		29-Feb-08
ENV16203	Corps Finalizes Draft ROD and NOA	ENV16201	1.0d	1.0d	0%		03-Mar-08		03-Mar-08
ENV16205	DHS Executive Secretary Review of Final ROD and NOA	ENV16203	2.0d	2.0d	0%		04-Mar-08		05-Mar-08
ENV16207	Corps Finalizes ROD for Signature and NOA	ENV16205, ENV16123	6.0d	6.0d	0%		06-Mar-08		13-Mar-08
ENV16209	Publication in FR of ROD and NOA	ENV16207, ENV16143	0.0d	0.0d	0%				07-Mar-08*
143875.95000.300	Environmental Waiver		6.0d	6.0d			01-Feb-08		10-Feb-08
143875.95000.300.001	Environmental Waiver - Phase 2		6.0d	6.0d			01-Feb-08		10-Feb-08
ENV16080	Prepare Waiver (if applicable)		10.0d	10.0d	0%		01-Feb-08*		10-Feb-08
ENV16075	Issue Waiver (if applicable)	ENV16080	0.0d	0.0d	0%				10-Feb-08
